

Panther Grove 2

	21-Aug-26	Today
Daily Weather as of 7:00am	0	0
Low Temperature (F)	63	63
High Temperature (F)	82	81
Ground Wind Speed (MPH):	8 MPH	12 MPH
Precipitation (in)	0.00	24%
August Precip Total (in)	4.50	

	ACTIVITY
Laydown Yard	Install Laydown Yard
Public Roads	Strip Public Road Radii
	Mowing
Access Roads	Stone Public Road Radii
	Strip Access Road
	Cement Stabilization
	Stone Access Road
	Strip Access Road Radii
Foundations	Stone Access Road Radii
	Strip Sites
	Geo-Piers
	Excavate Foundations
	Mud Mat
	Rebar Delivery
	Rebar Bottom Mat
	Anchor Bolt Build
	Anchor Bolt Set
	Internal Grounding
	Rebar Top Mat
	Base Conduit
	Pour Base
	Rebar Pedestal
	Form Pedestal
	Pour Pedestal
	Backfill Foundation
	Crane Pad Subgrade
	Crane Pad Stabilization
	Crane Pad Stone
	Set Load Spreader Plate
Set Grout Forms	
Pour Grout	

[illegible]

Daily Safety Topics

Tag Lines: Tag lines help reduce the risk and prevent injuries to yourself and co-workers. Helps keep your hands out of the line of fire and control components as they are being lifted in the air especially during windy days.

Heavy Equipment Right Of Way: We need to make sure we are giving heavy equipment and larger vehicles the right of way. When heavy equipment operators are working near or on the road, do not attempt to go around until they have stopped work and give you the signal to pass on through.

Site Notes

Saturday, August 22, 2026

[illegible][illegible]

WHITE
CONSTRUCTION

✦ a MasTec company

Quantity Tracking				
QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
	25	ACRE	25.0	100.0%
	6	EA	35	17.1%
	4	EA	35	11.4%
	34013.5	LF	161120	21.1%
	29489	LF	161120	18.3%
	18450.5	LF	161120	11.5%
	28	EA	140	20.0%
	23	EA	140	16.4%
	19	EA	105	18.1%
	0	EA	14	0.0%
2	4	EA	105	3.8%
	4	EA	105	3.8%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	0	EA	105	0.0%
	0	EA	105	0.0%
	0	EA	105	0.0%

Site Information

Manpower

4	White Construction Management
15	White Construction Operators
13	White Construction Laborers
	White Construction Ironworkers
	White Construction Millwright
	White Construction Electrician
	Dunn Company
	West Wind
	Tobey Construction & Cartage
	KVCC
6	Prairie Materials

Total

Equipment

7	Pickup Trucks
2	Dozers
2	Skid Steers
2	Rollers
2	Graders
3	Cargo Trailers
2	Reclaimer Stabilizer
1	Excavators
2	Smooth Drum Roller
3	Trailers
3	Water Trucks
2	Sheepfoot roller

Total

Qty Executed


Completion Certificates

0/20	WTG Civil Works Completion
0/105	WTG Foundation Completion
0/105	WTG Mechanical Completion
0/20	Collection Circuit Mechanical Completion
0/1	Substation Mechanical Completion
0/1	Electrical Substantial Completion
0/1	O&M Building Substantial Completion
0/1	Final Completion

Additional Comments

--

Notes from Previous Day		Weather Forecast			Notes for Today		Weather Forecast			Weather Forecast			Weather Forecast			Weather Forecast			Weather Forecast			Weather Forecast						
QTY	Manpower	81° / 58° Temp Range			QTY	Manpower	80° / 65° Temp Range			74° / 55° Temp Range			76° / 57° Temp Range			76° / 41° Temp Range			82° / 44° Temp Range			75° / 44° Temp Range						
22	Dunn Company	22% None 0.00 in Precipitation			22	Dunn Company	34% 12 AM-2 AM 0.00 in Precipitation			0% None 0.00 in Precipitation			2% None 0.00 in Precipitation			6% None 0.00 in Precipitation			13% None 0.24 in Precipitation			9% None 0.13 in Precipitation						
4	Tobey's Constr.	None Lighting Risk			4	Tobey's Constr.	None Lighting Risk			None Lighting Risk			None Lighting Risk			None Lighting Risk			None Lighting Risk			None Lighting Risk						
8	KVCC	Moderate None Severe Forecast			8	KVCC	Moderate None Severe Forecast			None None Severe Forecast			None None Severe Forecast			None None Severe Forecast			High None Severe Forecast			Moderate None Severe Forecast						
4	Millennia	10 mph Max Wind			4	Millennia	13 mph Max Wind			10 mph Max Wind			6 mph Max Wind			9 mph Max Wind			8 mph Max Wind			8 mph Max Wind						
0	Material Serv. Test.	21 mph Max Gust			0	Material Serv. Test.	23 mph Max Gust			13 mph Max Gust			6 mph Max Gust			18 mph Max Gust			18 mph Max Gust			10 mph Max Gust						
0	Beniach	Follow-Up Items			7	Beniach	Notes			Notes			Notes			Notes			Notes			Notes						
5	Dirtworks	1) Need detour plan for upcoming structure 113			5	Dirtworks	1) 148, 34 Delivery?			1) 148, 34 Delivery?			1) 148, 34 Delivery?			1) 148, 34 Delivery?			1) 148, 34 Delivery?			1) Culvert sequence?						
1	HLR	3) 165, 222, 152 delivery 8.20			1	HLR	2) 700E Layout			2) 700E Layout			2) Detour being posted			2) Detour in effect			2) Detour in effect			2) Detour in effect						
1	LPM Mgmt Services				1	LPM Mgmt Services							3) 222/223 Prof. Adj			3) 222/223 Prof. Adj												
(S) Start, (C) Continue, (F) Finish. Black text is planned. Grey text is alternate					Plan of the Day Report																							
		LAST WORKING DAY					TODAY			NEXT WORKING DAY			2-Day Lookahead Planning			3-Day Lookahead Planning			4-Day Lookahead Planning			5-Day Lookahead Planning						
		Friday, August 21, 2026					Saturday, August 22, 2026			Sunday, August 23, 2026			Monday, August 24, 2026			Tuesday, August 25, 2026			Wednesday, August 26, 2026			Thursday, August 27, 2026						
		LOCATION(S)					LOCATION(S)			LOCATION(S)			LOCATION(S)			LOCATION(S)			LOCATION(S)			LOCATION(S)						
Long Duration Road Closures		New Road	Repaving	Notes for Today			New Road	Repaving	Notes for Today			New Road	Repaving	Notes for Today			New Road	Repaving	Notes for Today			New Road	Repaving	Notes for Today				
		☐ 200E:1800N-1900N	8/24/2026	QTY Last Working Day QTY Completed Unit Total QTY % Complete			☐ 1600N:CH16-400E	8/24/2026	QTY Last Working Day QTY Completed Unit Total QTY % Complete			☐ 1600N:CH16-400E	8/24/2026	QTY Last Working Day QTY Completed Unit Total QTY % Complete			☐ 1300N:150E-100E	8/21/2026	QTY Last Working Day QTY Completed Unit Total QTY % Complete			☐ 1300N:150E-100E	8/21/2026	QTY Last Working Day QTY Completed Unit Total QTY % Complete				
		☐ 1800N:100E-200E	8/24/2026				☐ 1300N:200E-150E	9/9/2026				☐ 1300N:200E-150E	9/9/2026				☐ 1300N:200E-150E	9/9/2026				☐ 1300N:200E-150E	9/9/2026					
		☐ 1800N:200E-300	8/24/2026				☒ 1300N:200E-CH16	9/9/2026				☐ 1300N:200E-CH16	9/9/2026				☐ 1300N:200E-CH16	9/9/2026				☐ 1300N:200E-CH16	9/9/2026					
		☐ 200E:1800N-IL116	8/24/2026				☒ 150E:1300N-1400N	9/9/2026				☐ 150E:1300N-1400N	9/9/2026				☐ 150E:1300N-1400N	9/9/2026				☐ 150E:1300N-1400N	9/9/2026					
		☐ 1600N:CH16-400E	8/24/2026				☒ 200E:CH8-1300N	9/9/2026				☐ 200E:CH8-1300N	9/9/2026				☐ 200E:CH8-1300N	9/9/2026				☐ 200E:CH8-1300N	9/9/2026					
		☐ 1300N:150E-100E	9/15/2026				☒ 200E:1300N-1400N	9/9/2026				☐ 200E:1300N-1400N	9/9/2026				☐ 200E:1300N-1400N	9/9/2026				☐ 200E:1300N-1400N	9/9/2026					
		☐ 1300N:200E-150E	9/15/2026				☐ 700E:1600N-IL116	9/11/2026				☐ 700E:1600N-IL116	9/11/2026				☐ 700E:1600N-IL116	9/11/2026				☐ 700E:1600N-IL116	9/11/2026					
		☐ 150E:1300N-1400N	9/15/2026				☐ 700E:1500N-1600N	9/11/2026				☐ 700E:1500N-1600N	9/11/2026				☐ 700E:1500N-1600N	9/11/2026				☐ 700E:1500N-1600N	9/11/2026					
		☒ 700E:1600N-IL116	9/11/2026				☐ 1400N:CH16-400E	9/9/2026				☐ 1400N:CH16-400E	9/9/2026				☐ 1400N:CH16-400E	9/11/2026				☐ 1400N:CH16-400E	9/11/2026					
		☒ 700E:1500N-1600N	9/11/2026				☐ 1400N:400E-500E	9/9/2026				☐ 1400N:400E-500E	9/9/2026				☐ 1400N:400E-500E	9/11/2026				☐ 1400N:400E-500E	9/11/2026					
		☐ 1400N:CH16-400E	9/9/2026				☐ 500E:1400N-1500N	9/9/2026				☐ 500E:1400N-1500N	9/9/2026				☐ 500E:1400N-1500N	9/11/2026				☐ 500E:1400N-1500N	9/11/2026					
		☐ 1400N:400E-500E	9/9/2026				☐ 1600N:700E-800E	9/9/2026				☐ 1600N:700E-800E	9/9/2026				☐ 1600N:700E-800E	9/9/2026				☐ 1600N:700E-800E	9/9/2026					
		☐ 500E:1400N-1500N	9/9/2026				☐ 1600N:400E-700E	9/9/2026				☐ 1600N:400E-700E	9/9/2026				☐ 1600N:400E-700E	9/9/2026				☐ 1600N:400E-700E	9/9/2026					
Short Duration Road Closures							☐ 1600N:500E-600E	9/9/2026				☐ 1600N:500E-600E	9/9/2026				☐ 1600N:500E-600E	9/9/2026				☐ 1600N:500E-600E	9/9/2026					
							☐ 1600N:400E-500E	9/9/2026				☐ 1600N:400E-500E	9/9/2026				☐ 1600N:400E-500E	9/9/2026				☐ 1600N:400E-500E	9/9/2026					
							☐ 500E:1500N-1600N	9/9/2026				☐ 500E:1500N-1600N	9/9/2026				☐ 500E:1500N-1600N	9/9/2026				☐ 500E:1500N-1600N	9/9/2026					
							☐ 500E:IL116-1600N	9/9/2026				☐ 500E:IL116-1600N	9/9/2026				☐ 500E:IL116-1600N	9/9/2026				☐ 500E:IL116-1600N	9/9/2026					
							☐ 600E:1500N-1600N	8/24/2026				☐ 600E:1500N-1600N	8/24/2026				☐ 600E:1500N-1600N	9/1/2026				☐ 600E:1500N-1600N	9/1/2026					
							☐ 600E:IL116-1600N	8/24/2026				☐ 600E:IL116-1600N	8/24/2026				☐ 600E:IL116-1600N	9/1/2026				☐ 600E:IL116-1600N	9/1/2026					
																	☒ CH16:IL116-1600N	9/14/2026				☐ CH16:IL116-1600N	9/14/2026					
																	☒ CH13:1000N-900N	Trench West				☐ CH13:1000N-900N	9/18/2026					
																	☒ CH13:1100N-1000N	Trench West				☐ CH13:1100N-1000N	9/18/2026					
																	☒ CH13:CH8-1100N	Trench West				☐ CH13:CH8-1100N	9/18/2026					
																	☐ CH13:1000N-900N	9/18/2026				☐ CH13:1000N-900N	9/18/2					

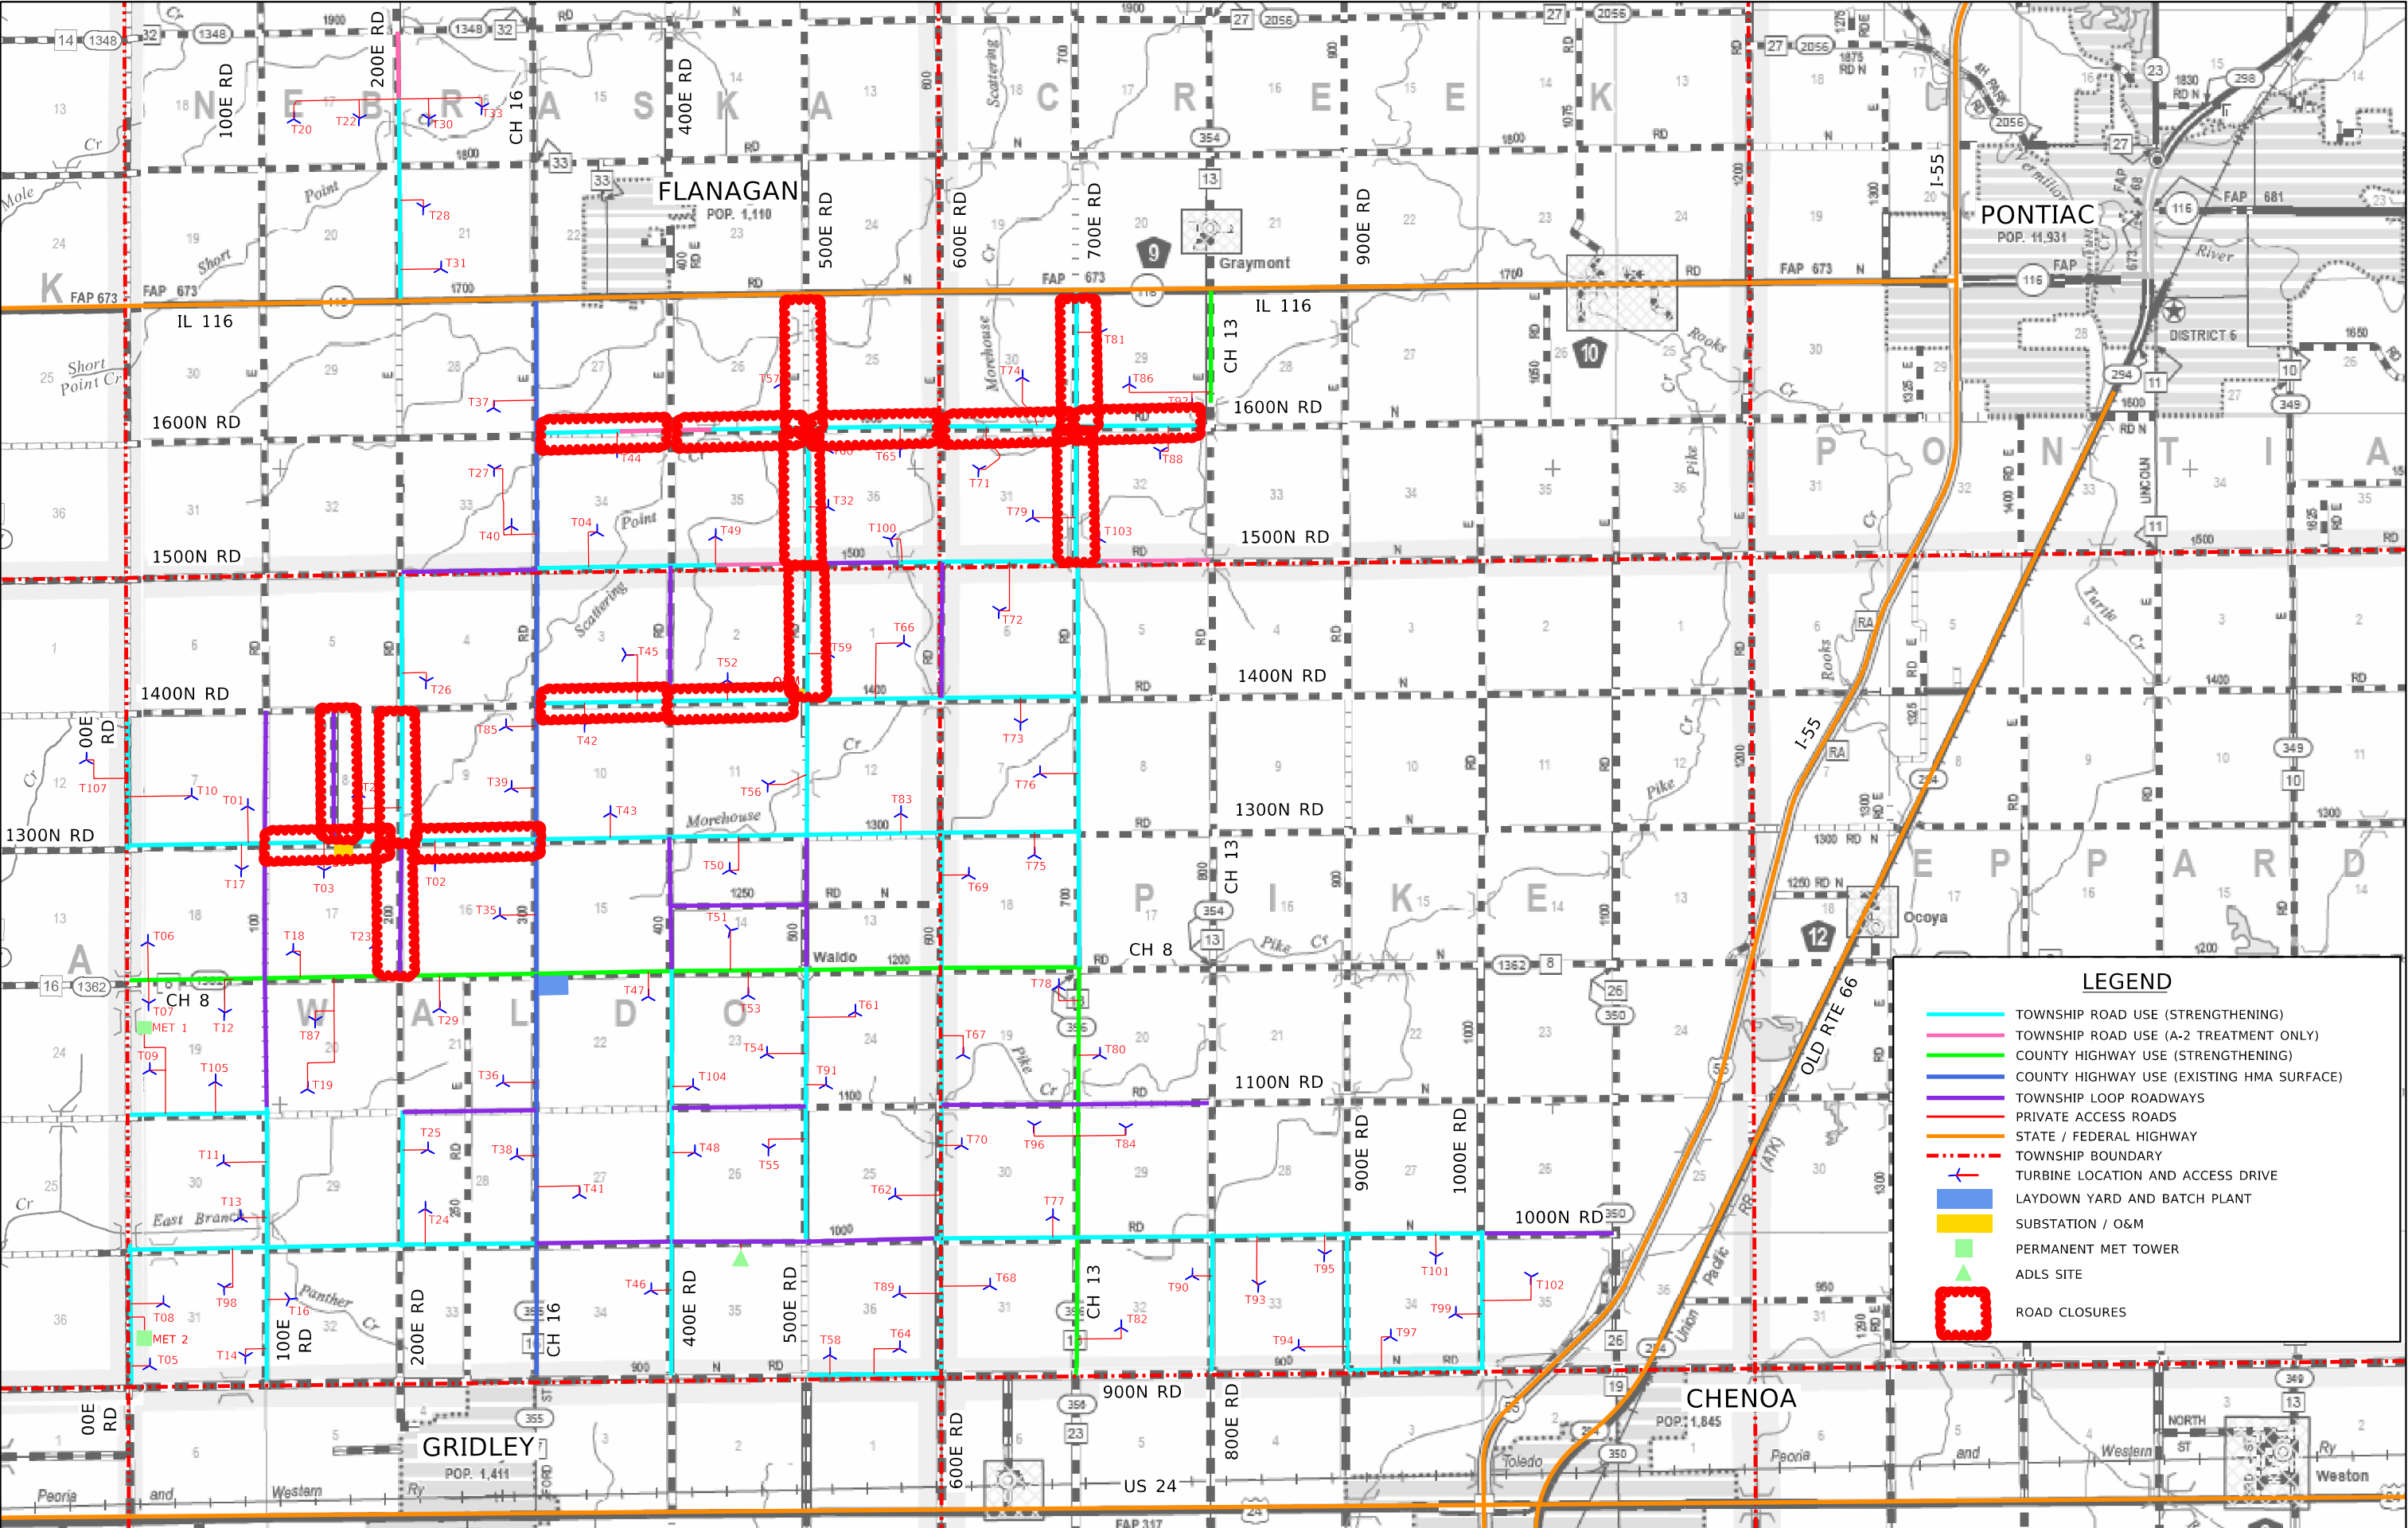

LEGEND

TOWNSHIP ROAD USE (STRENGTHENING)

TOWNSHIP ROAD USE (A-2 TREATMENT ONLY)

COUNTY HIGHWAY USE (STRENGTHENING)

COUNTY HIGHWAY USE (EXISTING HMA SURFACE)

TOWNSHIP LOOP ROADWAYS

PRIVATE ACCESS ROADS

STATE / FEDERAL HIGHWAY

TOWNSHIP BOUNDARY

TURBINE LOCATION AND ACCESS DRIVE


LAYDOWN YARD AND BATCH PLANT

SUBSTATION / O&M

PERMANENT MET TOWER

ADLS SITE

ROAD CLOSURES

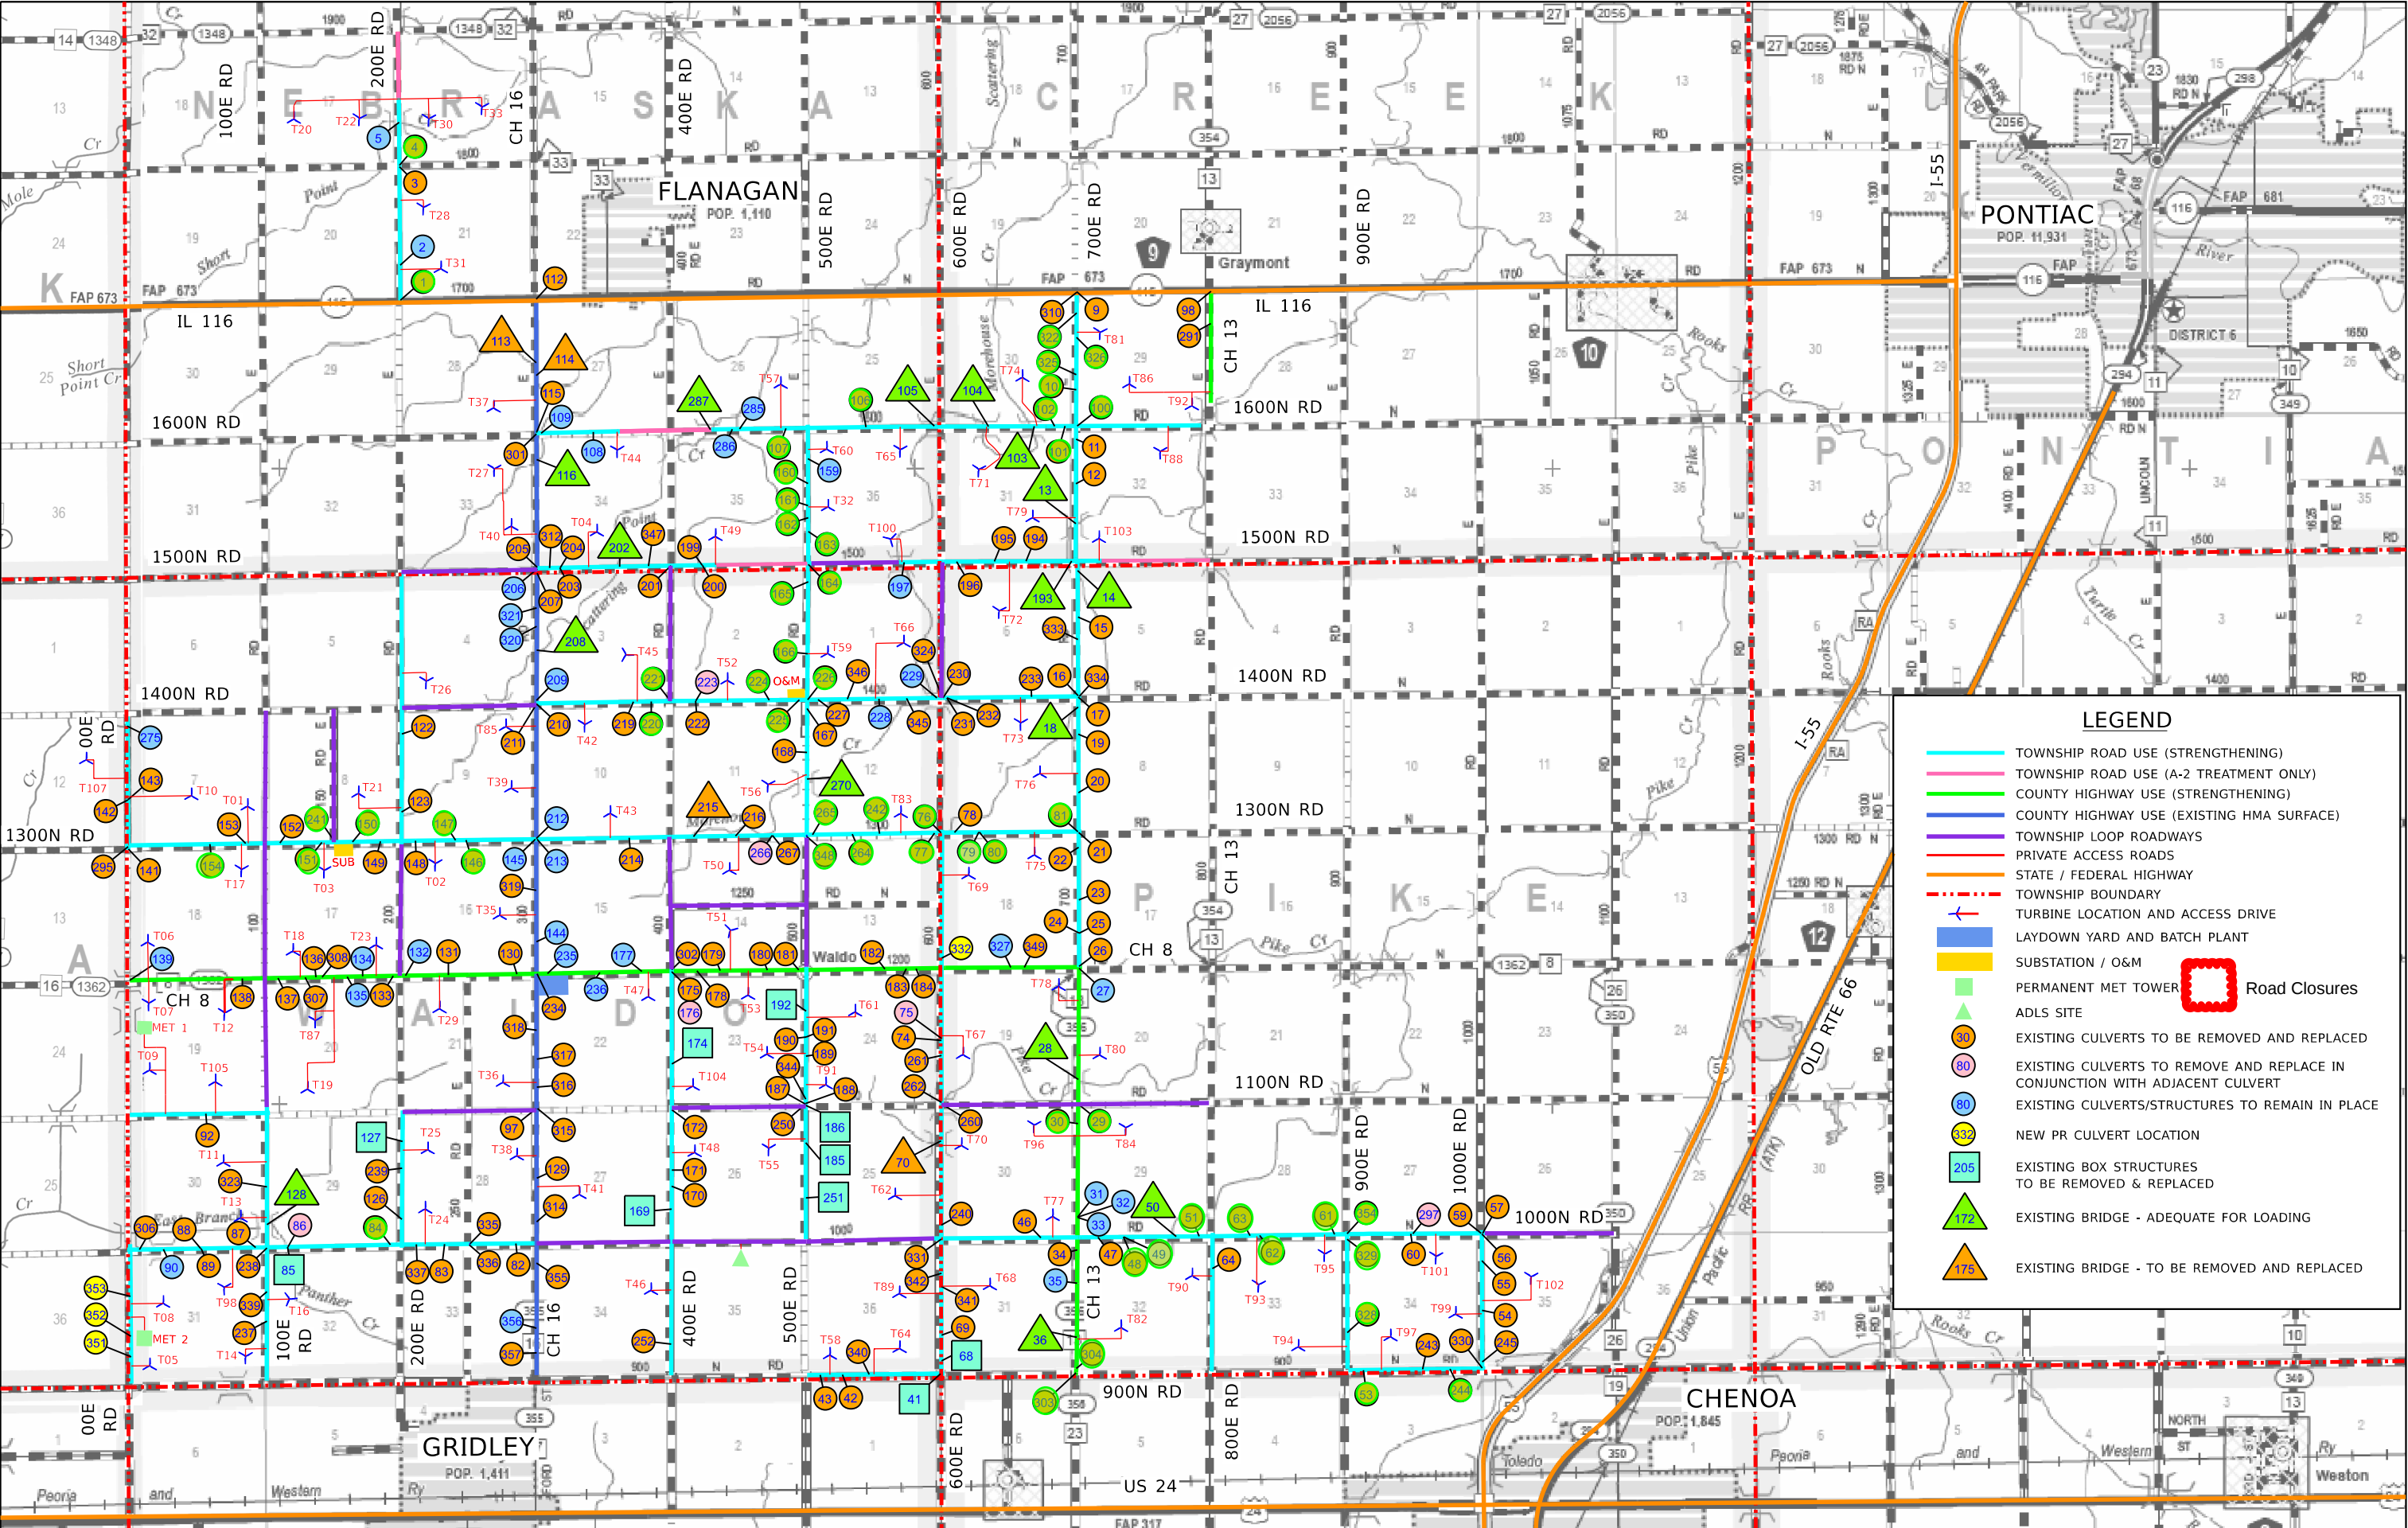

LEGEND

TOWNSHIP ROAD USE (STRENGTHENING)

TOWNSHIP ROAD USE (A-2 TREATMENT ONLY)

COUNTY HIGHWAY USE (STRENGTHENING)

COUNTY HIGHWAY USE (EXISTING HMA SURFACE)

TOWNSHIP LOOP ROADWAYS

PRIVATE ACCESS ROADS

STATE / FEDERAL HIGHWAY

TOWNSHIP BOUNDARY

TURBINE LOCATION AND ACCESS DRIVE

LAYDOWN YARD AND BATCH PLANT

SUBSTATION / O&M

PERMANENT MET TOWER

ADLS SITE

EXISTING CULVERTS TO BE REMOVED AND REPLACED

EXISTING CULVERTS TO REMOVE AND REPLACE IN CONJUNCTION WITH ADJACENT CULVERT

EXISTING CULVERTS/STRUCTURES TO REMAIN IN PLACE

NEW PR CULVERT LOCATION

EXISTING BOX STRUCTURES TO BE REMOVED & REPLACED

EXISTING BRIDGE - ADEQUATE FOR LOADING

EXISTING BRIDGE - TO BE REMOVED AND REPLACED

Road Closures

1	4/10/2026	REV 1
00	2/20/2026	IFC SUBMITTAL
REV	DATE	DESCRIPTION

DESIGNED - JDA
DRAWN - DRR/LNS
CHECKED - ML
DATE - 04/14/2026

PANTHER GROVE 2 WIND PROJECT
LIVINGSTON COUNTY, ILLINOIS

EXHIBIT A - PROJECT LAYOUT MAP (REVISION 1)

SCALE: N.T.S. SHEET 1 OF 1 SHEETS STA. TO STA.

Farnsworth GROUP

100 WALNUT ST #200
PEORIA, ILLINOIS 61602
(309) 689-9888 / info@f-w.com

TOTAL SHEETS	SHEET NO.	REVISION NO.
