

Panther Grove 2

	5-Aug-26	Today
Daily Weather as of 7:00am	0	0
Low Temperature (F)	68	67
High Temperature (F)	80	79
Ground Wind Speed (MPH):	9 MPH	6 MPH
Precipitation (in)	0.00	50%
August Precip Total (in)	1.60	

	ACTIVITY
Laydown Yard	Install Laydown Yard
Public Roads	Strip Public Road Radii
	Mowing Public Road Radii
	Stone Public Road Radii
Access Roads	Strip Access Road
	Cement Stabilization
	Stone Access Road
	Strip Access Road Radii
	Stone Access Road Radii
Foundations	Strip Sites
	Geo-Piers
	Excavate Foundations
	Mud Mat
	Rebar Delivery
	Rebar Bottom Mat
	Anchor Bolt Build
	Anchor Bolt Set
	Internal Grounding
	Rebar Top Mat
	Base Conduit
	Pour Base
	Rebar Pedestal
	Form Pedestal
	Pour Pedestal
	Backfill Foundation
	Crane Pad Subgrade
	Crane Pad Stabilization
	Crane Pad Stone
	Set Load Spreader Plate
	Set Grout Forms
	Pour Grout

[illegible]

Daily Safety Topics

On going weather events- Reminder to check your sites and plan around on-going events. Set yourselves up for success by coming up with a game plan to pick up and cab out.

Truck Rodeo- We will be having a truck rodeo to inspect trucks and update any needed info or safety equipment.

*subject to change because of weather

Site Notes

Thursday, August 6, 2026

[illegible][illegible]

Quantity Tracking

QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
	25	ACRE	25.0	100.0%
	6	EA	35	17.1%
				5.7%
	2	EA	35	5.7%
	18821.5	LF	161120	11.7%
	14128	LF	161120	8.8%
3	12087	LF	161120	7.5%
2	22	EA	140	15.7%
1	13	EA	140	9.3%
2	15	EA	105	14.3%
	0	EA	14	0.0%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	2	EA	105	1.9%
	0	EA	105	0.0%
	0	EA	105	0.0%
	0	EA	105	0.0%

Site Information

Manpower

[illegible]

30	Total


Equipment

10	Pickup Trucks
2	Dozers
2	Skid Steers
2	Rollers
2	Graders
3	Cargo Trailers
2	Reclaimer Stabilizer
1	Excavators
2	Smooth Drum Roller
3	Trailers
3	Water Trucks
2	Sheepfoot roller

34	Total
Qty Executed	Completion Certificates
0/20	WTG Civil Works Completion
0/105	WTG Foundation Completion
0/105	WTG Mechanical Completion
0/20	Collection Circuit Mechanical Completion
0/1	Substation Mechanical Completion
0/1	Electrical Substantial Completion
0/1	O&M Building Substantial Completion
0/1	Final Completion

Additional Comments

--

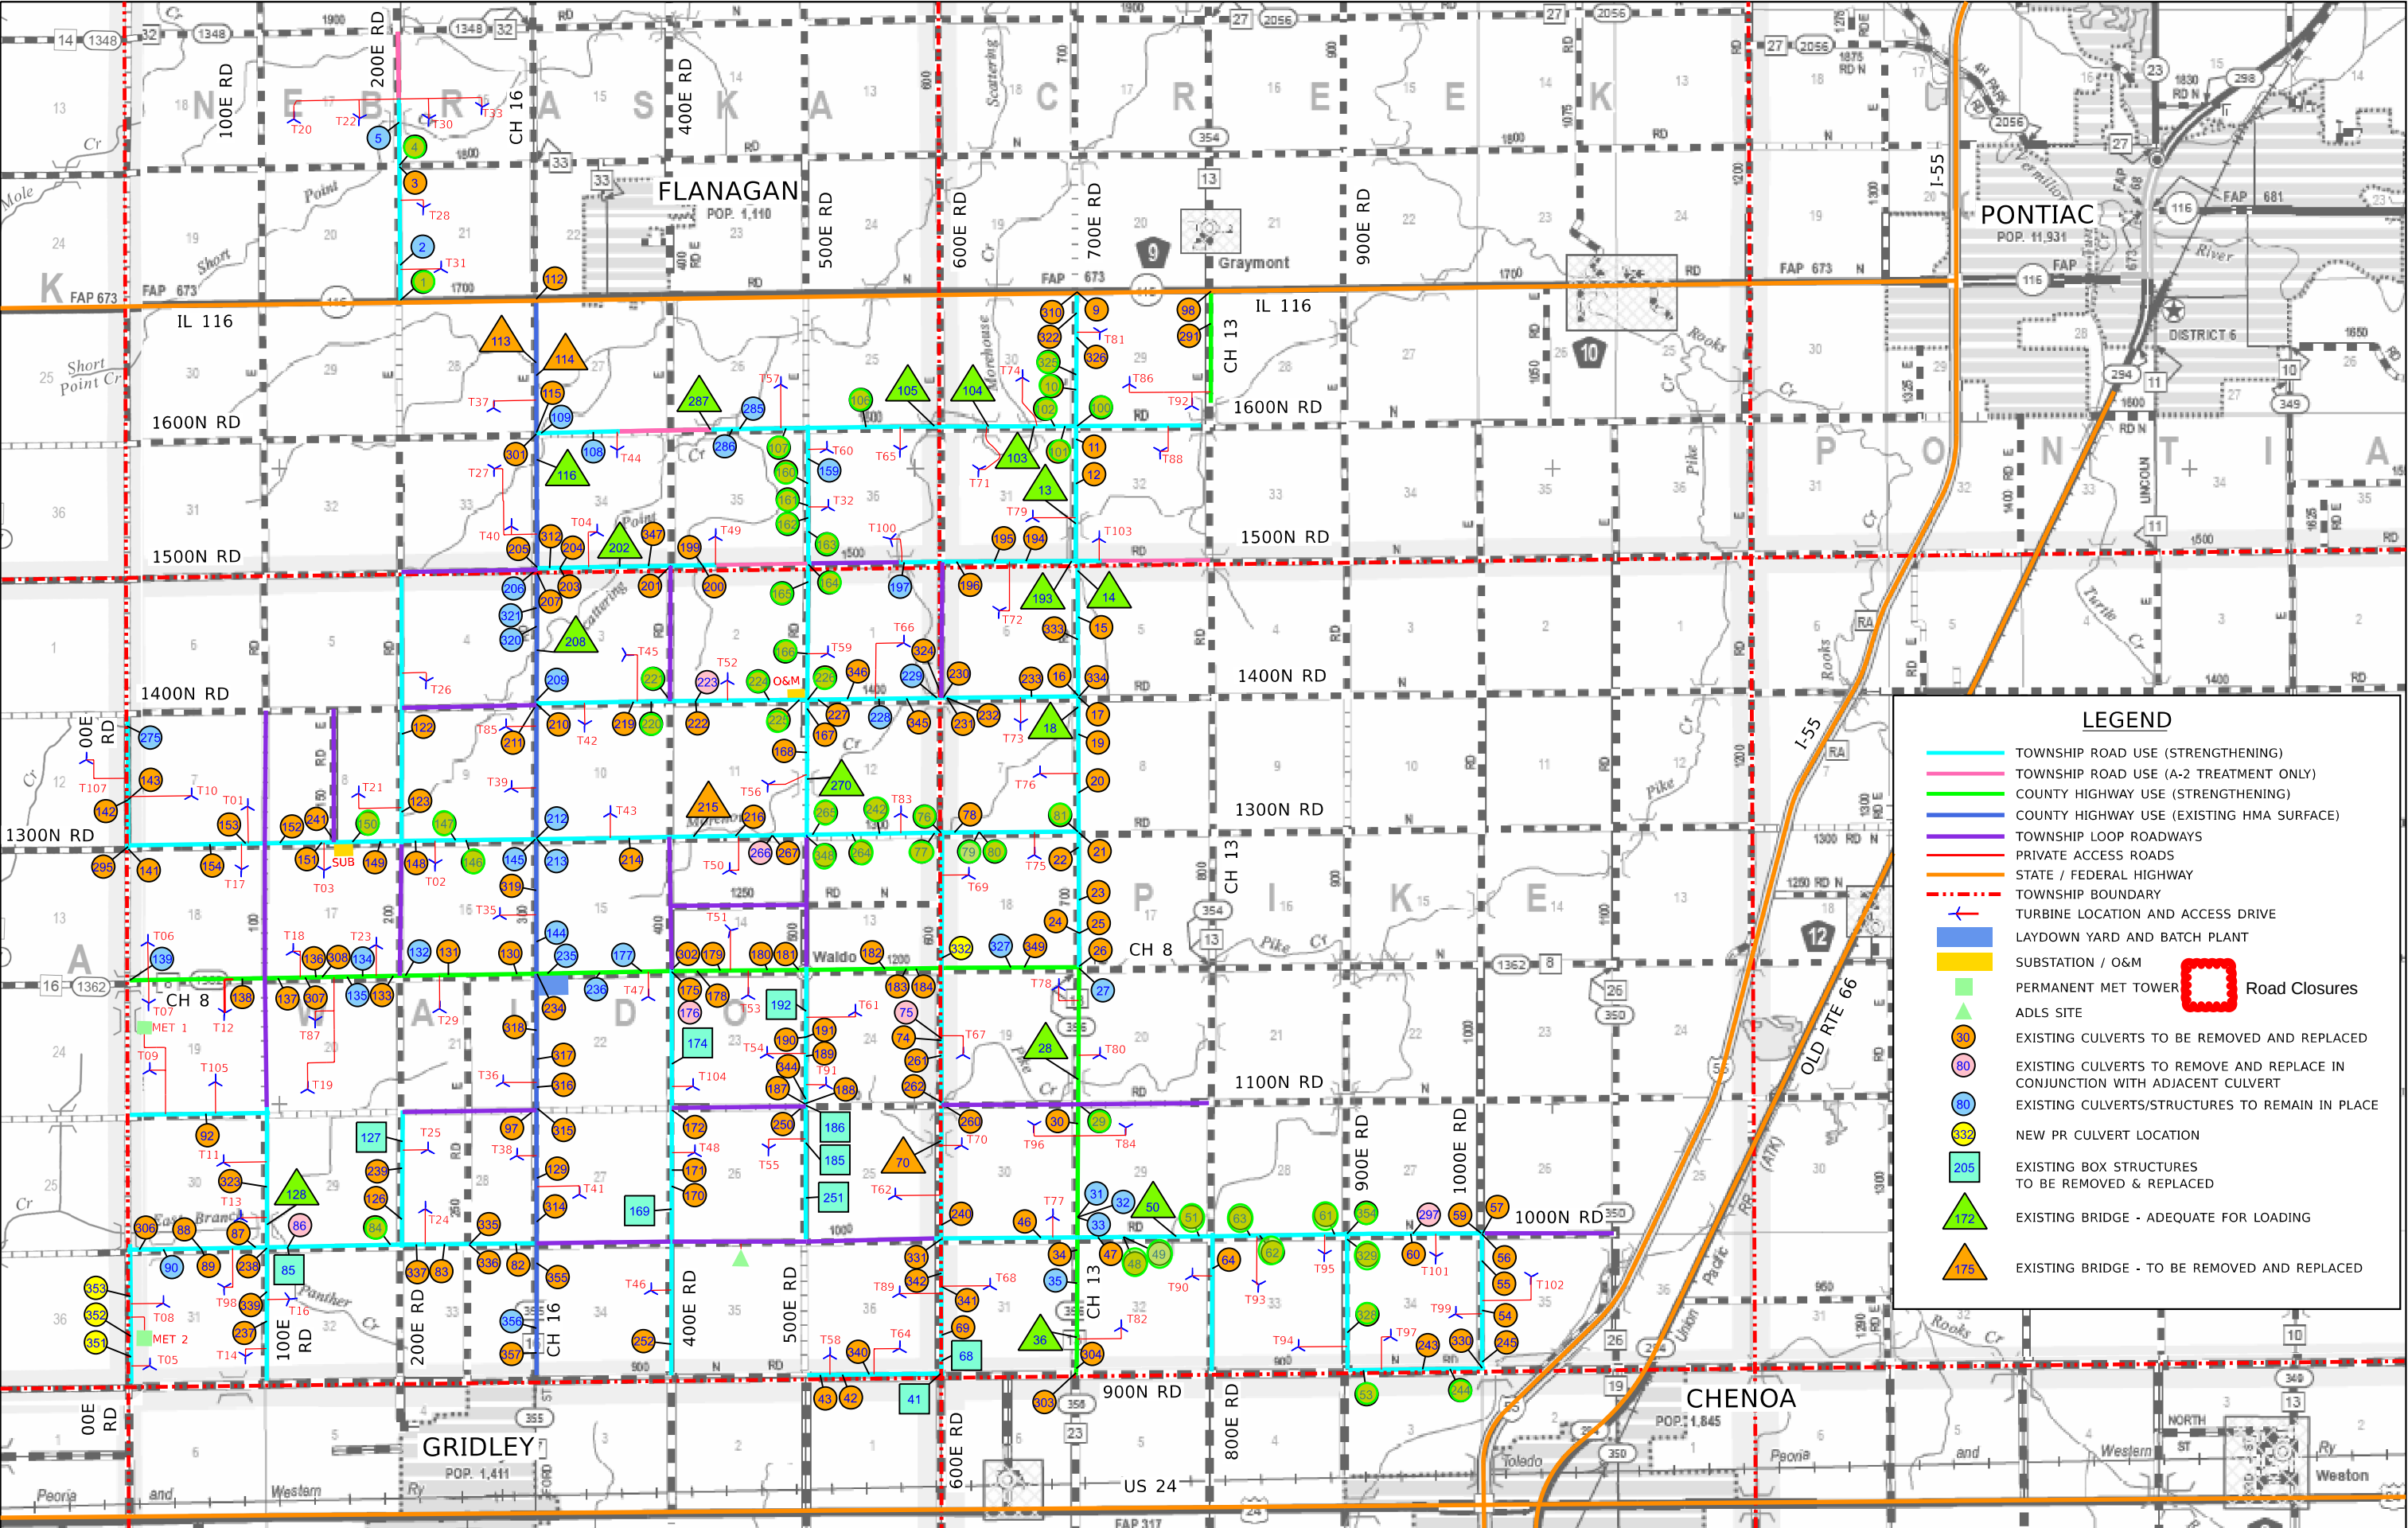

LEGEND

TOWNSHIP ROAD USE (STRENGTHENING)

TOWNSHIP ROAD USE (A-2 TREATMENT ONLY)

COUNTY HIGHWAY USE (STRENGTHENING)

COUNTY HIGHWAY USE (EXISTING HMA SURFACE)

TOWNSHIP LOOP ROADWAYS

PRIVATE ACCESS ROADS

STATE / FEDERAL HIGHWAY

TOWNSHIP BOUNDARY

TURBINE LOCATION AND ACCESS DRIVE

LAYDOWN YARD AND BATCH PLANT

SUBSTATION / O&M

PERMANENT MET TOWER

ADLS SITE

EXISTING CULVERTS TO BE REMOVED AND REPLACED

EXISTING CULVERTS TO REMOVE AND REPLACE IN CONJUNCTION WITH ADJACENT CULVERT

EXISTING CULVERTS/STRUCTURES TO REMAIN IN PLACE

NEW PR CULVERT LOCATION

EXISTING BOX STRUCTURES TO BE REMOVED & REPLACED

EXISTING BRIDGE - ADEQUATE FOR LOADING

EXISTING BRIDGE - TO BE REMOVED AND REPLACED

Road Closures
