

Panther Grove 2

	18-Jul-26	Today
Daily Weather as of 7:00am	0	0
Low Temperature (F)	64	73
High Temperature (F)	91	88
Ground Wind Speed (MPH):	12 MPH	9 MPH
Precipitation (in)	0.00	10%
July Precip Total (In)	2.67	

	ACTIVITY
Public Roads	
	Road Closures (Curing Roads)
	Road Closures (Pipe Culverts)
	Road Closures
	Culvert Work
	Road Pulverization
	Cement Stabilization
	Agg Surface Install
	Oil and Chip
	Earthen Shoulders
	Aggregate Widening
	Strip Public Road Radii
	Mowing Public Road Radii
	Stone Public Road Radii
Strip Access Road	
Cement Stabilization	
Stone Access Road	

[illegible]

Daily Safety Topics	
Site Conditions- with the small cell that keep in let's make sure we do a good assessment of our work area. Be your brothers/sisters keeper- Lets make sure we are keeping up with each other and doing buddy checks with this heat.	
Site Notes	

Monday, July 20, 2026


TODAY	
Monday, July 20, 2026	
LOCATION(S)	
	600E:1500N-1600N (Cure day 4) 600E:IL116-1600N (Cure day 4) 1600N:500E-600E (Cure day 4) 1600N:700E-800E (Cure day 4)
	1300N:400E-500E (245,348) 1300N:500E-600E (348) 600E:1300N-1400N (348) 600E:Ch8-1300N (348)
	200E:1800N-1900N (Agg Cap/Earth Shoulders) 1800N:100E-200E (Agg Cap/Earth Shoulders) 1800N:200E-300E (Agg Cap/Earth Shoulders) 200E:1800N-IL116 (Agg Cap/Earth Shoulders) 1600N:400E-CH16 (Agg Cap/Earth Shoulders) 1600N:400E-500E (widening/pulverization)
	265,348
	1600N:400E-500E
	200E:1800N-1900N 1800N:100E-200E 1800N:200E-300E 200E:1800N-IL116 1600N:400E-CH16
	No work available
	200E:1800N-1900N 1800N:100E-200E 1800N:200E-300E 200E:1800N-IL116
	P9 (1500-Hwy16) P11 (1400-Hwy16)
	T41, T38, T36, T35, T39, T85, T40, T27


NEXT WORKING DAY	
Tuesday, July 21, 2026	
LOCATION(S)	
600E:1500N-1600N (Cure day 5) 600E:IL116-1600N (Cure day 5) 1600N:500E-600E (Cure day 5) 1600N:700E-800E (Cure day 5)	
900N:1000E-900E (244,243)	
200E:1800N-1900N (Earth Shoulders) 1800N:100E-200E (Earth Shoulders) 1800N:200E-300E (Earth Shoulders) 200E:1800N-IL116 (Earth Shoulders) 1600N:400E-CH16 (Agg Cap) 1600N:500E-600E (Agg Cap) 1600N:400E-500E (stabilization)	
244,243	
1600N:400E-500E 1600N:500E-600E	
1600N:400E-CH16	
200E:1800N-1900N 1800N:100E-200E 1800N:200E-300E 200E:1800N-IL116 1600N:400E-CH16	
P9 (1500-Hwy16) P11 (1400-Hwy16)	
T41, T38, T36, T35, T39, T85, T40, T27	



Quantity Tracking				
QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
2	32	EA	222	14.4%
	23,781.86	LF	374014	6.4%
	20,250.22	LF	374014	5.4%
	5402	LF	374014	1.4%
	0	LF	374014	0.0%
	0	LF	374014	0.0%
	0	LF	374014	0.0%
	2	EA	35	5.7%
	0	EA	35	0.0%
	0	LF	161120	0.0%
	12945	LF	161120	8.0%
	0	LF	161120	0.0%

Site Information	
Manpower	
4	White Construction Management
15	White Construction Operators
10	White Construction Laborers
	White Construction Ironworkers
	White Construction Millwright
	White Construction Electrician
13	Dunn Company
	West Wind
4	Tobey's Construction & Cartage
7	KVCC
53	Total
Equipment	
11	Pickup Trucks
2	Dozers
3	Skid Steers
2	Rollers
2	Graders
2	Cargo Trailer
0	Cranes
1	Excavators
0	Forklift
3	Trailers

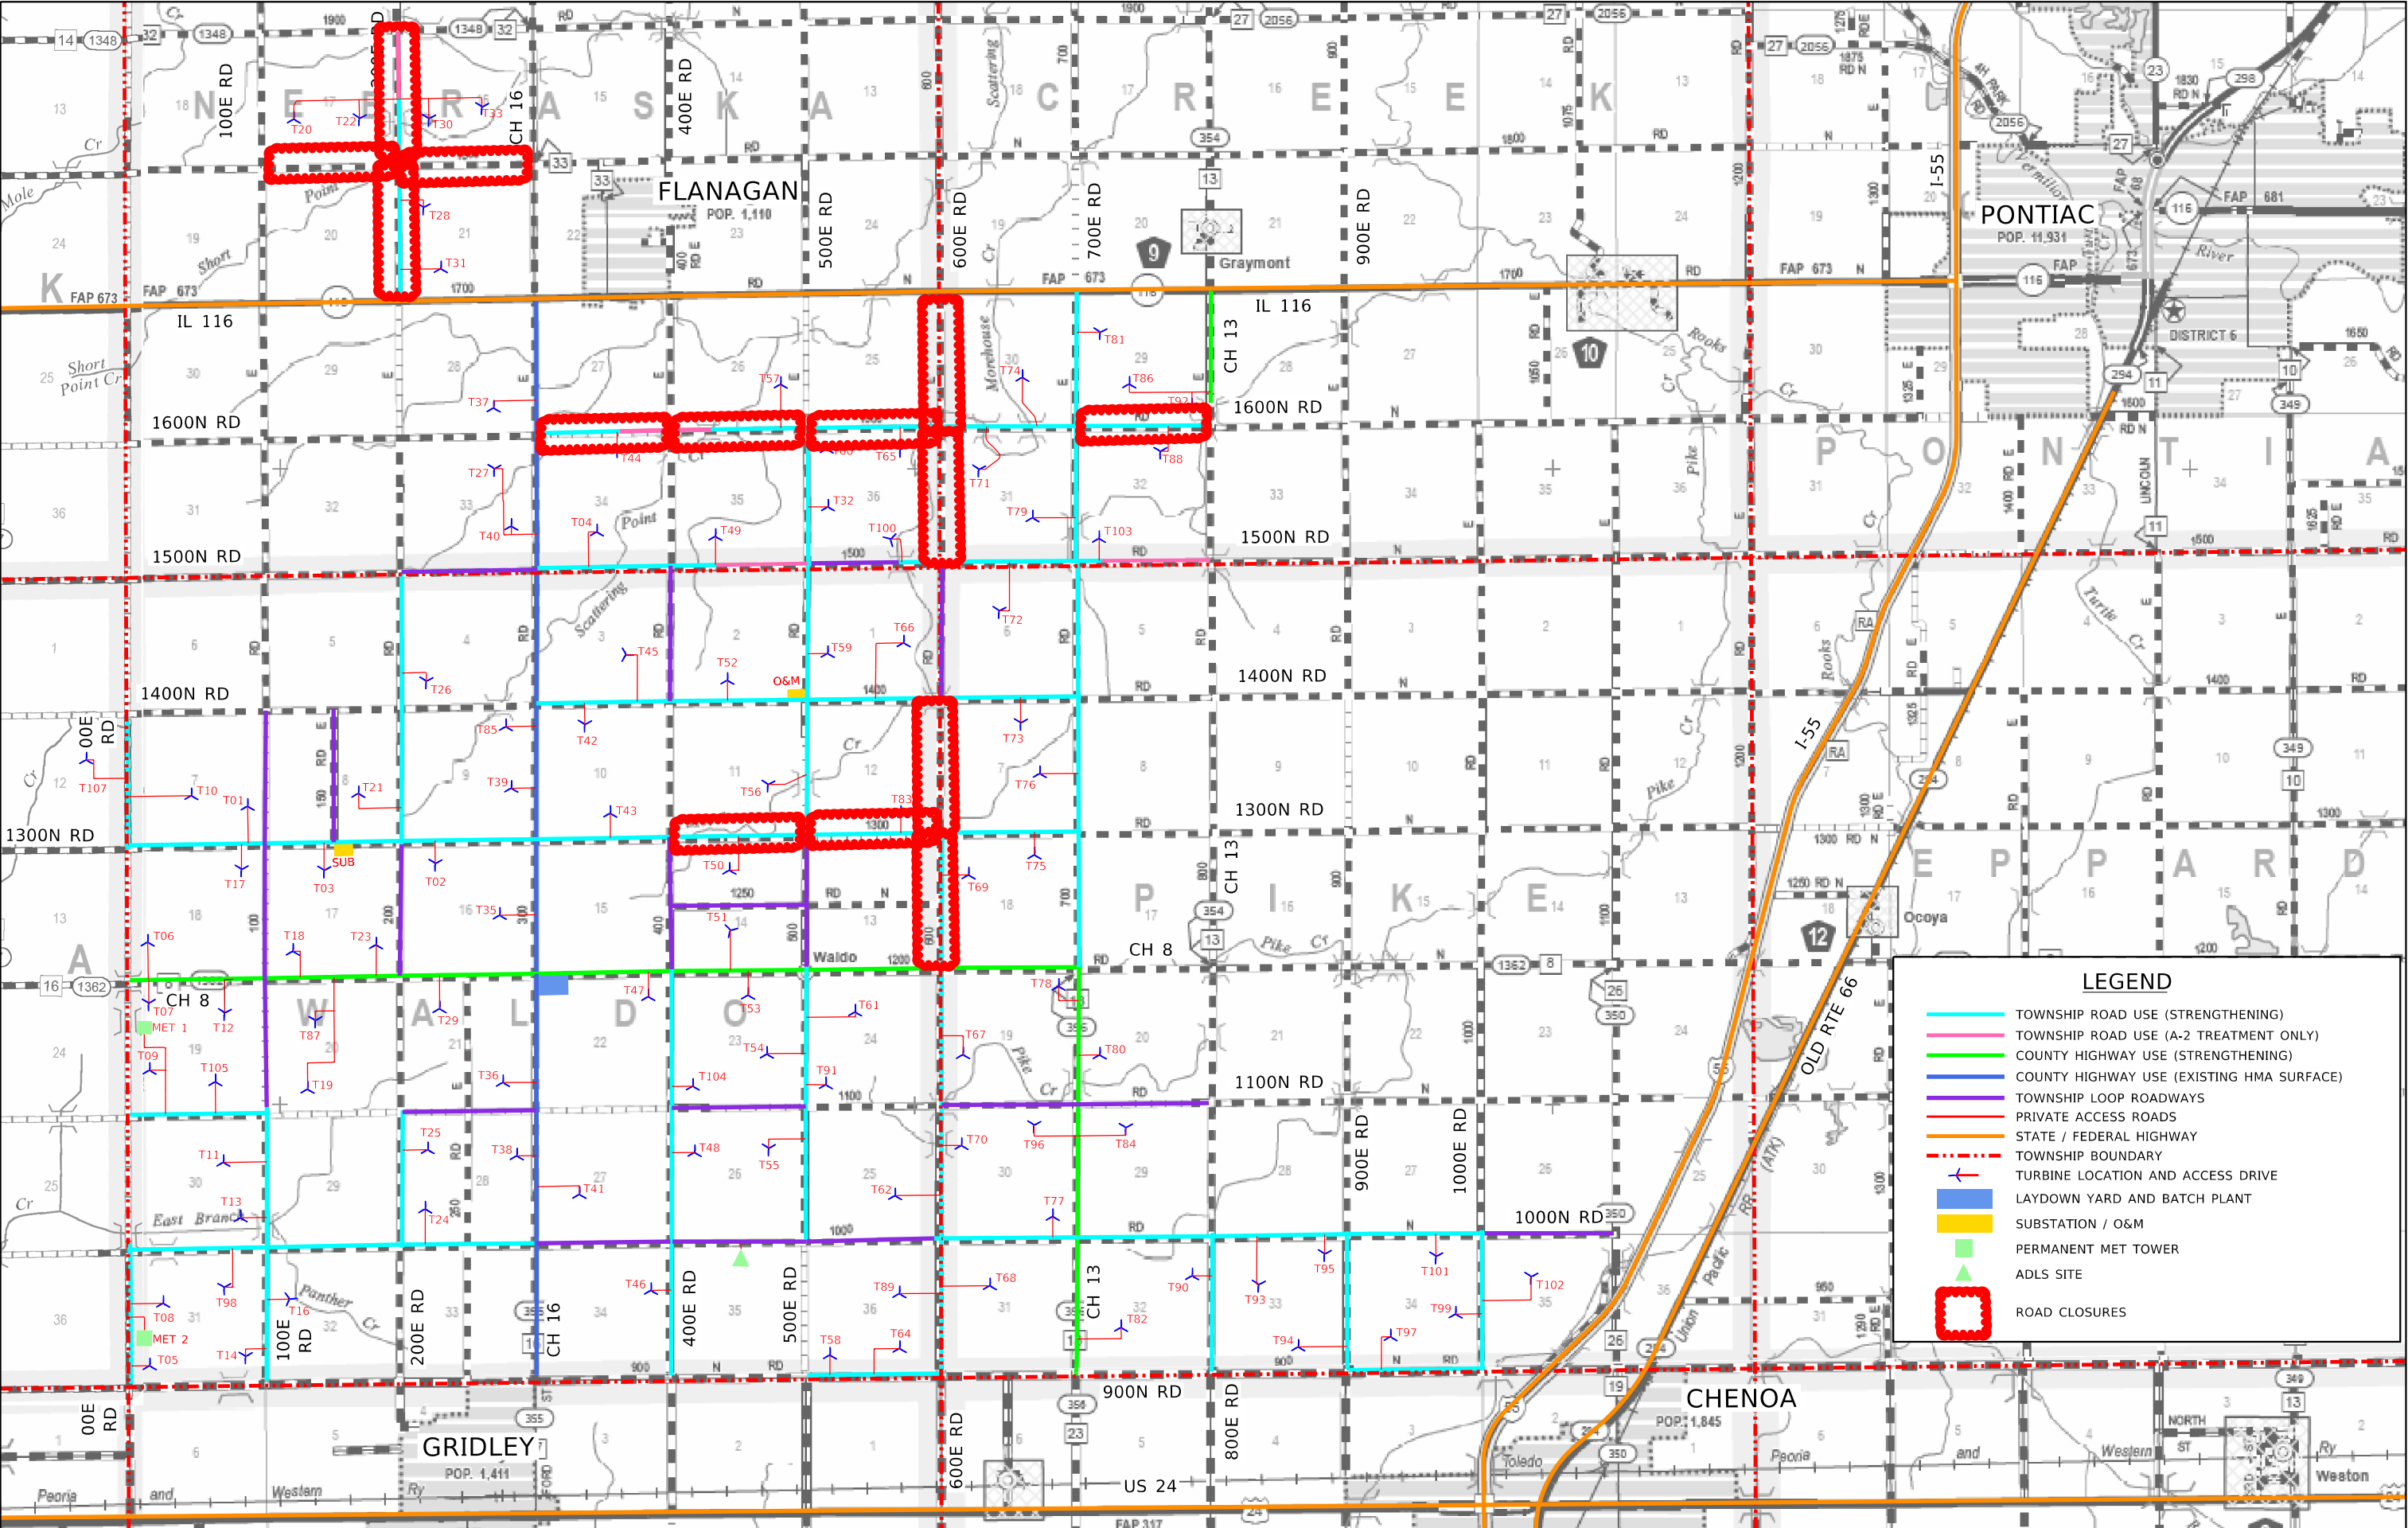

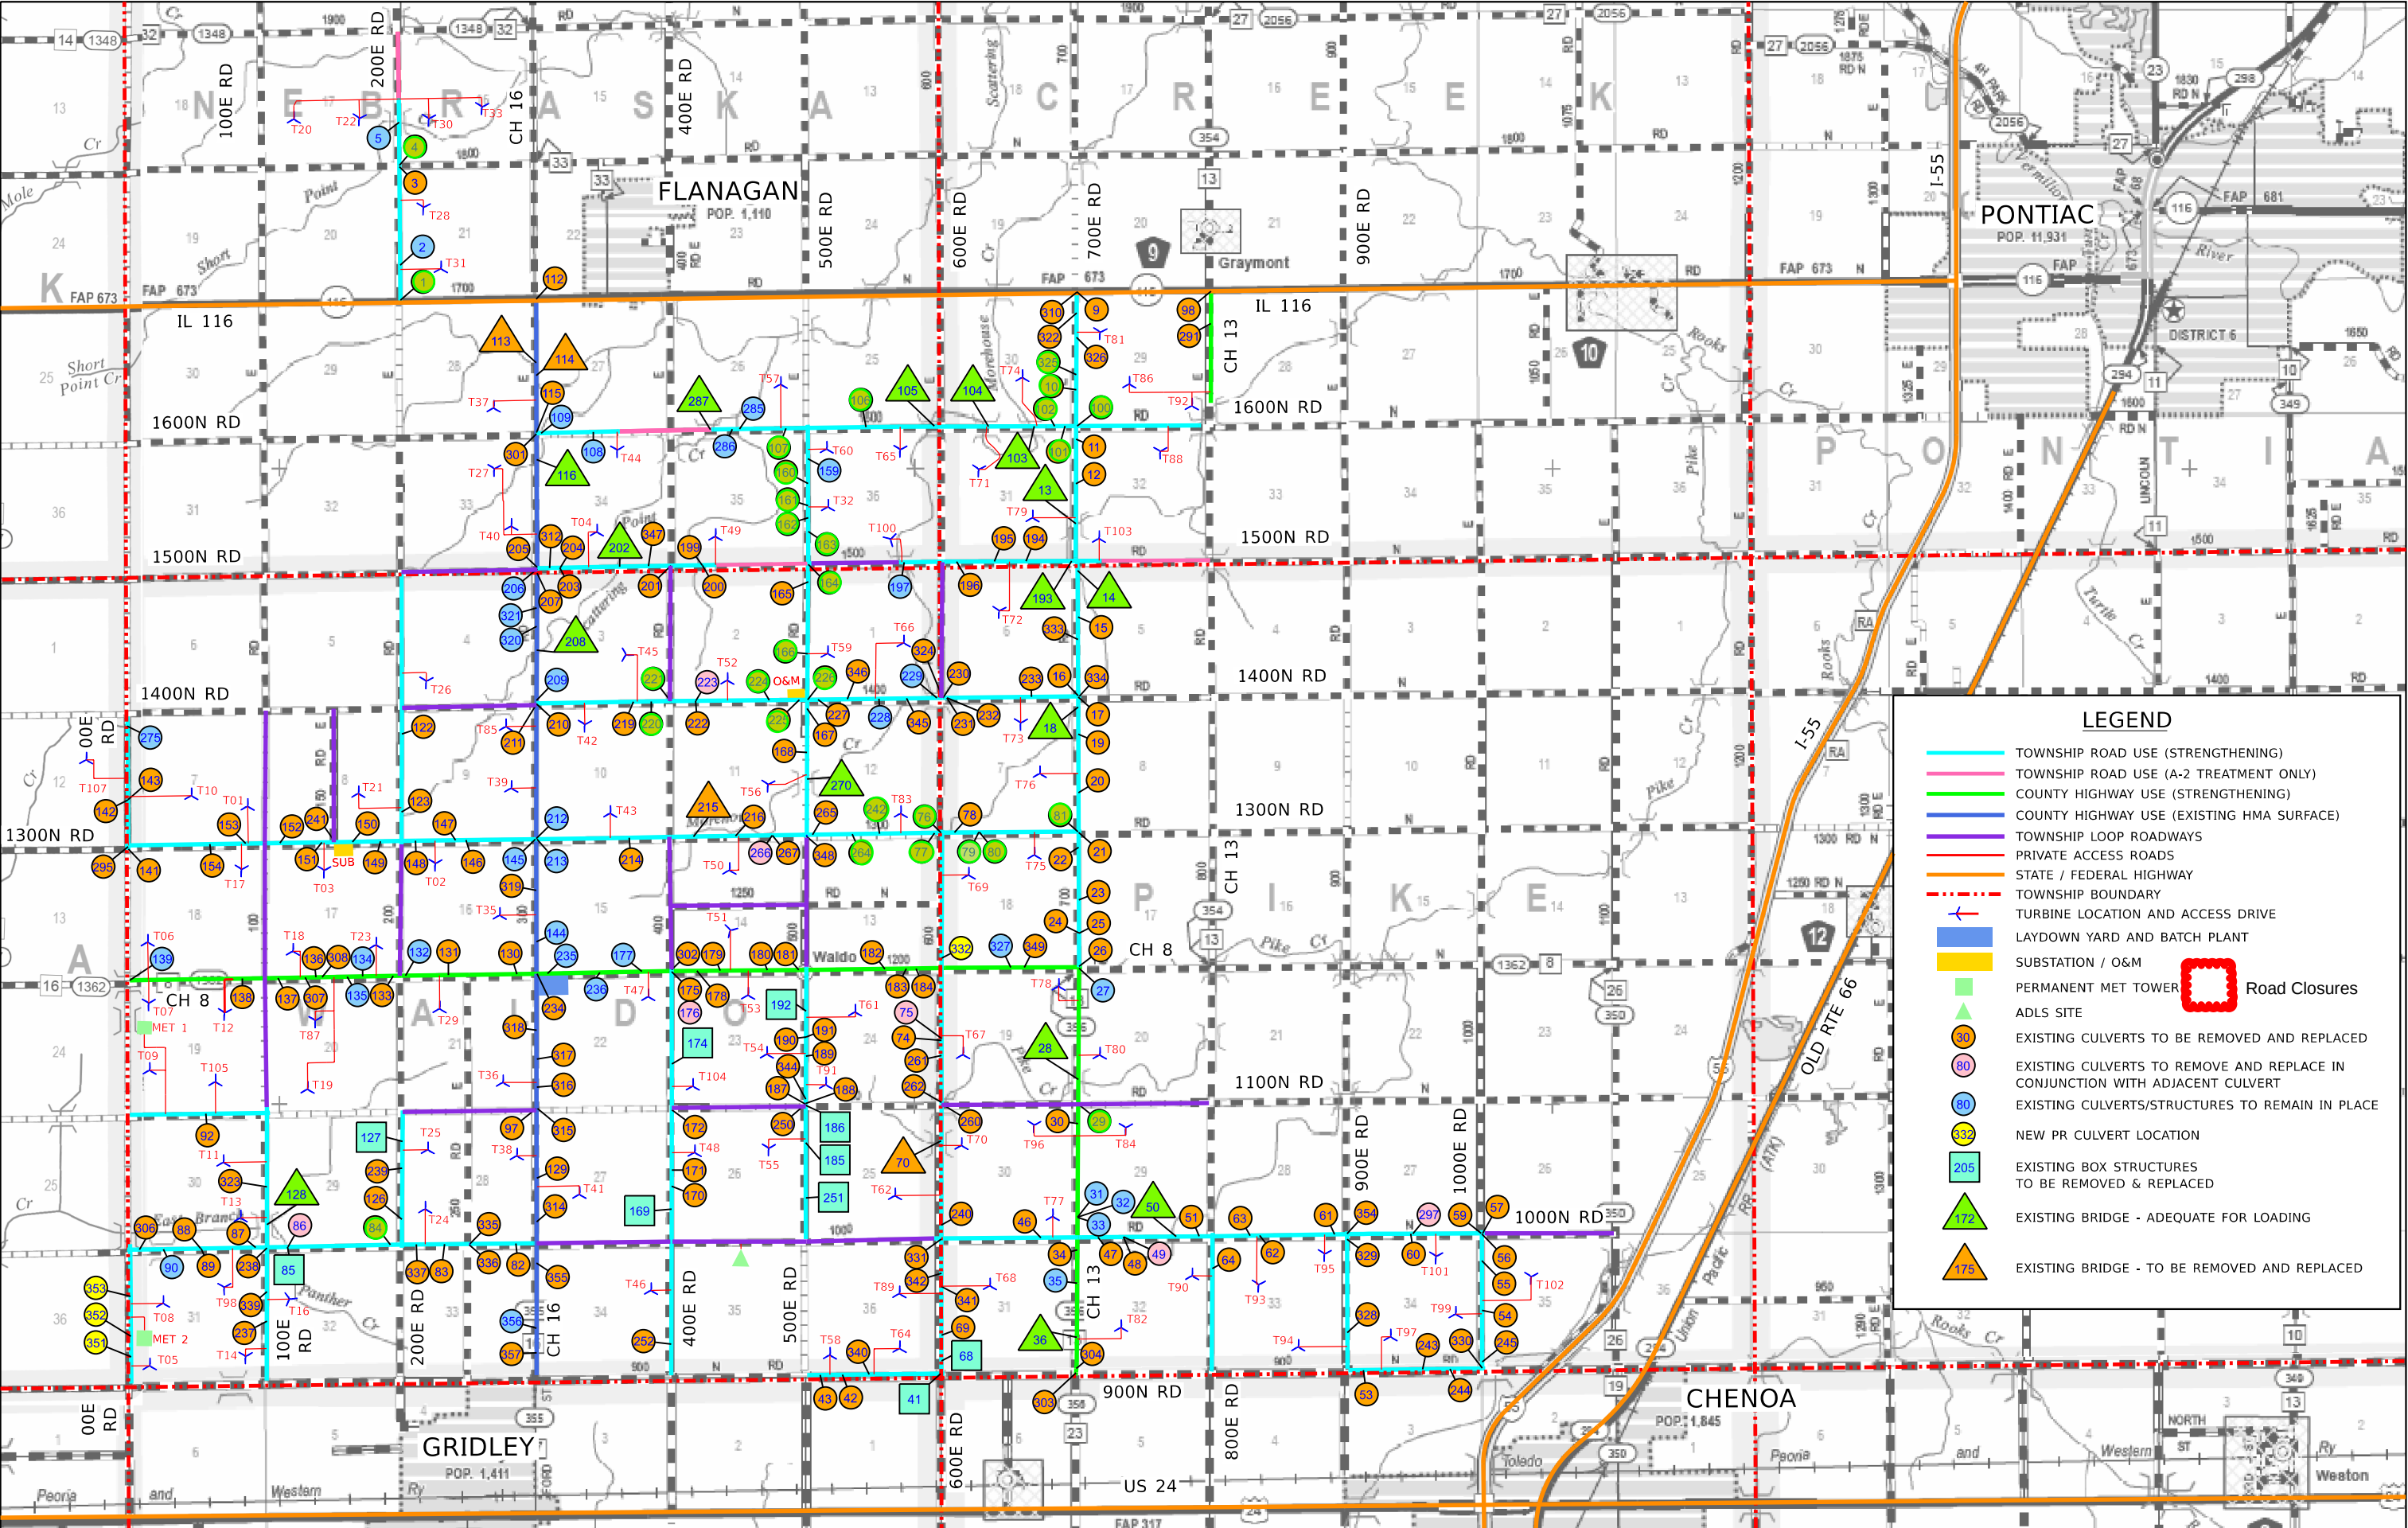

1	4/10/2026	REV 1	DESIGNED - JDA
00	2/20/2026	IFC SUBMITTAL	DRAWN - DRR/LNS
REV	DATE	DESCRIPTION	CHECKED - ML
			DATE - 04/14/2026

PANTHER GROVE 2 WIND PROJECT
LIVINGSTON COUNTY, ILLINOIS

EXHIBIT A - PROJECT LAYOUT MAP (REVISION 1)			
SCALE: N.T.S.	SHEET 1 OF 1 SHEETS	STA.	TO STA.

100 WALNUT ST #200
PEORIA, ILLINOIS 61602
(309) 689-9888 / info@f-w.com

TOTAL SHEETS	SHEET NO.	REVISION NO.
