

Panther Grove 2

	30-Oct-26	Today
Daily Weather as of 7:00am	Clear	Clear
Low Temperature (F)	52	54
High Temperature (F)	65	68
Ground Wind Speed (MPH):	10mph	9 mph
Precipitation (in)	0.00	15%
October Precip Total (in)	1.50	

	ACTIVITY
Public Roads	Strip Public Road Radii
	Mowing Public Road Radii
	Stone Public Road Radii
Access Roads	Strip Access Road
	Cement Stabilization
	Stone Access Road
	Strip Access Road Radii
	Stone Access Road Radii

LAST WORKING DAY
Friday, October 30, 2026
LOCATION(S)
Public Road
P2 (IL 116-CH 16)
T03
T02, T03

Daily Safety Topics
Headlights/Taillights: When doing daily inspections make sure your headlights and taillights are visible. Take the time to wipe any mud or dirt off them to allow them to be seen from a distance. And report any lighting issues so they can be replaced or repaired.
Ergonomics- fitting the job to the worker, rather than forcing the body to adapt to an uncomfortable or unsafe task.
Site Notes

Saturday, October 31, 2026

TODAY
Saturday, October 31, 2026
LOCATION(S)

NEXT WORKING DAY
Monday, November 2, 2026
LOCATION(S)
P2 (IL 116-CH 16)
T59, T52, T45
T03



Quantity Tracking				
QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
	11	EA	35	31.4%
	9	EA	35	25.7%
	66695	LF	161120	41.4%
	67827.5	LF	161120	42.1%
	55073.5	LF	161120	34.2%
	63	EA	TBD	#VALUE!
	59	EA	TBD	#VALUE!


Site Information	
Manpower	
19	White Construction Management
47	White Construction Operators
27	White Construction Laborers
16	White Construction Ironworkers
0	White Construction Millwright
3	White Construction Electrician
40	Dunn Company
8	West Wind
4	Tobey's Construction & Cartage
8	KVCC
6	Prairie Materials
19	JF Edwards
5	Keeley
202	Total
Equipment	
48	Pickup Trucks
3	Dozers
0	Rollers
1	Graders
1	Cargo Trailer
0	Cranes
3	Excavators
0	Forklift
13	Trailers
0	Sand Truck
1	Sheepfoot Roller
0	Reclaimer Stabilizer
1	Smooth Drum Roller
2	Water Trucks
5	Skid Steer
78	Total

Additional Comments

Weather Notes: Rain out on 10-15	65° / 44°	Temp Range	<div>Plan of the Day (POD) Report</div> <div>31-Oct-2026</div>	62° / 51°	Temp Range	65° / 53°	Temp Range	60° / 55°	Temp Range			
	19% 0.00 in None	Precipitation		18% 0.02 in 9 PM	Precipitation	15% 0.00 in None	Precipitation	41% 0.02 in 8 AM - 11 PM	Precipitation			
	None None	Lighting Risk		None None	Lighting Risk	None None	Lighting Risk	None None	Lighting Risk			
	None 0% None	Severe Forecast		None 0% None	Severe Forecast	None 0% None	Severe Forecast	None 0% None	Severe Forecast			
	12.2	Max Wind		12.7	Max Wind	15.7	Max Wind	17.3	Max Wind			
	24.4	Max Gust		23.3	Max Gust		26.4	Max Gust		34.4	Max Gust	
(S) Start (C) Continue (F) Finish	LAST WORKING DAY		<div></div> <div>Today's Notes</div>	TODAY		NEXT WORKING DAY		2-Day Lookahead				
	Friday, October 30, 2026			Saturday, October 31, 2026		Sunday, November 1, 2026		Monday, November 2, 2026				
	LOCATION(S)			LOCATION(S)		LOCATION(S)		LOCATION(S)				
Long Duration Road Closures	Road	Repening	<div><div>Active Cure</div><div>Date</div><div>Day</div><div>Cure</div></div> <div><div>CH8:CH16-400E</div><div>10/23</div><div>8</div><div>10/30</div></div> <div><div>N/A</div><div></div><div></div><div></div></div> <div><div>N/A</div><div></div><div></div><div></div></div> <div><div>N/A</div><div></div><div></div><div></div></div> <div><div>N/A</div><div></div><div></div><div></div></div> <div><div>Business</div><div>Scope</div><div>QTY</div></div> <div><div>Dunn Company</div><div>Agg Surface, Earthwork</div><div>15</div></div> <div><div>Tobey's Constr.</div><div>Pipe Culvert</div><div>0</div></div> <div><div>KVCC</div><div>Agg Surface</div><div>0</div></div> <div><div>Millennia</div><div>OC</div><div>0</div></div> <div><div>Material Serv. Test.</div><div>OC</div><div>0</div></div> <div><div>Beniach</div><div>Oil and Chip</div><div>0</div></div> <div><div>Notes:</div><div>Box Culvert: In procurement</div><div>Pipe Culvert: Ongoing</div><div>Agg Widening: On hold</div><div>Profile Adj./Add Rock: On hold</div><div>Pulverization: on hold</div><div>Stabilization: on hold</div><div>Agg Surface: on hold</div><div>Oil and Chip: on hold</div><div>Earthwork: Using existing material where possible, brining new to locations as needed. Roads listed in punchwork section.</div><div>Seeding: Resuming this week</div><div>HMA: On hold until IDOT permits are in place.</div><div>Punchlist: On going</div></div> <div><div>QTY Last Work Day</div><div>QTY Complete</div><div>Unit</div><div>Total QTY</div><div>% Complete</div></div>	<div><div>☐ 1300N:100E-150E</div><div>10/13/2026</div></div> <div><div>☐ 1300N:150E-200E</div><div>10/13/2026</div></div> <div><div>☐ 150E:1300N-1400N</div><div>10/13/2026</div></div> <div><div>☐ 1300N:200E-CH16</div><div>10/13/2026</div></div> <div><div>☐ 1600N:700E-800E</div><div>10/20/2026</div></div> <div><div>☐ 1600N:600E-700E</div><div>10/20/2026</div></div> <div><div>☐ 500E:IL116-1600N</div><div>10/13/2026</div></div> <div><div>☐ 1600N:400E-500E</div><div>10/13/2026</div></div> <div><div>☐ 1600N:500E-600E</div><div>10/13/2026</div></div> <div><div>☐ 500E:1500N-1600N</div><div>10/13/2026</div></div> <div><div>☐ 500E:1400N-1500N</div><div>10/13/2026</div></div> <div><div>☐ 1400N:400E-500E</div><div>10/13/2026</div></div> <div><div>☐ 1400N:CH16-400E</div><div>10/13/2026</div></div> <div><div>☐ CH8:CH13-600E</div><div>10/13/2026</div></div> <div><div>☐ CH13:900N-1000N</div><div>10/13/2026</div></div> <div><div>☐ 1000N:CH13-800E</div><div>10/13/2026</div></div> <div><div>☐ 1000N:CH13-600E</div><div>10/13/2026</div></div> <div><div>☐ CH13:1000N-1100N</div><div>10/13/2026</div></div> <div><div>☐ 1100N:CH13-800E</div><div>10/13/2026</div></div> <div><div>☐ 1100N:CH13-600E</div><div>10/13/2026</div></div> <div><div>☐ CH13:1100N-CH8</div><div>10/13/2026</div></div> <div><div>☐ CH8:CH13-600E</div><div>10/13/2026</div></div> <div><div>☐ CH8:CH13-800E</div><div>10/13/2026</div></div> <div><div>☐ 700E:CH8-1300N</div><div>10/13/2026</div></div> <div><div>☐ CH8:600E-500E</div><div>10/20/2026</div></div> <div><div>☐ CH8:500E-400E</div><div>10/20/2026</div></div> <div><div>☐ CH8:400E-CH16</div><div>10/20/2026</div></div> <div><div>☐ CH8:CH16-400E</div><div>10/30/2026</div></div>	<div><div>☐ CH13:900N-1000N</div><div>11/2/2026</div></div> <div><div>☐ CH13:1000N-1100N</div><div>11/2/2026</div></div> <div><div>☐ CH13:1100N-CH8</div><div>11/2/2026</div></div> <div><div>☐ CH8:CH13-600E</div><div>11/2/2026</div></div> <div><div>☐ CH8:CH13-800E</div><div>11/2/2026</div></div> <div><div>☐ 700E:CH8-1300N</div><div>11/2/2026</div></div> <div><div>☐ CH8:600E-500E</div><div>11/2/2026</div></div> <div><div>☐ CH8:CH16-400E</div><div>11/2/2026</div></div>	<div><div>☐ CH13:900N-1000N</div><div>11/2/2026</div></div> <div><div>☐ CH13:1000N-1100N</div><div>11/2/2026</div></div> <div><div>☐ CH13:1100N-CH8</div><div>11/2/2026</div></div> <div><div>☐ CH8:CH13-600E</div><div>11/2/2026</div></div> <div><div>☐ CH8:CH13-800E</div><div>11/2/2026</div></div> <div><div>☐ 700E:CH8-1300N</div><div>11/2/2026</div></div> <div><div>☐ CH8:600E-500E</div><div>11/2/2026</div></div> <div><div>☐ CH8:CH16-400E</div><div>11/2/2026</div></div>						
	Short Duration Road Closures			<div><div>☒ 1000N:00E-100E</div><div>10/30/2026</div></div> <div><div>☒ 1300N:500E-600E</div><div>10/30/2026</div></div>								
	Public Road Improvements	Box Culvert			0.0	1.0	EA	15.0	6.7%			
		Pipe Culvert			0.0	106.0	EA	222.0	27.7%			
		Aggregate Widening		Trenching	0.0					Trenching		Trenching
				Aggregate Install-Trench Fill	0.0	23.0	Mi	75.0	30.7%	Aggregate Install-Trench Fill	Aggregate Install-Trench Fill	Aggregate Install-Trench Fill
		Prof. Adj.			0.0	12.0	EA					
		Pulverization			0.0	23.5	Mi	75.0	31.3%			
		Stabilization			0.0	23.5	Mi	75.0	31.3%			
		Agg Surface			0.0	23.5	Mi	75.0	31.3%			
		Oil and Chip			0.0	23.5	Mi	75.0	31.3%			
		Earthwork			0.0	23.5	Mi	75.0	31.3%	S CH8:CH16-400E Patch		
		Seeding		F CH8:500E-600E	1.0	19.5	Mi	75.0	26.0%		S CH8:600E-CH13 S CH13:900N-1000N S CH13:1000N-1100N S CH13:1100N-CH8	
		Punchlist			0.0	23.5	Mi	75.0	31.3%			
	HMA			0.0	7.0	EA	17.0	41.2%		CH 8 Patches		
	Site	Crane Pad			0.0	9.0	EA	109.0	8.3%			
		Access Road			0.0	38.0	EA	109.0	34.9%			

Panther Grove 2 Road Closure Map

10/31/2026

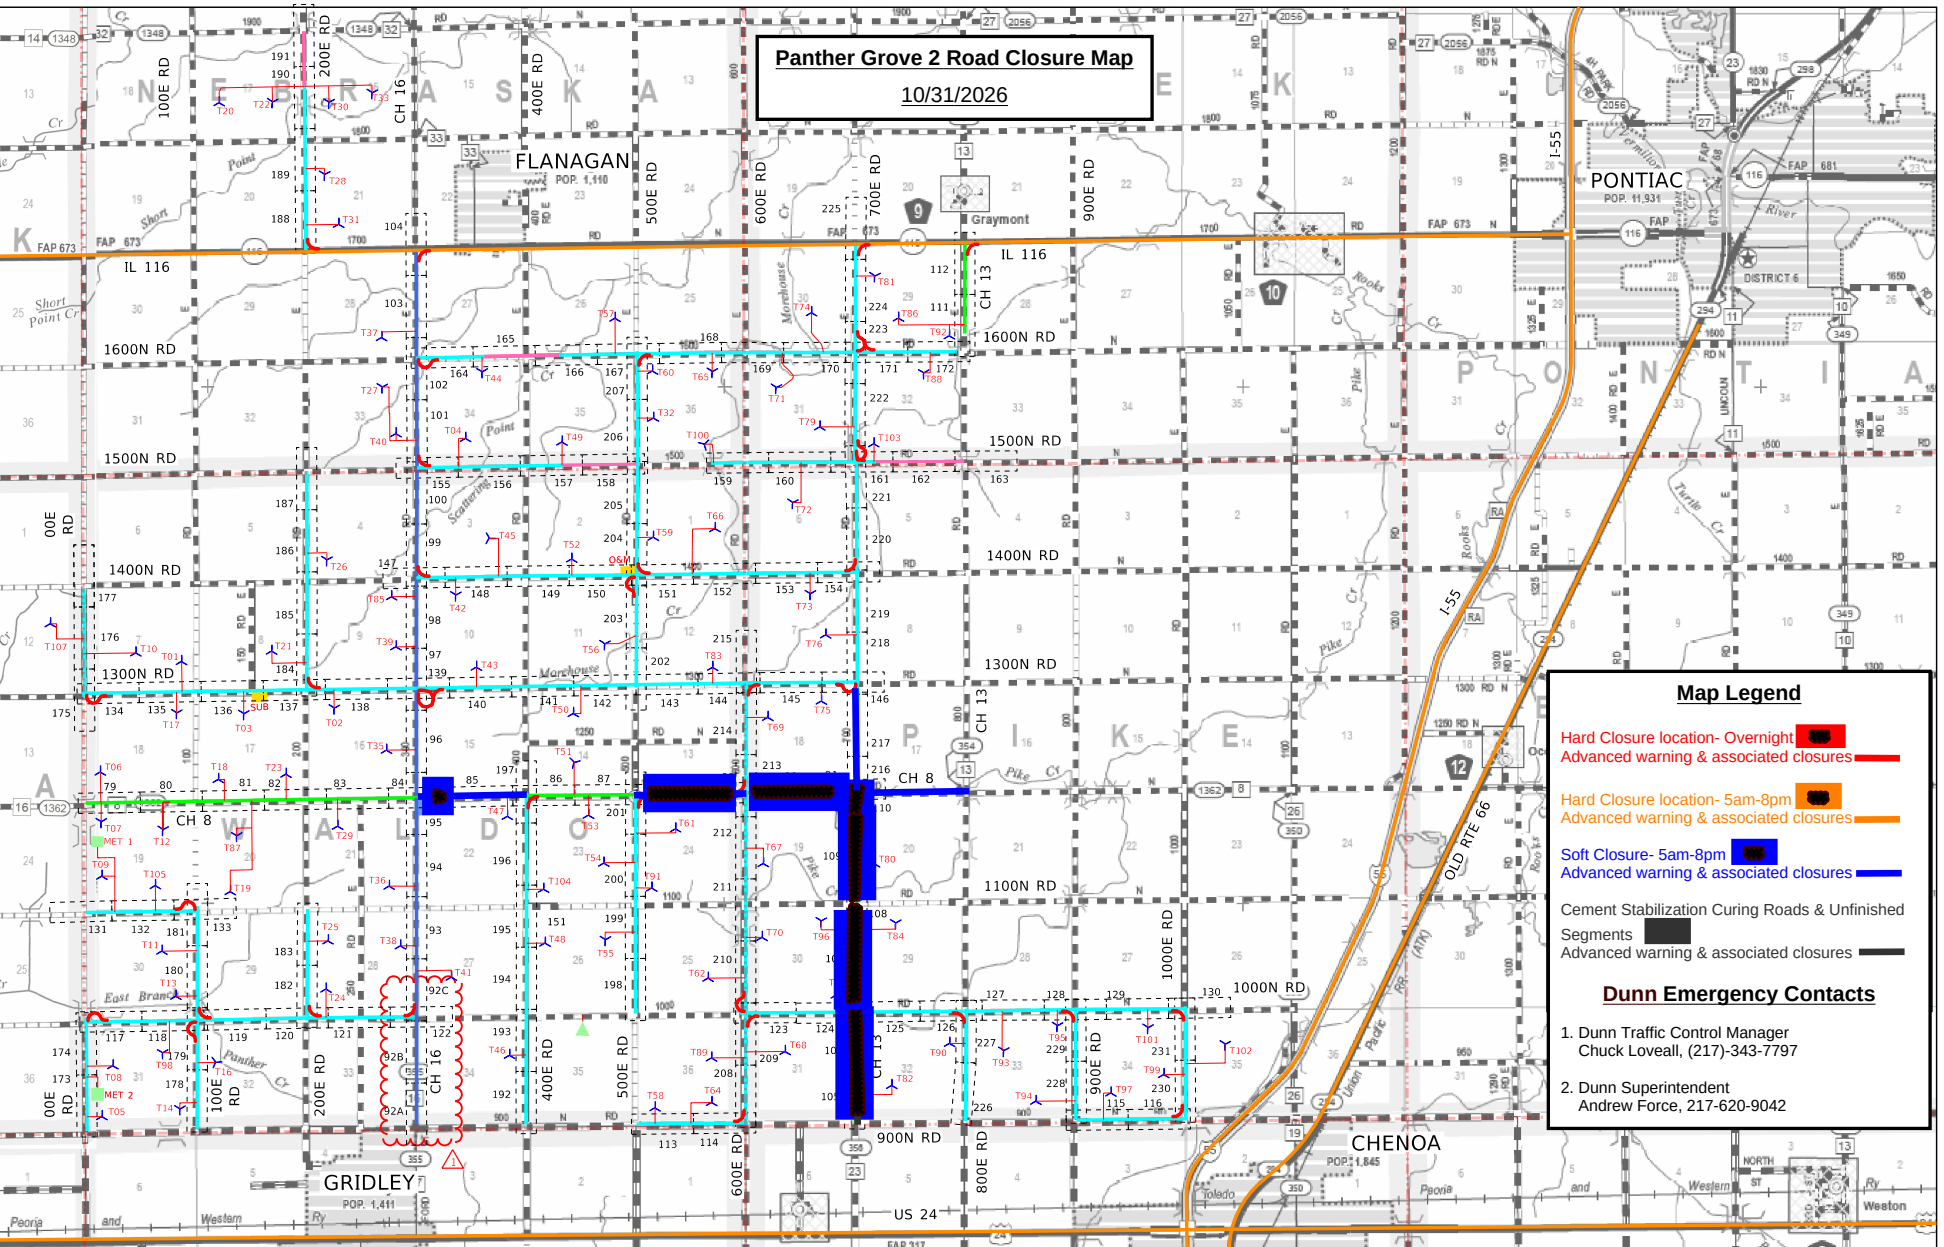


Map Legend

- Hard Closure location- Overnight 
Advanced warning & associated closures 
- Hard Closure location- 5am-8pm 
Advanced warning & associated closures 
- Soft Closure- 5am-8pm 
Advanced warning & associated closures 
- Cement Stabilization Curing Roads & Unfinished Segments 
Advanced warning & associated closures 

Dunn Emergency Contacts

1. Dunn Traffic Control Manager
Chuck Loveall, (217)-343-7797
2. Dunn Superintendent
Andrew Force, 217-620-9042

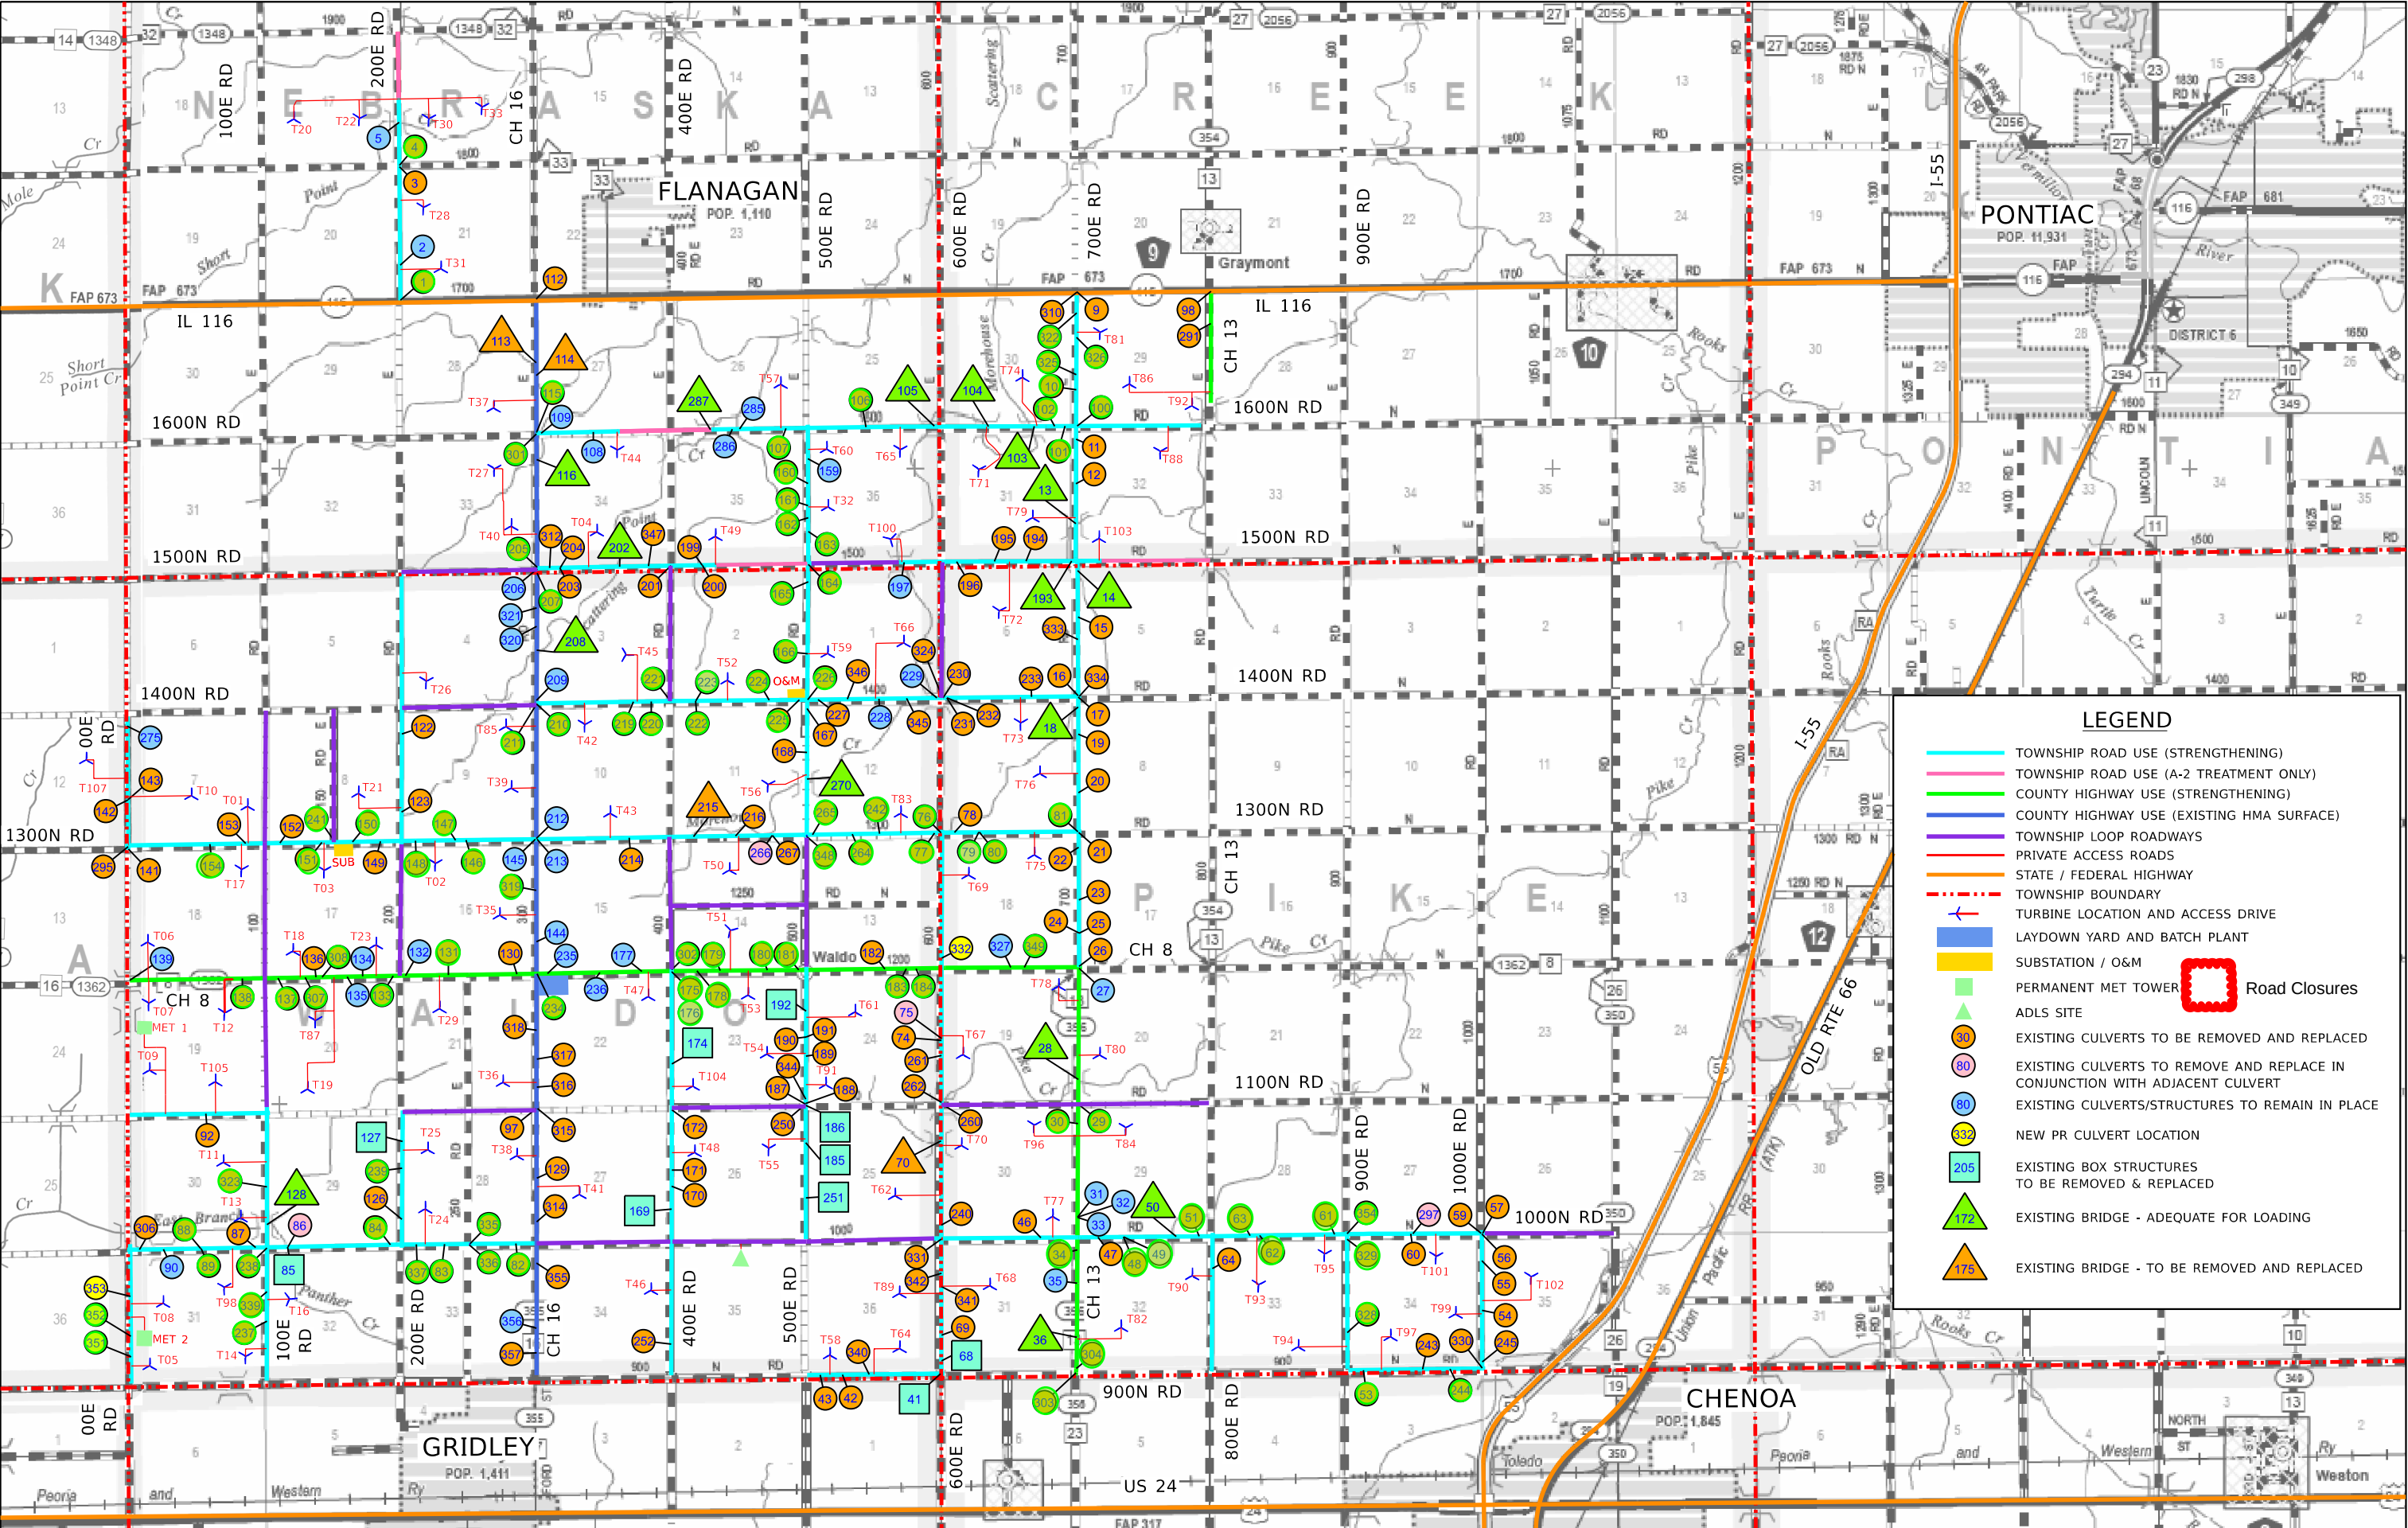

LEGEND

TOWNSHIP ROAD USE (STRENGTHENING)

TOWNSHIP ROAD USE (A-2 TREATMENT ONLY)

COUNTY HIGHWAY USE (STRENGTHENING)

COUNTY HIGHWAY USE (EXISTING HMA SURFACE)

TOWNSHIP LOOP ROADWAYS

PRIVATE ACCESS ROADS

STATE / FEDERAL HIGHWAY

TOWNSHIP BOUNDARY

TURBINE LOCATION AND ACCESS DRIVE

LAYDOWN YARD AND BATCH PLANT

SUBSTATION / O&M

PERMANENT MET TOWER

ADLS SITE

EXISTING CULVERTS TO BE REMOVED AND REPLACED

EXISTING CULVERTS TO REMOVE AND REPLACE IN CONJUNCTION WITH ADJACENT CULVERT

EXISTING CULVERTS/STRUCTURES TO REMAIN IN PLACE

NEW PR CULVERT LOCATION

EXISTING BOX STRUCTURES TO BE REMOVED & REPLACED

EXISTING BRIDGE - ADEQUATE FOR LOADING

EXISTING BRIDGE - TO BE REMOVED AND REPLACED

Road Closures

1	4/10/2026	REV 1	DESIGNED - JDA
00	2/20/2026	IFC SUBMITTAL	DRAWN - DRR/LNS
REV	DATE	DESCRIPTION	CHECKED - ML
			DATE - 04/14/2026

PANTHER GROVE 2 WIND PROJECT
LIVINGSTON COUNTY, ILLINOIS

EXHIBIT A - PROJECT LAYOUT MAP (REVISION 1)

SCALE: N.T.S. SHEET 1 OF 1 SHEETS STA. TO STA.

Farnsworth GROUP

100 WALNUT ST #200
PEORIA, ILLINOIS 61602
(309) 689-9888 / info@f-w.com

TOTAL SHEETS	SHEET NO.	REVISION NO.
