

Panther Grove 2

	10-Aug-26	Today
Daily Weather as of 7:00am	0	0
Low Temperature (F)	88	82
High Temperature (F)	71	68
Ground Wind Speed (MPH):	9 MPH	11 MPH
Precipitation (in)	0.00	43%
August Precip Total (in)	1.60	

	ACTIVITY
Public Roads	Strip Public Road Radii
	Mowing Public Road Radii
	Stone Public Road Radii
Access Roads	Strip Access Road
	Cement Stabilization
	Stone Access Road
	Strip Access Road Radii
	Stone Access Road Radii

LAST WORKING DAY
Monday, August 10, 2026
LOCATION(S)
P29 (1000N RD- CH 16)(C)
T51, T53, T78, T80
P17 (1300N RD- CH 16)(C)☐
T23, T29, T47
T07, T12, T87, T19
T51, T53(C), T78(C), T80(C)
T51, T53(C), T78(C)

Daily Safety Topics
LOTO- Reminder See a lock or tag → STOP. Do not operate or remove it.
Housekeeping- Keep working area clean weather its cabs, platforms, or ladders clean and free of trip hazards. Weather its trash, bolts, or any material clean as you go when possible or designate a time frame to do a pass on housekeeping.
Site Notes

Tuesday, August 11, 2026

TODAY
Tuesday, August 11, 2026
LOCATION(S)
P29 (1000N RD- CH 16)
T53, T78, T80, T96
P17 (1300N RD- CH 16) P29 (1000N RD- CH 16)
T51, T53
T29, T23, T47
T53, T78, T80, T96, T84
T53, T78, T80, T96, T84


NEXT WORKING DAY
Wednesday, August 12, 2026
LOCATION(S)
P29 (1000N RD- CH 16)
P17 (1300N RD- CH 16) P29 (1000N RD- CH 16)
T53, T78, T80, T96, T84
T53, T78, T80, T96, T84



Quantity Tracking				
QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
	6	EA	35	17.1%
	4	EA	35	11.4%
	22217	LF	161120	13.8%
	18628.5	LF	161120	11.6%
	13436	LF	161120	8.3%
	21	EA	TBD	#VALUE!
	14	EA	TBD	#VALUE!

Site Information	
Manpower	
4	White Construction Management
14	White Construction Operators
12	White Construction Laborers
	White Construction Ironworkers
	White Construction Millwright
	White Construction Electrician
	Dunn Company
	West Wind
	Tobey's Construction & Cartage
	KVCC
30	Total
Equipment	
10	Pickup Trucks
2	Dozers
2	Rollers
2	Graders
2	Cargo Trailer
0	Cranes
1	Excavators
0	Forklift
3	Trailers
1	Sand Truck
2	Sheepfoot Roller
2	Reclaimer Stabilizer
2	Smooth Drum Roller
3	Water Trucks
2	Skid Steer
34	Total

Additional Comments

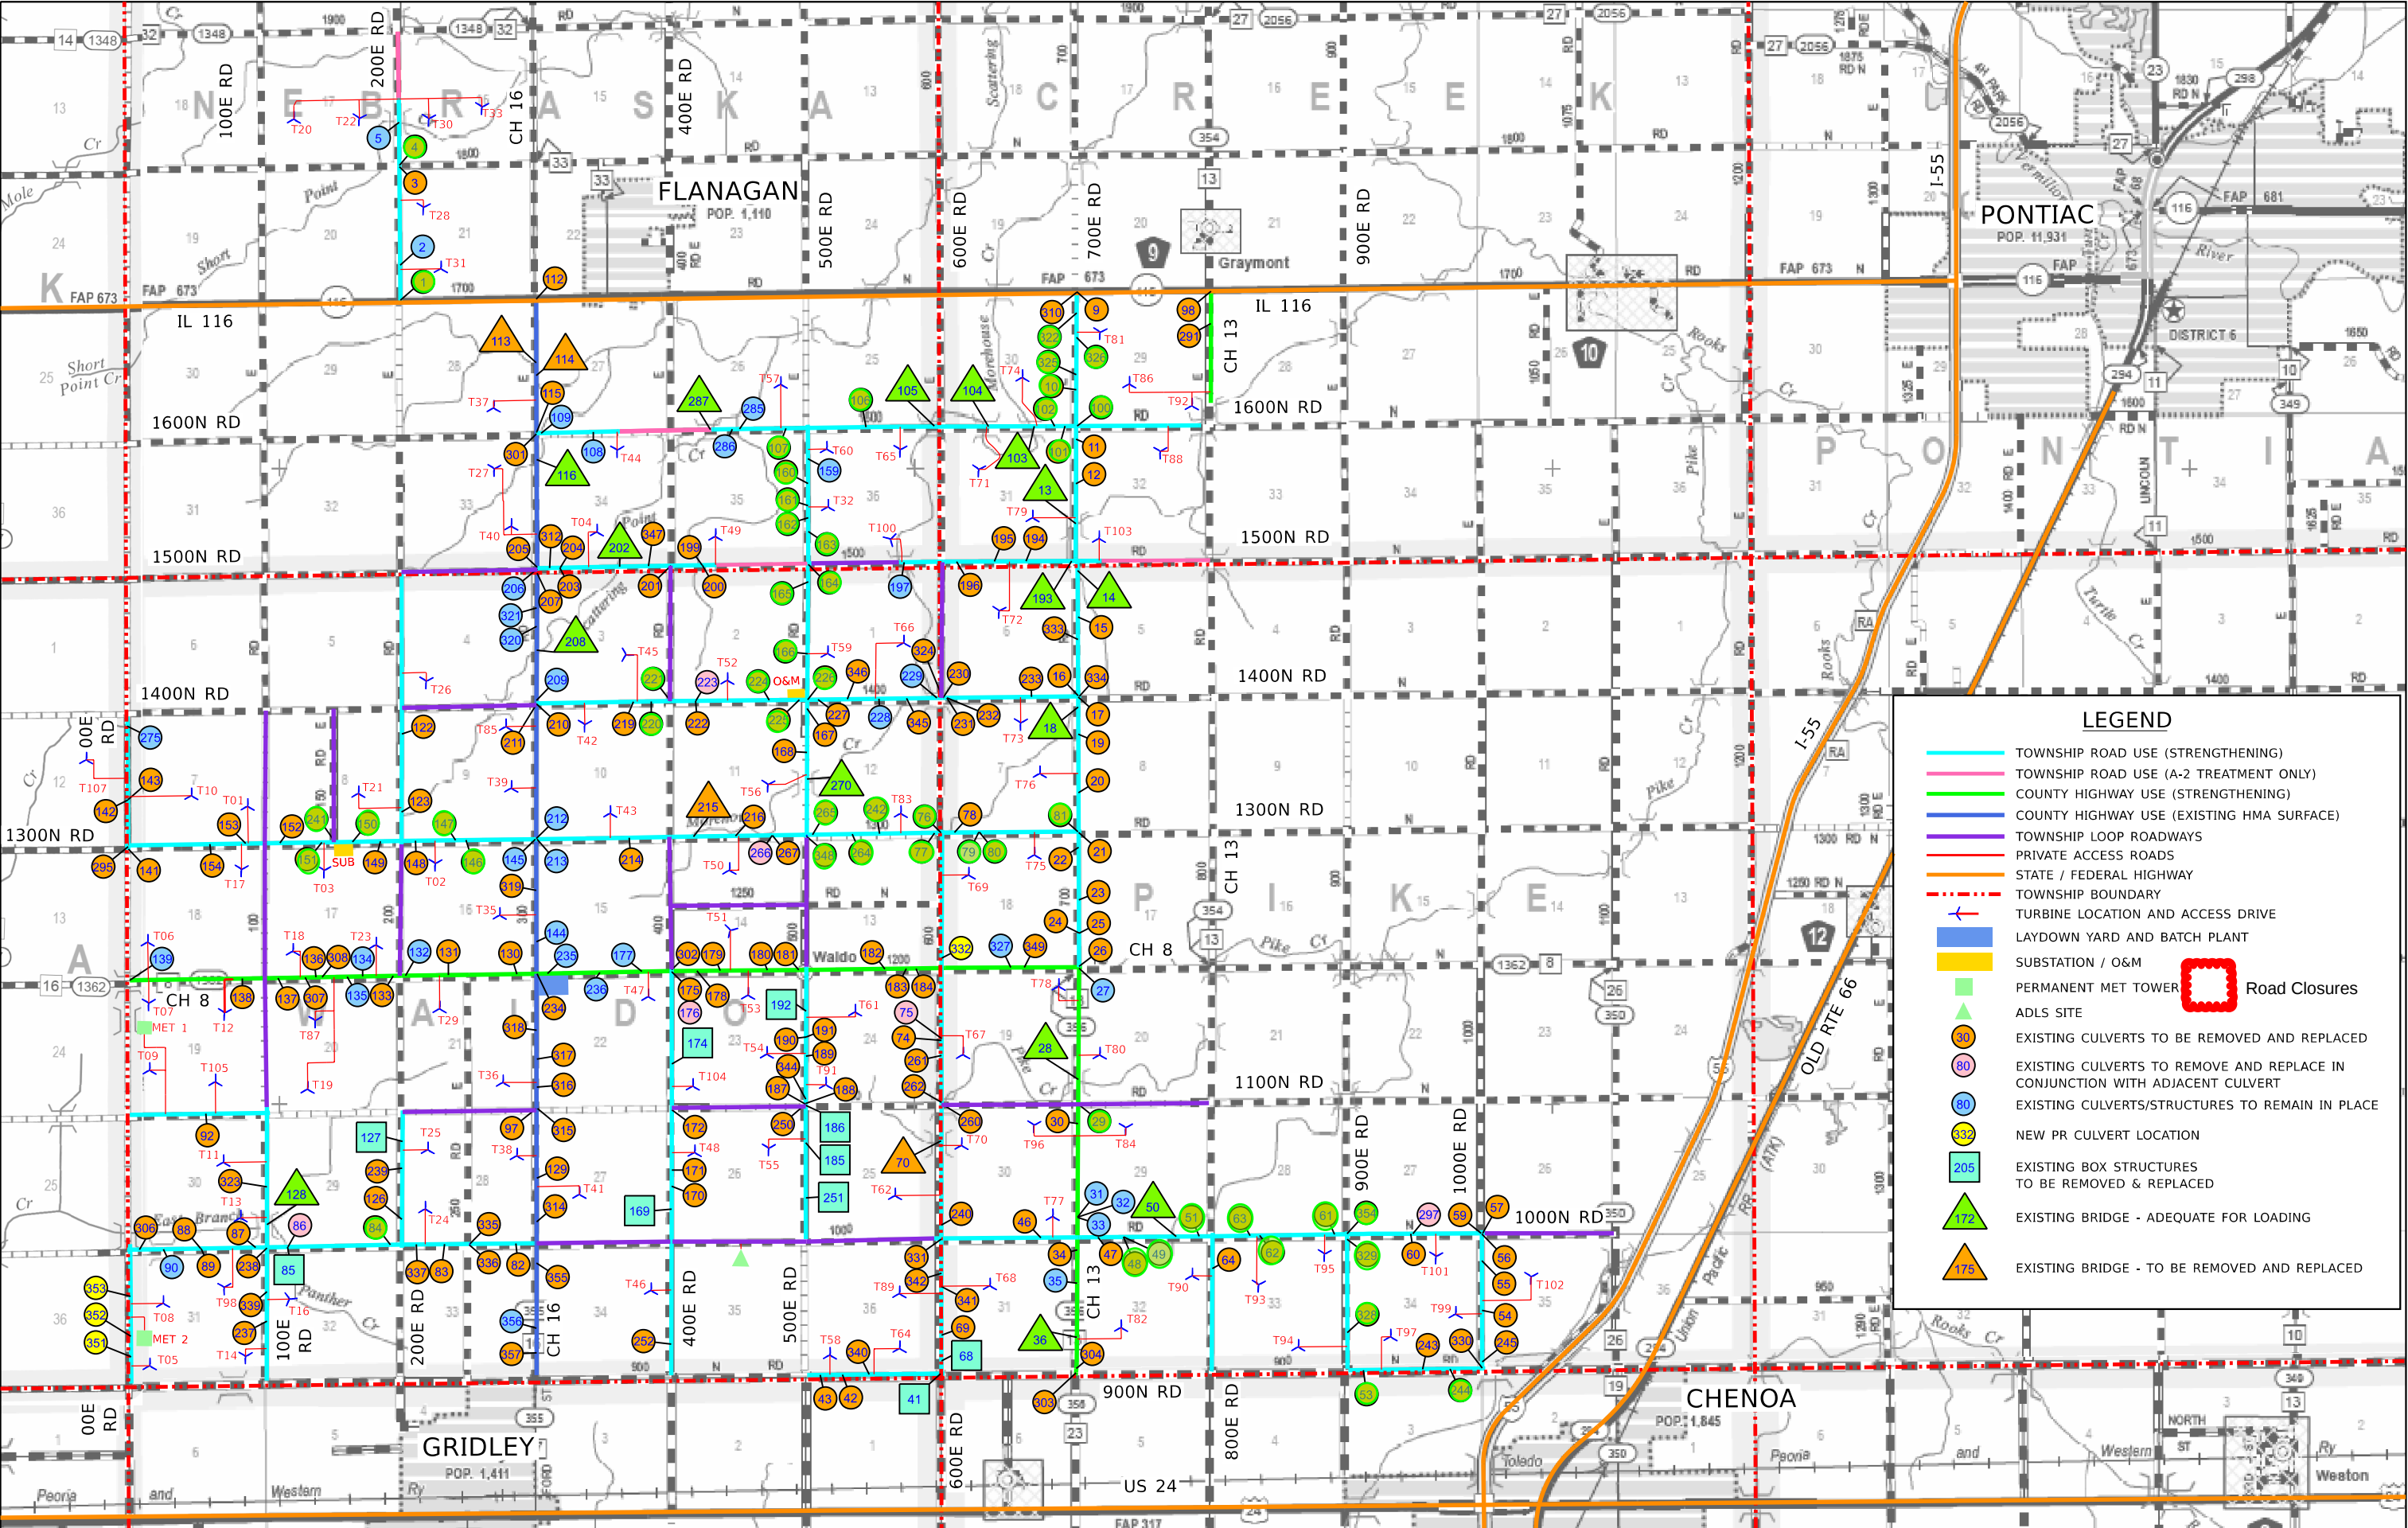

LEGEND

TOWNSHIP ROAD USE (STRENGTHENING)

TOWNSHIP ROAD USE (A-2 TREATMENT ONLY)

COUNTY HIGHWAY USE (STRENGTHENING)

COUNTY HIGHWAY USE (EXISTING HMA SURFACE)

TOWNSHIP LOOP ROADWAYS

PRIVATE ACCESS ROADS

STATE / FEDERAL HIGHWAY

TOWNSHIP BOUNDARY

TURBINE LOCATION AND ACCESS DRIVE

LAYDOWN YARD AND BATCH PLANT

SUBSTATION / O&M

PERMANENT MET TOWER

ADLS SITE

EXISTING CULVERTS TO BE REMOVED AND REPLACED

EXISTING CULVERTS TO REMOVE AND REPLACE IN CONJUNCTION WITH ADJACENT CULVERT

EXISTING CULVERTS/STRUCTURES TO REMAIN IN PLACE

NEW PR CULVERT LOCATION

EXISTING BOX STRUCTURES TO BE REMOVED & REPLACED

EXISTING BRIDGE - ADEQUATE FOR LOADING

EXISTING BRIDGE - TO BE REMOVED AND REPLACED

Road Closures

