

Panther Grove 2

	26-Oct-26	Today
Daily Weather as of 7:00am	Clear	Clear
Low Temperature (F)	47	52
High Temperature (F)	74	73
Ground Wind Speed (MPH):	7 mph	9 mph
Precipitation (in)	0.00	4%
October Precip Total (in)	1.50	

	ACTIVITY
Public Roads	Strip Public Road Radii
	Mowing Public Road Radii
	Stone Public Road Radii
Access Roads	Strip Access Road
	Cement Stabilization
	Stone Access Road
	Strip Access Road Radii
	Stone Access Road Radii

LAST WORKING DAY
Monday, October 26, 2026
LOCATION(S)
Public Road
P7 (1600N RD-500E RD)
T57, T65, T74
T45, T42
T39, T32, T52

Daily Safety Topics
Dewatering/ Excavation: If we have to dewater excavations let’s make sure we are following procedures. Excavation work requires Trench & Excavation permit and the UAP, if we are within 10 feet of a known utility. Let’s make sure we have all this complete before we start our work for the day. Rollover prevention: Operate on a stable surface, ensure proper loader operation, be mindful of the slopes that we are working on. Ensure that we are wearing our seat belts during operation.
Site Notes

Tuesday, October 27, 2026

TODAY
Tuesday, October 27, 2026
LOCATION(S)
Public Road
T42, T45
T81, T88, T71
T02, T03
T52, T45, T42

NEXT WORKING DAY
Wednesday, October 28, 2026
LOCATION(S)
Public Road
T02, T03
T52, T45, T42




Quantity Tracking				
QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
	11	EA	35	31.4%
	9	EA	35	25.7%
	62839.5	LF	161120	39.0%
	64274	LF	161120	39.9%
	52428.5	LF	161120	32.5%
	61	EA	TBD	#VALUE!
	57	EA	TBD	#VALUE!

Site Information	
Manpower	
18	White Construction Management
45	White Construction Operators
26	White Construction Laborers
16	White Construction Ironworkers
0	White Construction Millwright
3	White Construction Electrician
40	Dunn Company
8	West Wind
4	Tobey's Construction & Cartage
8	KVCC
6	Prairie Materials
5	JF Edwards
5	Keeley
184	Total
Equipment	
48	Pickup Trucks
3	Dozers
0	Rollers
1	Graders
1	Cargo Trailer
0	Cranes
3	Excavators
0	Forklift
13	Trailers
0	Sand Truck
1	Sheepfoot Roller
0	Reclaimer Stabilizer
1	Smooth Drum Roller
2	Water Trucks
5	Skid Steer
78	Total

Additional Comments

10/26/2026

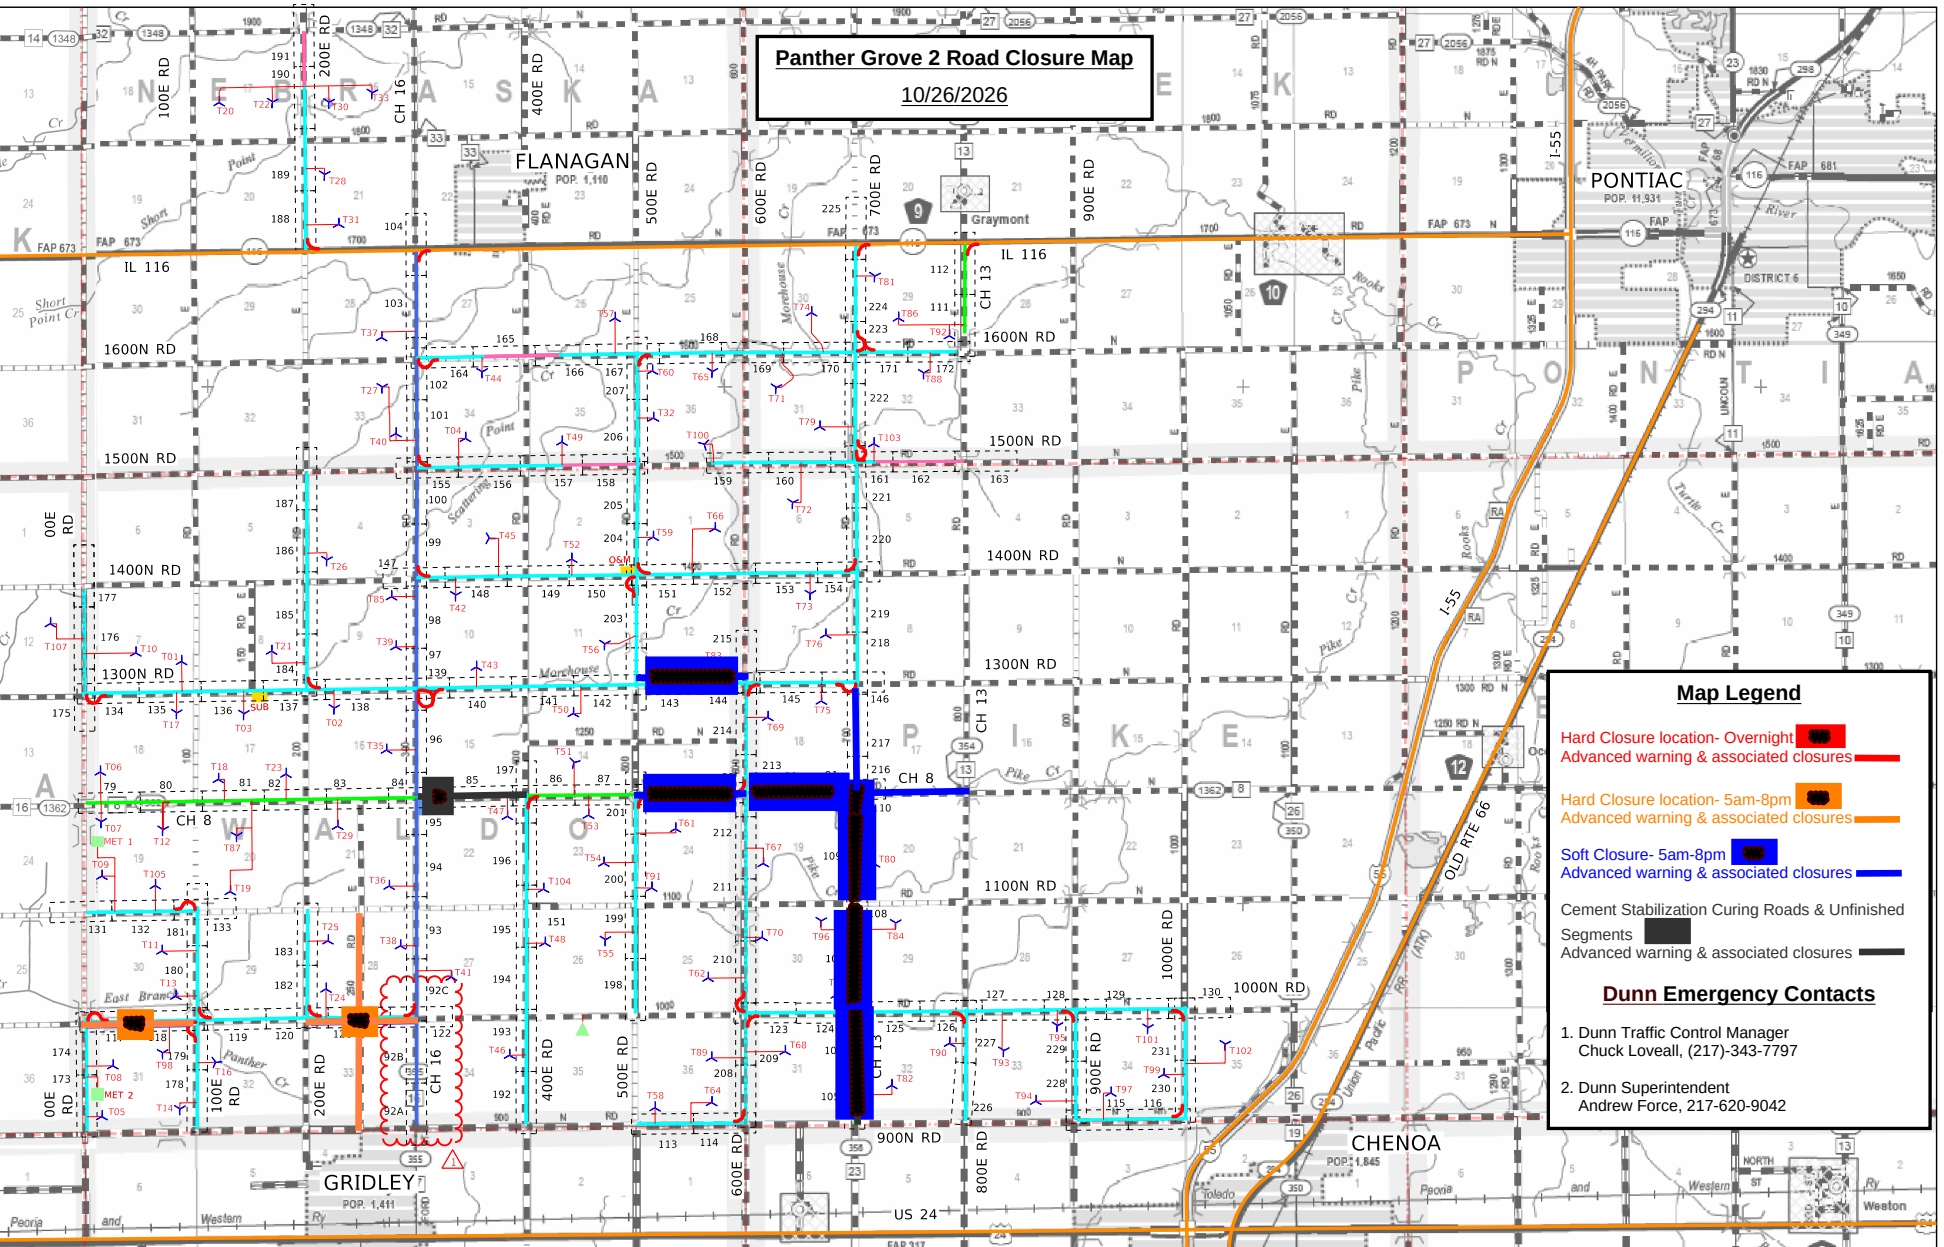[illegible]

1. **Introduction**
 2. **Background**
 3. **Methodology**
 4. **Results**
 5. **Conclusion**
 6. **References**


Soft Closure: 5am 9pm 

Cement Stabilization Curing Roads & Unfinished

Advanced warning & associated closures

1. Dunn Traffic Control Manager

-

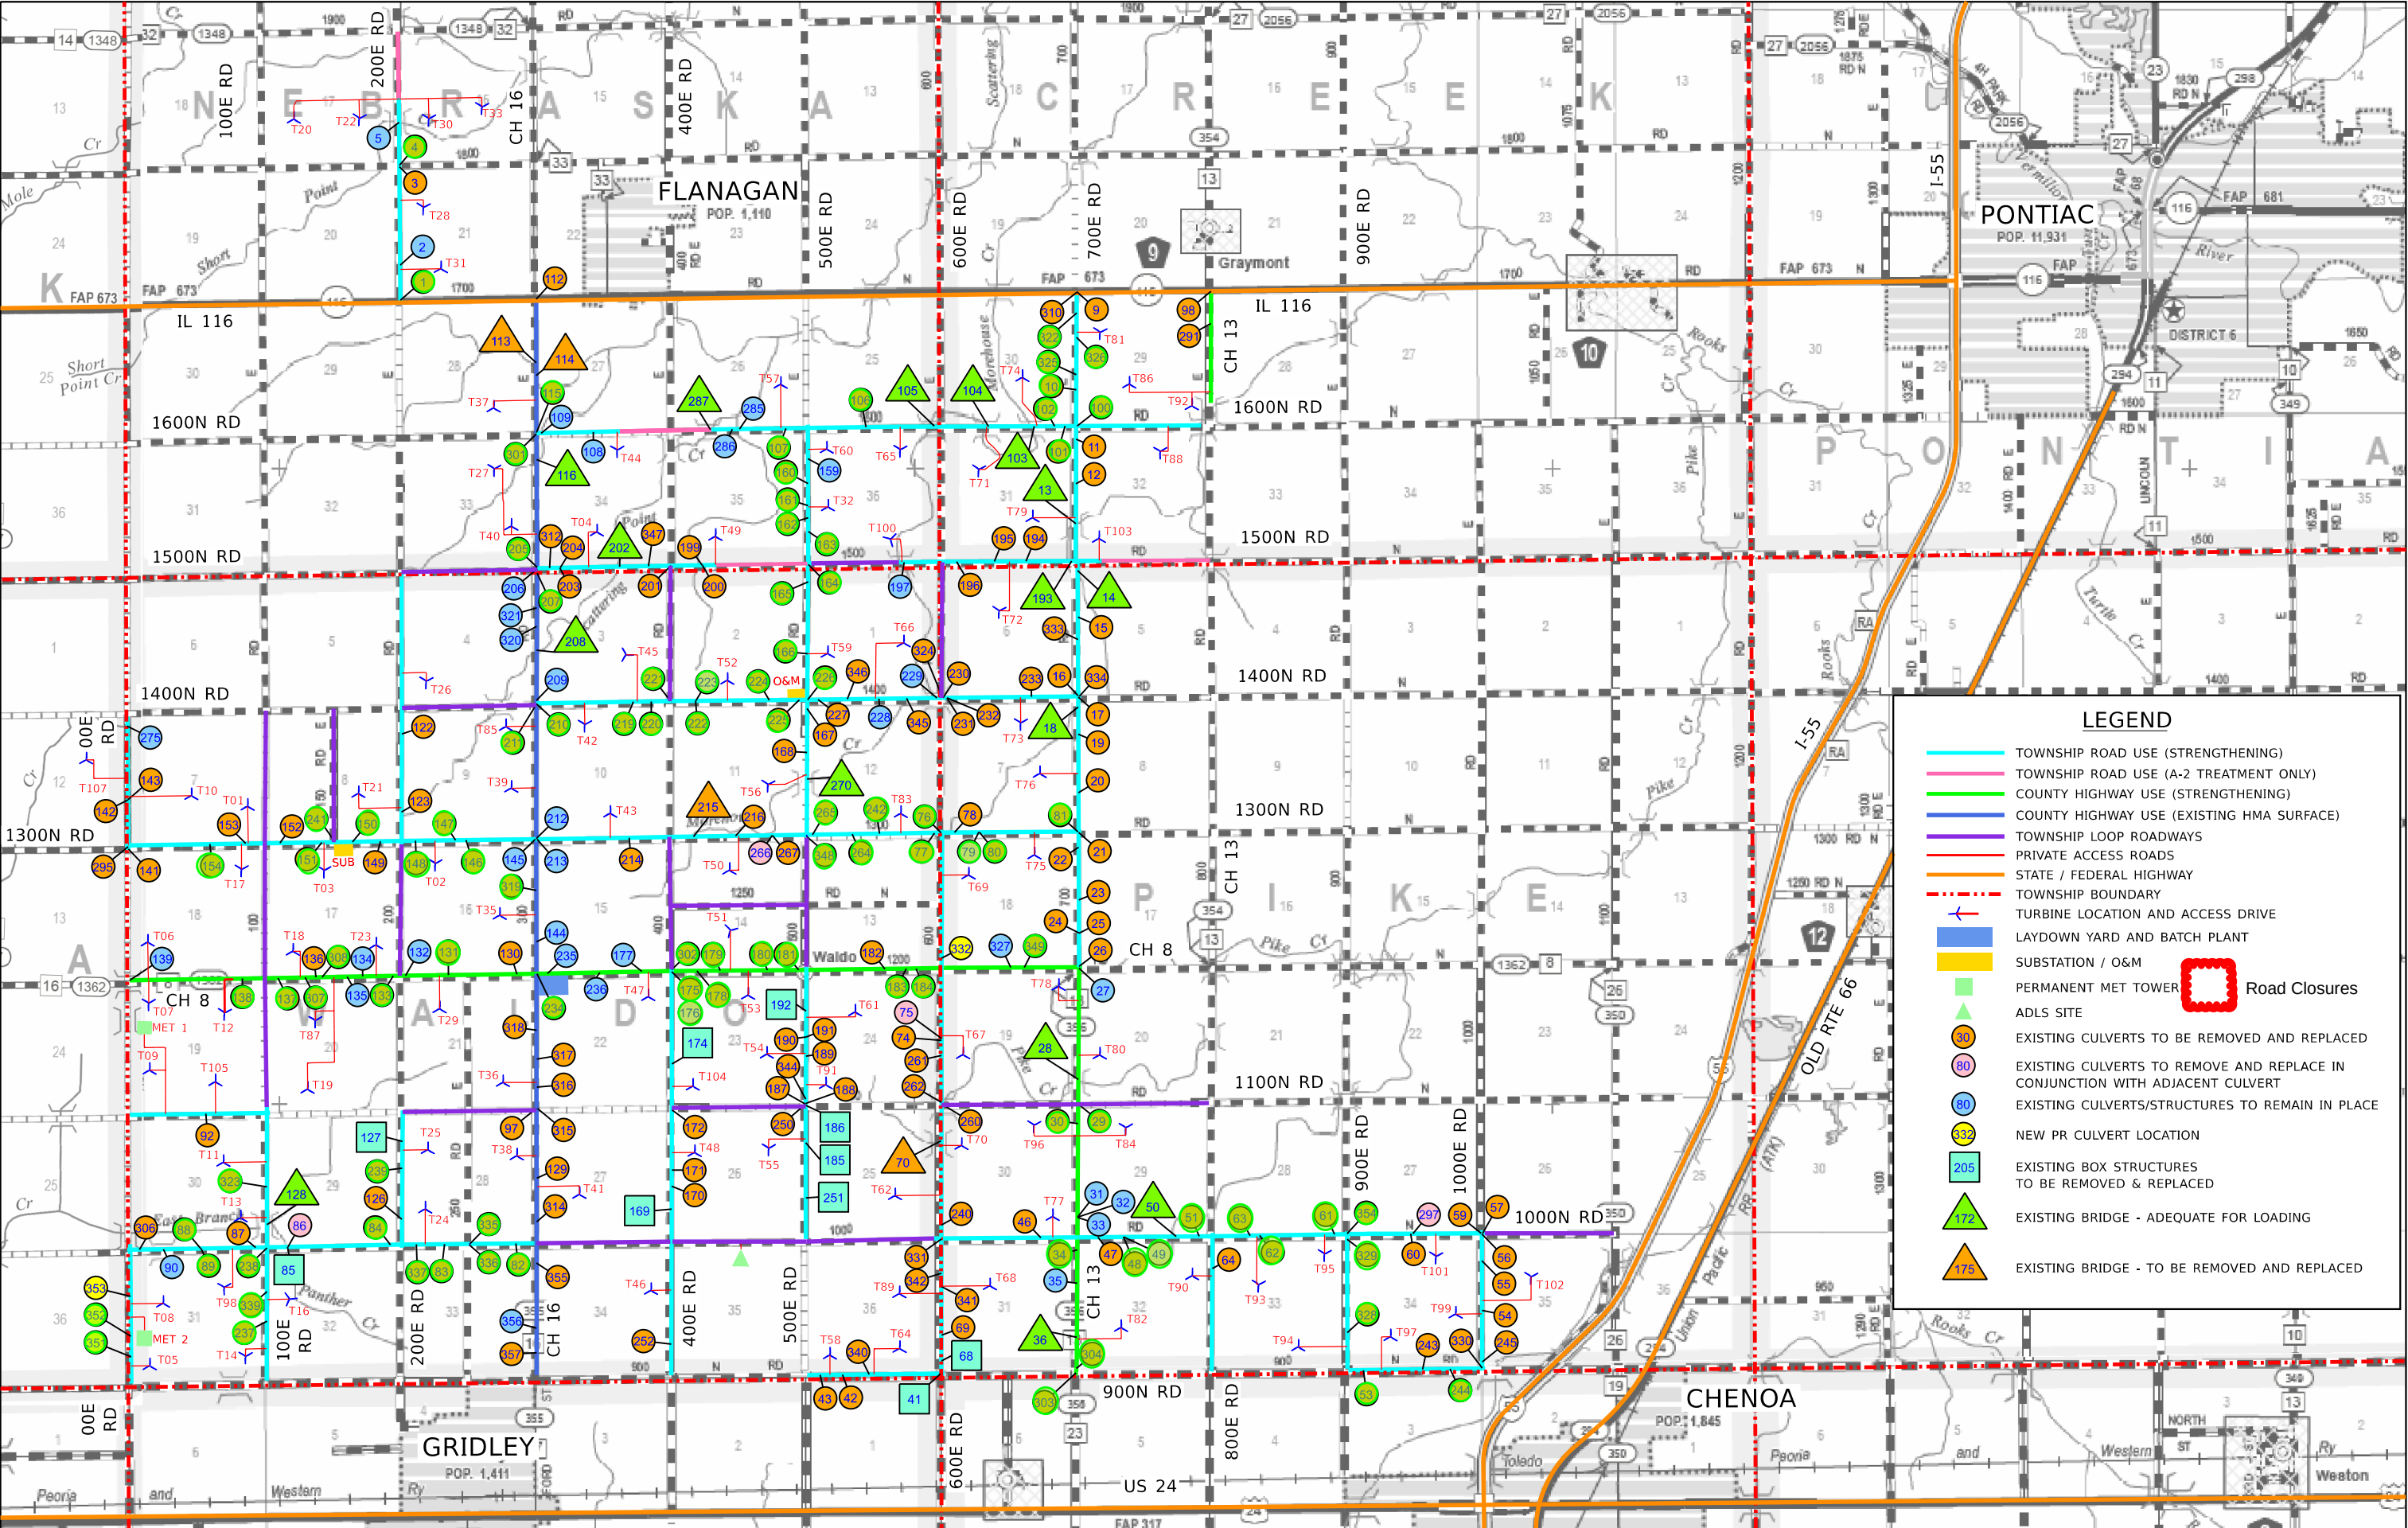

LEGEND

TOWNSHIP ROAD USE (STRENGTHENING)

TOWNSHIP ROAD USE (A-2 TREATMENT ONLY)

COUNTY HIGHWAY USE (STRENGTHENING)

COUNTY HIGHWAY USE (EXISTING HMA SURFACE)

TOWNSHIP LOOP ROADWAYS

PRIVATE ACCESS ROADS

STATE / FEDERAL HIGHWAY

TOWNSHIP BOUNDARY

TURBINE LOCATION AND ACCESS DRIVE

LAYDOWN YARD AND BATCH PLANT

SUBSTATION / O&M

PERMANENT MET TOWER

ADLS SITE

EXISTING CULVERTS TO BE REMOVED AND REPLACED

EXISTING CULVERTS TO REMOVE AND REPLACE IN CONJUNCTION WITH ADJACENT CULVERT

EXISTING CULVERTS/STRUCTURES TO REMAIN IN PLACE

NEW PR CULVERT LOCATION

EXISTING BOX STRUCTURES TO BE REMOVED & REPLACED

EXISTING BRIDGE - ADEQUATE FOR LOADING

EXISTING BRIDGE - TO BE REMOVED AND REPLACED

Road Closures
