



## Panther Grove 2

|                            | 20-Jul-26 | Today |
|----------------------------|-----------|-------|
| Daily Weather as of 7:00am | #N/A      | #N/A  |
| Low Temperature (F)        | 59        | 58    |
| High Temperature (F)       | 74        | 74    |
| Ground Wind Speed (MPH):   | 15 MPH    | 14    |
| Precipitation (in)         | 0.00      | 20%   |
| June Precip Total (in)     | 4.30      |       |

|              | ACTIVITY                      | LOCATION(S)                                                                                                                                                                                                                                                                     |
|--------------|-------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Public Roads | Road Closures (Curing Roads)  | 600E:1500N-1600N (Cure day 4)<br>600E:IL116-1600N (Cure day 4)<br>1600N:500E-600E (Cure day 4)<br>1600N:700E-800E (Cure day 4)                                                                                                                                                  |
|              | Road Closures (Pipe Culverts) | 1300N:400E-500E (245,348)<br>1300N:500E-600E (348)<br>600E:1300N-1400N (348)<br>600E:Ch8-1300N (348)                                                                                                                                                                            |
|              | Road Closures (Roadwork)      | 200E:1800N-1900N (Agg Cap/Earth Shoulders)<br>1800N:100E-200E (Agg Cap/Earth Shoulders)<br>1800N:200E-300E (Agg Cap/Earth Shoulders)<br>200E:1800N-IL116 (Agg Cap/Earth Shoulders)<br>1600N:400E-CH16 (Agg Cap/Earth Shoulders)<br><br>1600N:400E-500E (widening/pulverization) |
|              | Culvert Work                  | 265,348                                                                                                                                                                                                                                                                         |
|              | Road Pulverization            | No work available                                                                                                                                                                                                                                                               |
|              | Cement Stabilization          | No work available                                                                                                                                                                                                                                                               |
|              | Agg Surface Install           | 200E:1800N-1900N<br>1800N:100E-200E<br>1800N:200E-300E<br>200E:1800N-IL116<br><br>1600N:400E-CH16                                                                                                                                                                               |
|              | Oil and Chip                  |                                                                                                                                                                                                                                                                                 |
|              | Earthen Shoulders             | 200E:1800N-1900N<br>1800N:100E-200E<br>1800N:200E-300E<br>200E:1800N-IL116                                                                                                                                                                                                      |

|  |                     |  |
|--|---------------------|--|
|  | Daily Safety Topics |  |
|  |                     |  |
|  |                     |  |
|  | Site Notes          |  |
|  |                     |  |


**Tuesday, July 21, 2026**

| TODAY                                                                                                                                                                                                                                                                                                                                       |  | NEXT WORKING DAY                                                                                                                                                                                                                                                                                                                                  |  |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--|
| Tuesday, July 21, 2026                                                                                                                                                                                                                                                                                                                      |  | Wednesday, July 22, 2026                                                                                                                                                                                                                                                                                                                          |  |
| LOCATION(S)                                                                                                                                                                                                                                                                                                                                 |  | LOCATION(S)                                                                                                                                                                                                                                                                                                                                       |  |
| 600E:1500N-1600N (Cure day 5)<br>600E:IL116-1600N (Cure day 5)<br>1600N:500E-600E (Cure day 5)<br>1600N:700E-800E (Cure day 5)                                                                                                                                                                                                              |  | 600E:1500N-1600N (Cure day 6)<br>600E:IL116-1600N (Cure day 6)<br>1600N:500E-600E (Cure day 6)<br>1600N:700E-800E (Cure day 6)                                                                                                                                                                                                                    |  |
| 900N:1000E-900E (244,243)                                                                                                                                                                                                                                                                                                                   |  | 900N:1000E-900E (53)<br>900E:1000N-900N (328)                                                                                                                                                                                                                                                                                                     |  |
| 200E:1800N-1900N (Agg Cap/Earth Shoulders)<br>1800N:100E-200E (Agg Cap/Earth Shoulders)<br>1800N:200E-300E (Agg Cap/Earth Shoulders)<br>200E:1800N-IL116 (Agg Cap/Earth Shoulders)<br><br>1600N:400E-CH16 (Agg Cap)<br><br>1600N:400E-500E (widening/pulverization)<br><br>1300N:500E-600E (Widening/Add Rock)<br>1300N:500E-600E (staging) |  | 200E:1800N-1900N (Earth Shoulders)<br>1800N:100E-200E (Earth Shoulders)<br>1800N:200E-300E (Earth Shoulders)<br>200E:1800N-IL116 (Earth Shoulders)<br><br>1600N:400E-CH16 (Agg Cap)<br><br>1300N:500E-600E (Add/RockPulverization)<br>1300N:600E-700E (Widening/Pulverization)<br>1300:400E-500E (Staging)<br><br>1600N:400E-500E (Stabilization) |  |
| 244,243                                                                                                                                                                                                                                                                                                                                     |  | 53,328                                                                                                                                                                                                                                                                                                                                            |  |
| 1600N:400E-500E                                                                                                                                                                                                                                                                                                                             |  | 1300N:500E-600E                                                                                                                                                                                                                                                                                                                                   |  |
| No work available                                                                                                                                                                                                                                                                                                                           |  | No work available                                                                                                                                                                                                                                                                                                                                 |  |
| 200E:1800N-1900N<br>1800N:100E-200E<br>1800N:200E-300E<br>200E:1800N-IL116<br><br>1300N:500E-600E (Add Rock)<br>1300N:500E-600E (staging)<br><br>1600N:400E-CH16 (Agg Cap)                                                                                                                                                                  |  | 1300N:500E-600E (Add Rock)<br>1300N:500E-600E (staging)                                                                                                                                                                                                                                                                                           |  |
| 200E:1800N-1900N<br>1800N:100E-200E<br>1800N:200E-300E<br>200E:1800N-IL116                                                                                                                                                                                                                                                                  |  | 200E:1800N-1900N<br>1800N:100E-200E<br>1800N:200E-300E<br>200E:1800N-IL116                                                                                                                                                                                                                                                                        |  |

[illegible][illegible]

### Additional Comments



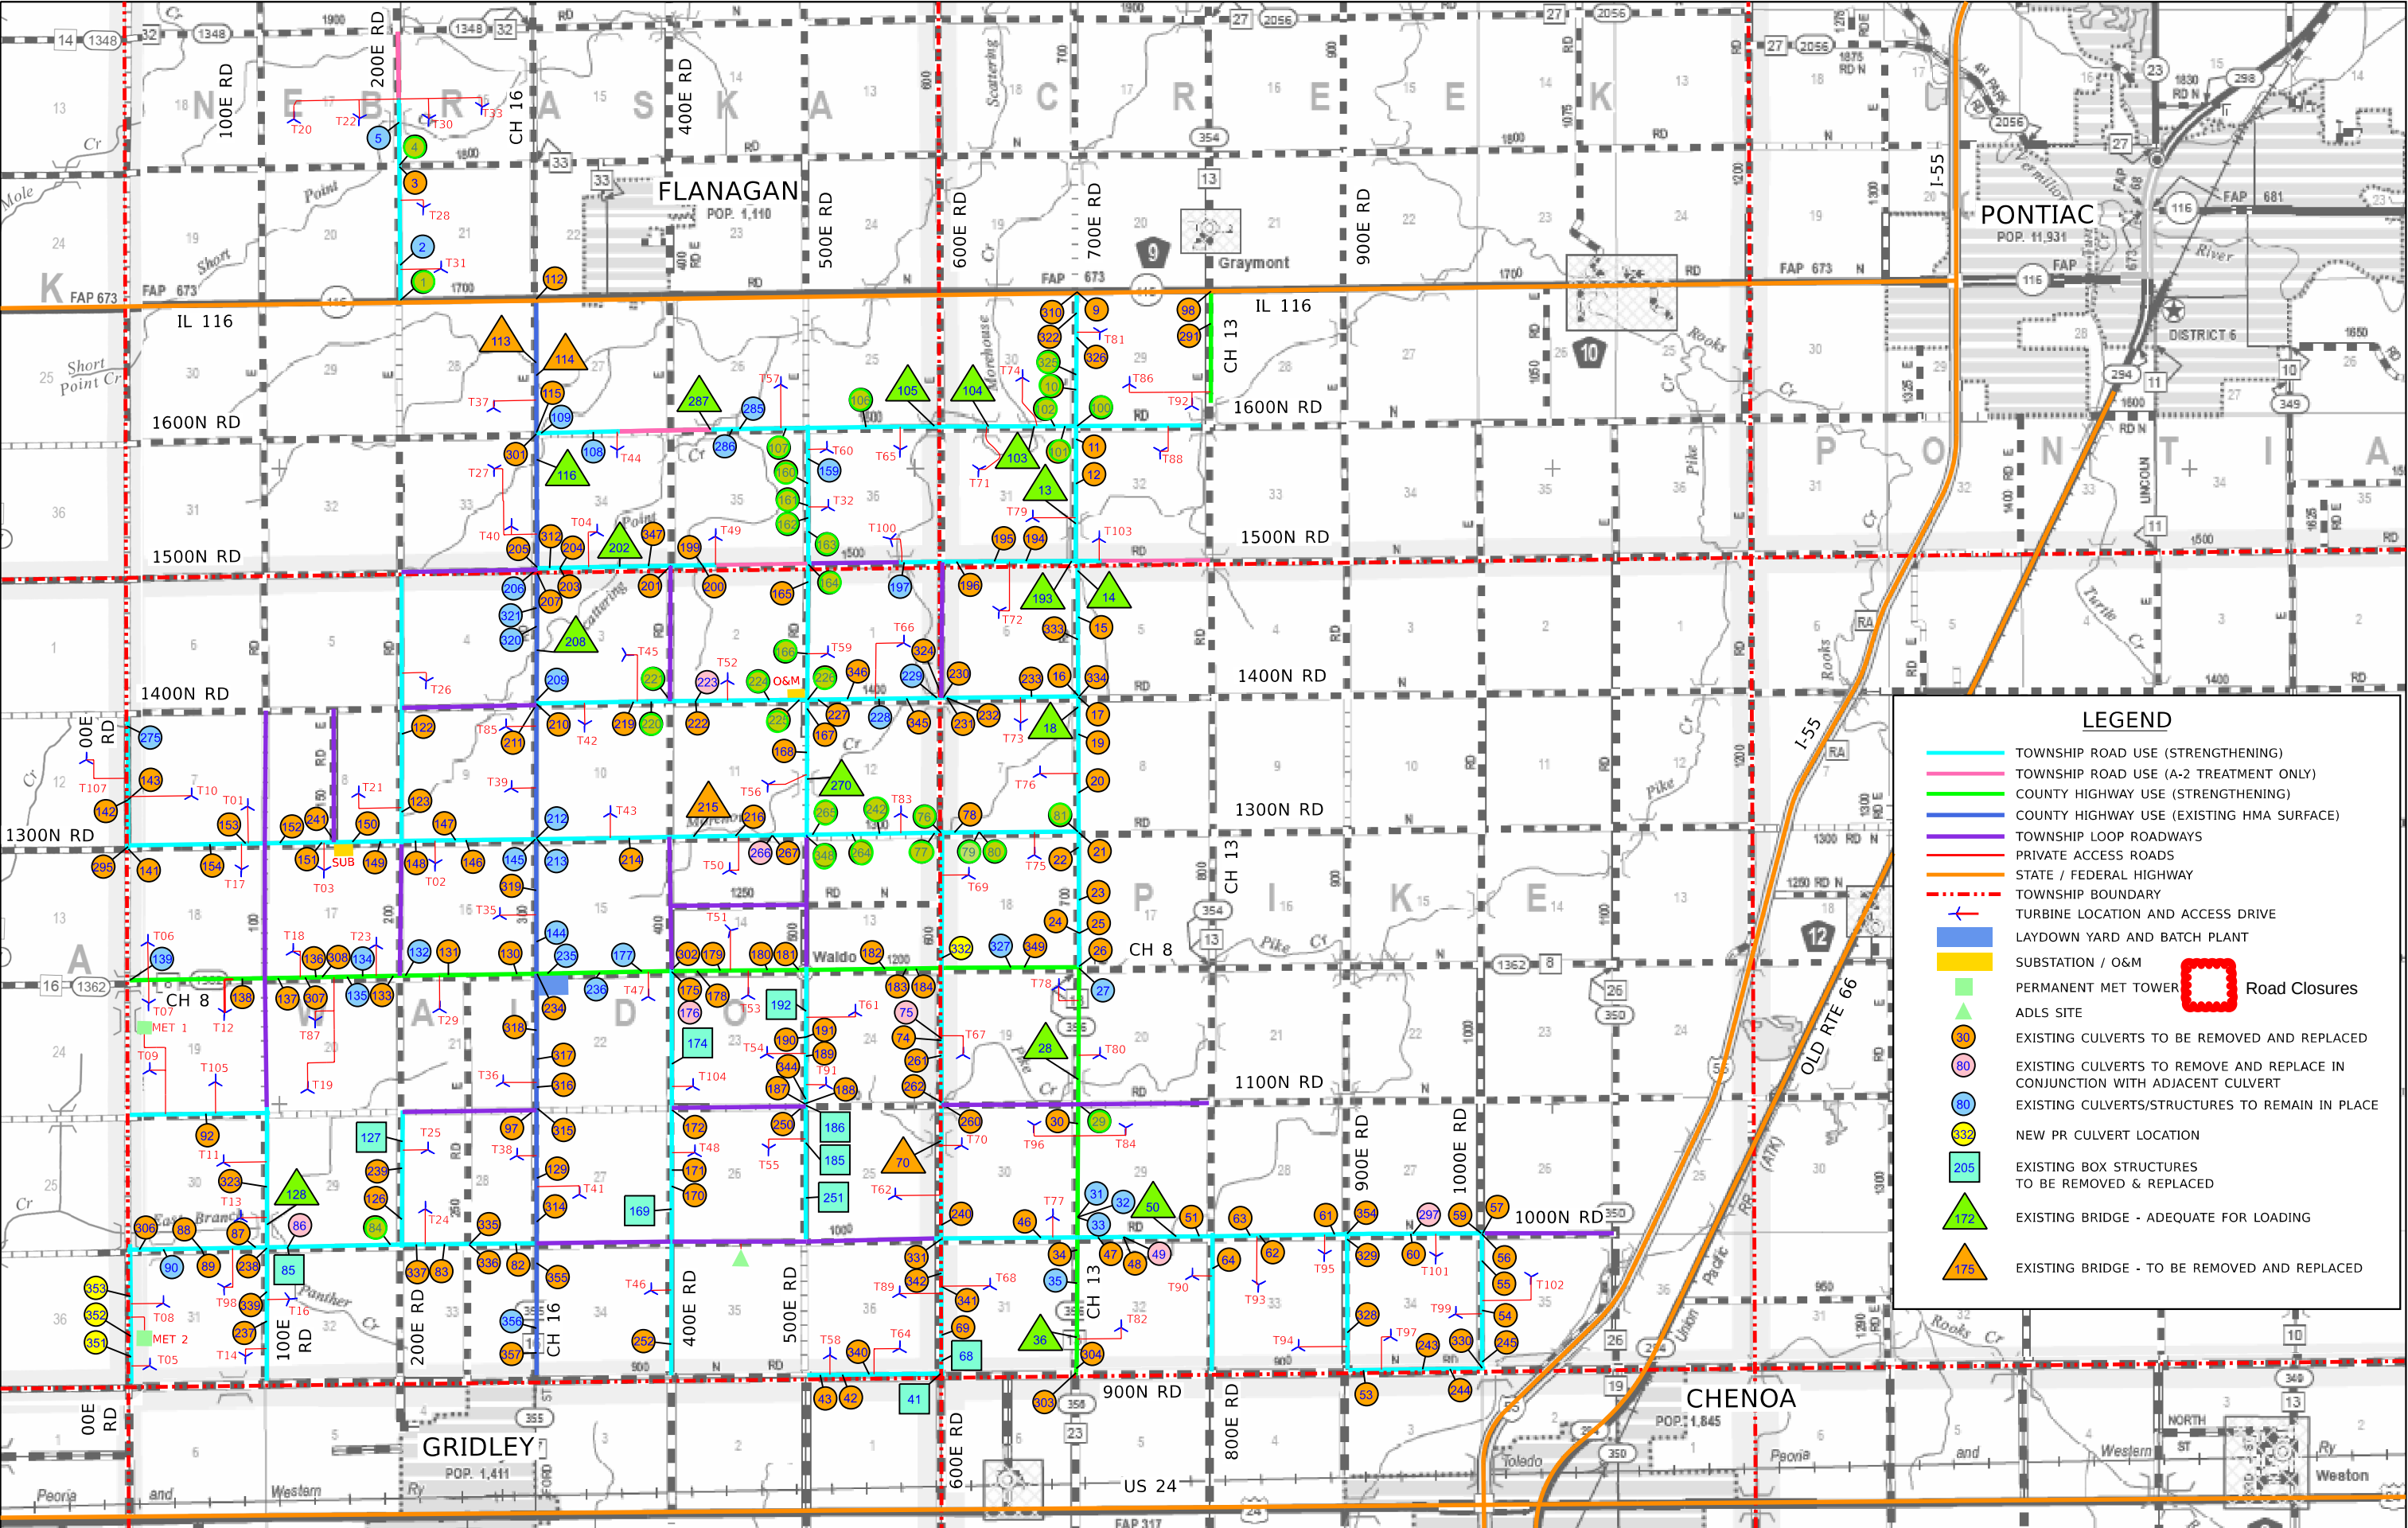

LEGEND

TOWNSHIP ROAD USE (STRENGTHENING)

TOWNSHIP ROAD USE (A-2 TREATMENT ONLY)

COUNTY HIGHWAY USE (STRENGTHENING)

COUNTY HIGHWAY USE (EXISTING HMA SURFACE)

TOWNSHIP LOOP ROADWAYS

PRIVATE ACCESS ROADS

STATE / FEDERAL HIGHWAY

TOWNSHIP BOUNDARY

TURBINE LOCATION AND ACCESS DRIVE

LAYDOWN YARD AND BATCH PLANT

SUBSTATION / O&M

PERMANENT MET TOWER

ADLS SITE

EXISTING CULVERTS TO BE REMOVED AND REPLACED

EXISTING CULVERTS TO REMOVE AND REPLACE IN CONJUNCTION WITH ADJACENT CULVERT

EXISTING CULVERTS/STRUCTURES TO REMAIN IN PLACE

NEW PR CULVERT LOCATION

EXISTING BOX STRUCTURES TO BE REMOVED & REPLACED

EXISTING BRIDGE - ADEQUATE FOR LOADING

EXISTING BRIDGE - TO BE REMOVED AND REPLACED

Road Closures

|     |           |               |
|-----|-----------|---------------|
| 1   | 4/10/2026 | REV 1         |
| 00  | 2/20/2026 | IFC SUBMITTAL |
| REV | DATE      | DESCRIPTION   |

|                   |
|-------------------|
| DESIGNED - JDA    |
| DRAWN - DRR/LNS   |
| CHECKED - ML      |
| DATE - 04/14/2026 |

PANTHER GROVE 2 WIND PROJECT  
LIVINGSTON COUNTY, ILLINOIS

EXHIBIT A - PROJECT LAYOUT MAP (REVISION 1)

SCALE: N.T.S. SHEET 1 OF 1 SHEETS STA. TO STA.

Farnsworth GROUP

100 WALNUT ST #200  
PEORIA, ILLINOIS 61602  
(309) 689-9888 / info@f-w.com

|              |           |              |
|--------------|-----------|--------------|
| TOTAL SHEETS | SHEET NO. | REVISION NO. |
|              |           |              |
