

Panther Grove 2

	29-Oct-26	Today
Daily Weather as of 7:00am	Clear	Clear
Low Temperature (F)	43	52
High Temperature (F)	72	65
Ground Wind Speed (MPH):	10mph	8 mph
Precipitation (in)	0.00	48%
October Precip Total (in)	1.50	

	ACTIVITY
Public Roads	Strip Public Road Radii
	Mowing Public Road Radii
	Stone Public Road Radii
Access Roads	Strip Access Road
	Cement Stabilization
	Stone Access Road
	Strip Access Road Radii
	Stone Access Road Radii

LAST WORKING DAY
Thursday, October 29, 2026
LOCATION(S)
Public Road
P3 (IL 116-700E RD) P2 (IL 116-CH 16)
T81
T03
T42, T02

Daily Safety Topics
Special thanks: Wanted to take the team to give everyone thanks and that the landowner are very pleased with housekeeping, keeping up with speed limits, and being considerate of them.
Traffic control- Reminder to continue to give heavy equipment, school busses, and harvesting equipment the right of way.
Site Notes

Friday, October 30, 2026

TODAY
Friday, October 30, 2026
LOCATION(S)
Public Road
P3 (IL 116-700E RD) P2 (IL 116-CH 16)
T88, T81
T03
T42, T02

NEXT WORKING DAY
Saturday, October 31, 2026
LOCATION(S)




Quantity Tracking				
QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
	11	EA	35	31.4%
	9	EA	35	25.7%
	66695	LF	161120	41.4%
	67827.5	LF	161120	42.1%
	53942.5	LF	161120	33.5%
	63	EA	TBD	#VALUE!
	58	EA	TBD	#VALUE!

Site Information	
Manpower	
19	White Construction Management
47	White Construction Operators
27	White Construction Laborers
16	White Construction Ironworkers
0	White Construction Millwright
3	White Construction Electrician
40	Dunn Company
8	West Wind
4	Tobey's Construction & Cartage
8	KVCC
6	Prairie Materials
19	JF Edwards
5	Keeley
202	Total
Equipment	
48	Pickup Trucks
3	Dozers
0	Rollers
1	Graders
1	Cargo Trailer
0	Cranes
3	Excavators
0	Forklift
13	Trailers
0	Sand Truck
1	Sheepfoot Roller
0	Reclaimer Stabilizer
1	Smooth Drum Roller
2	Water Trucks
5	Skid Steer
78	Total

Additional Comments

Panther Grove 2 Road Closure Map

10/30/2026

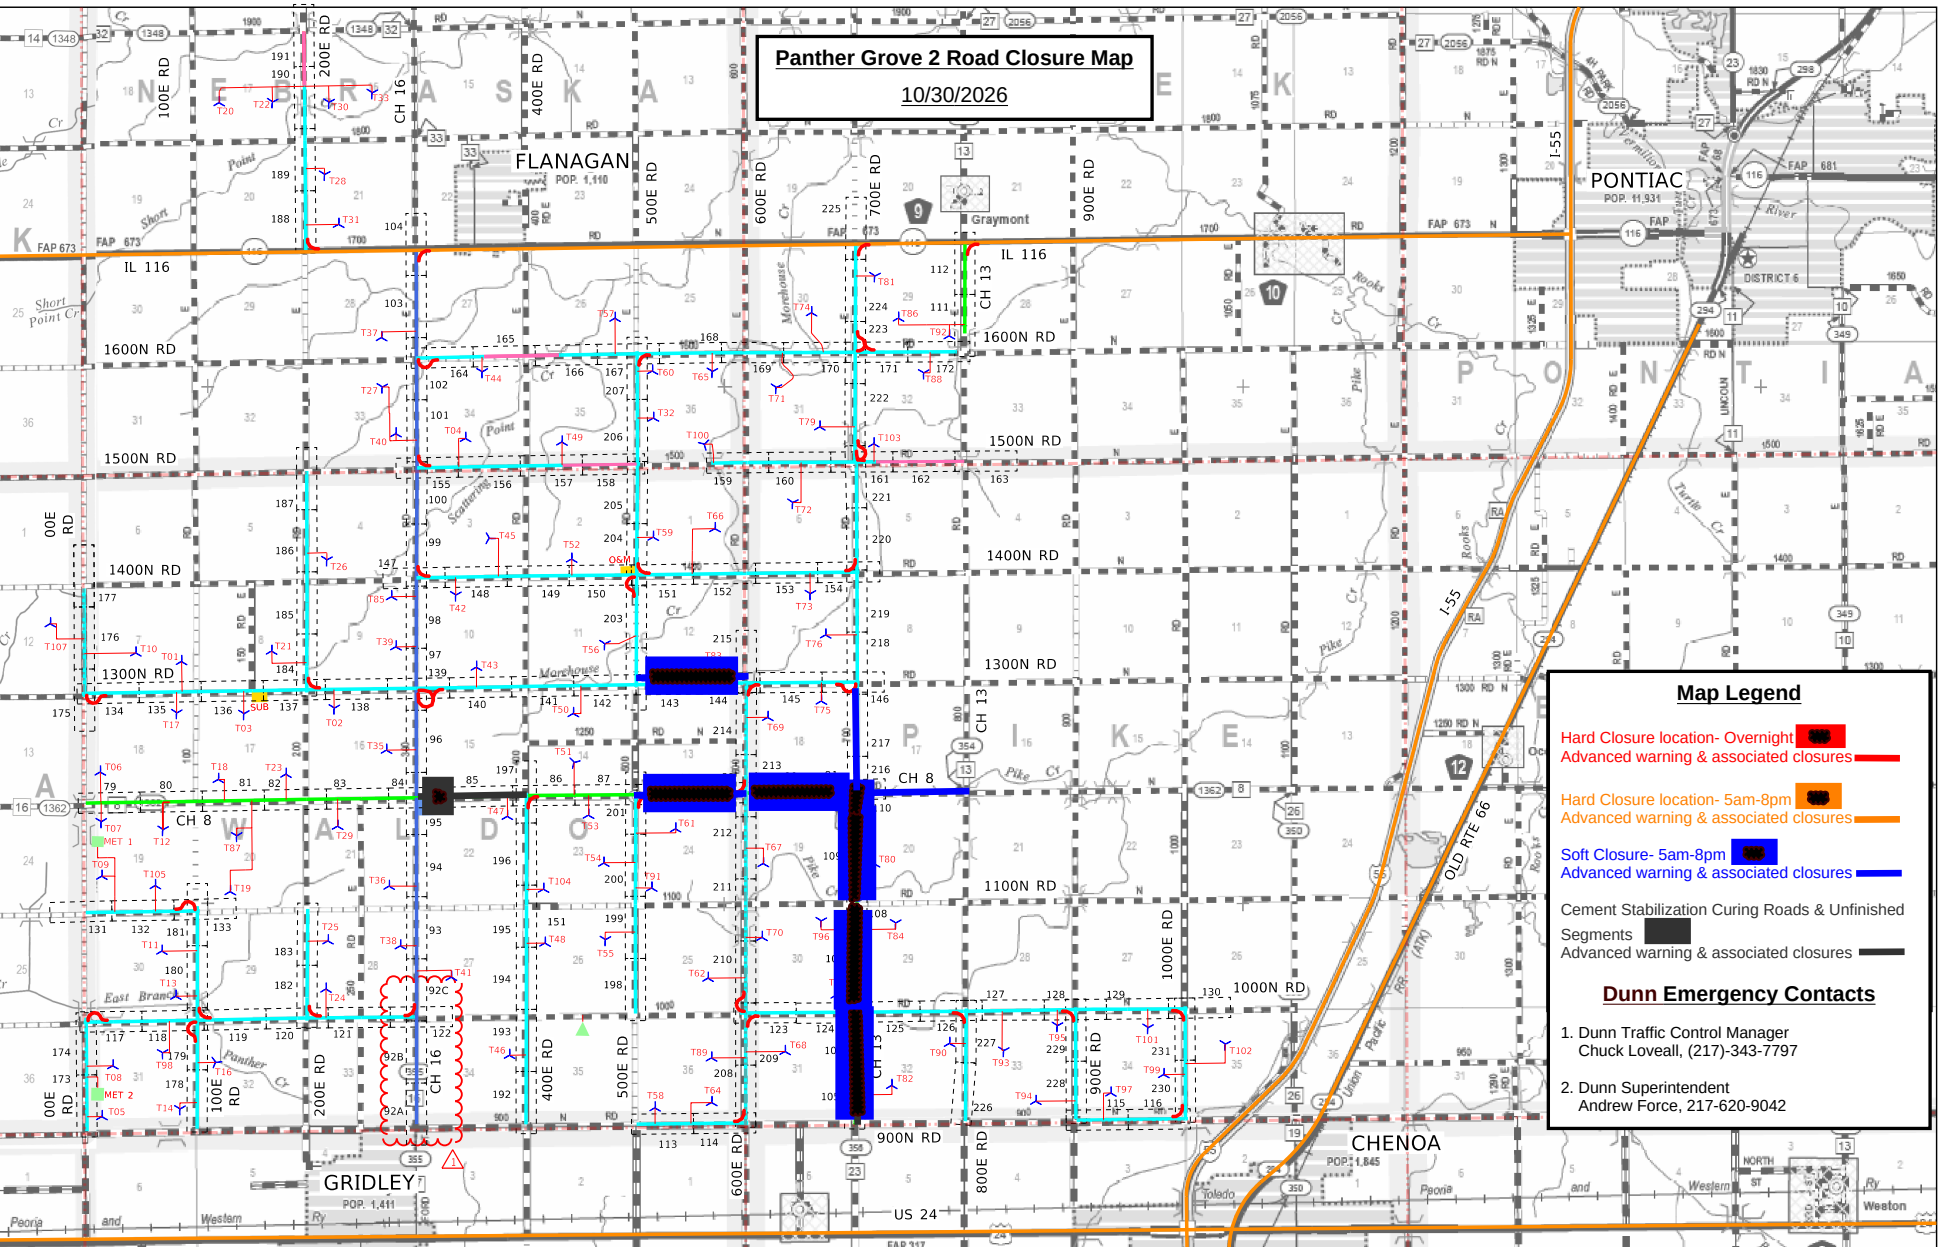


Map Legend

- Hard Closure location- Overnight Advanced warning & associated closures
- Hard Closure location- 5am-8pm Advanced warning & associated closures
- Soft Closure- 5am-8pm Advanced warning & associated closures
- Cement Stabilization Curing Roads & Unfinished Segments
- Advanced warning & associated closures

Dunn Emergency Contacts

1. Dunn Traffic Control Manager
Chuck Loveall, (217)-343-7797
2. Dunn Superintendent
Andrew Force, 217-620-9042

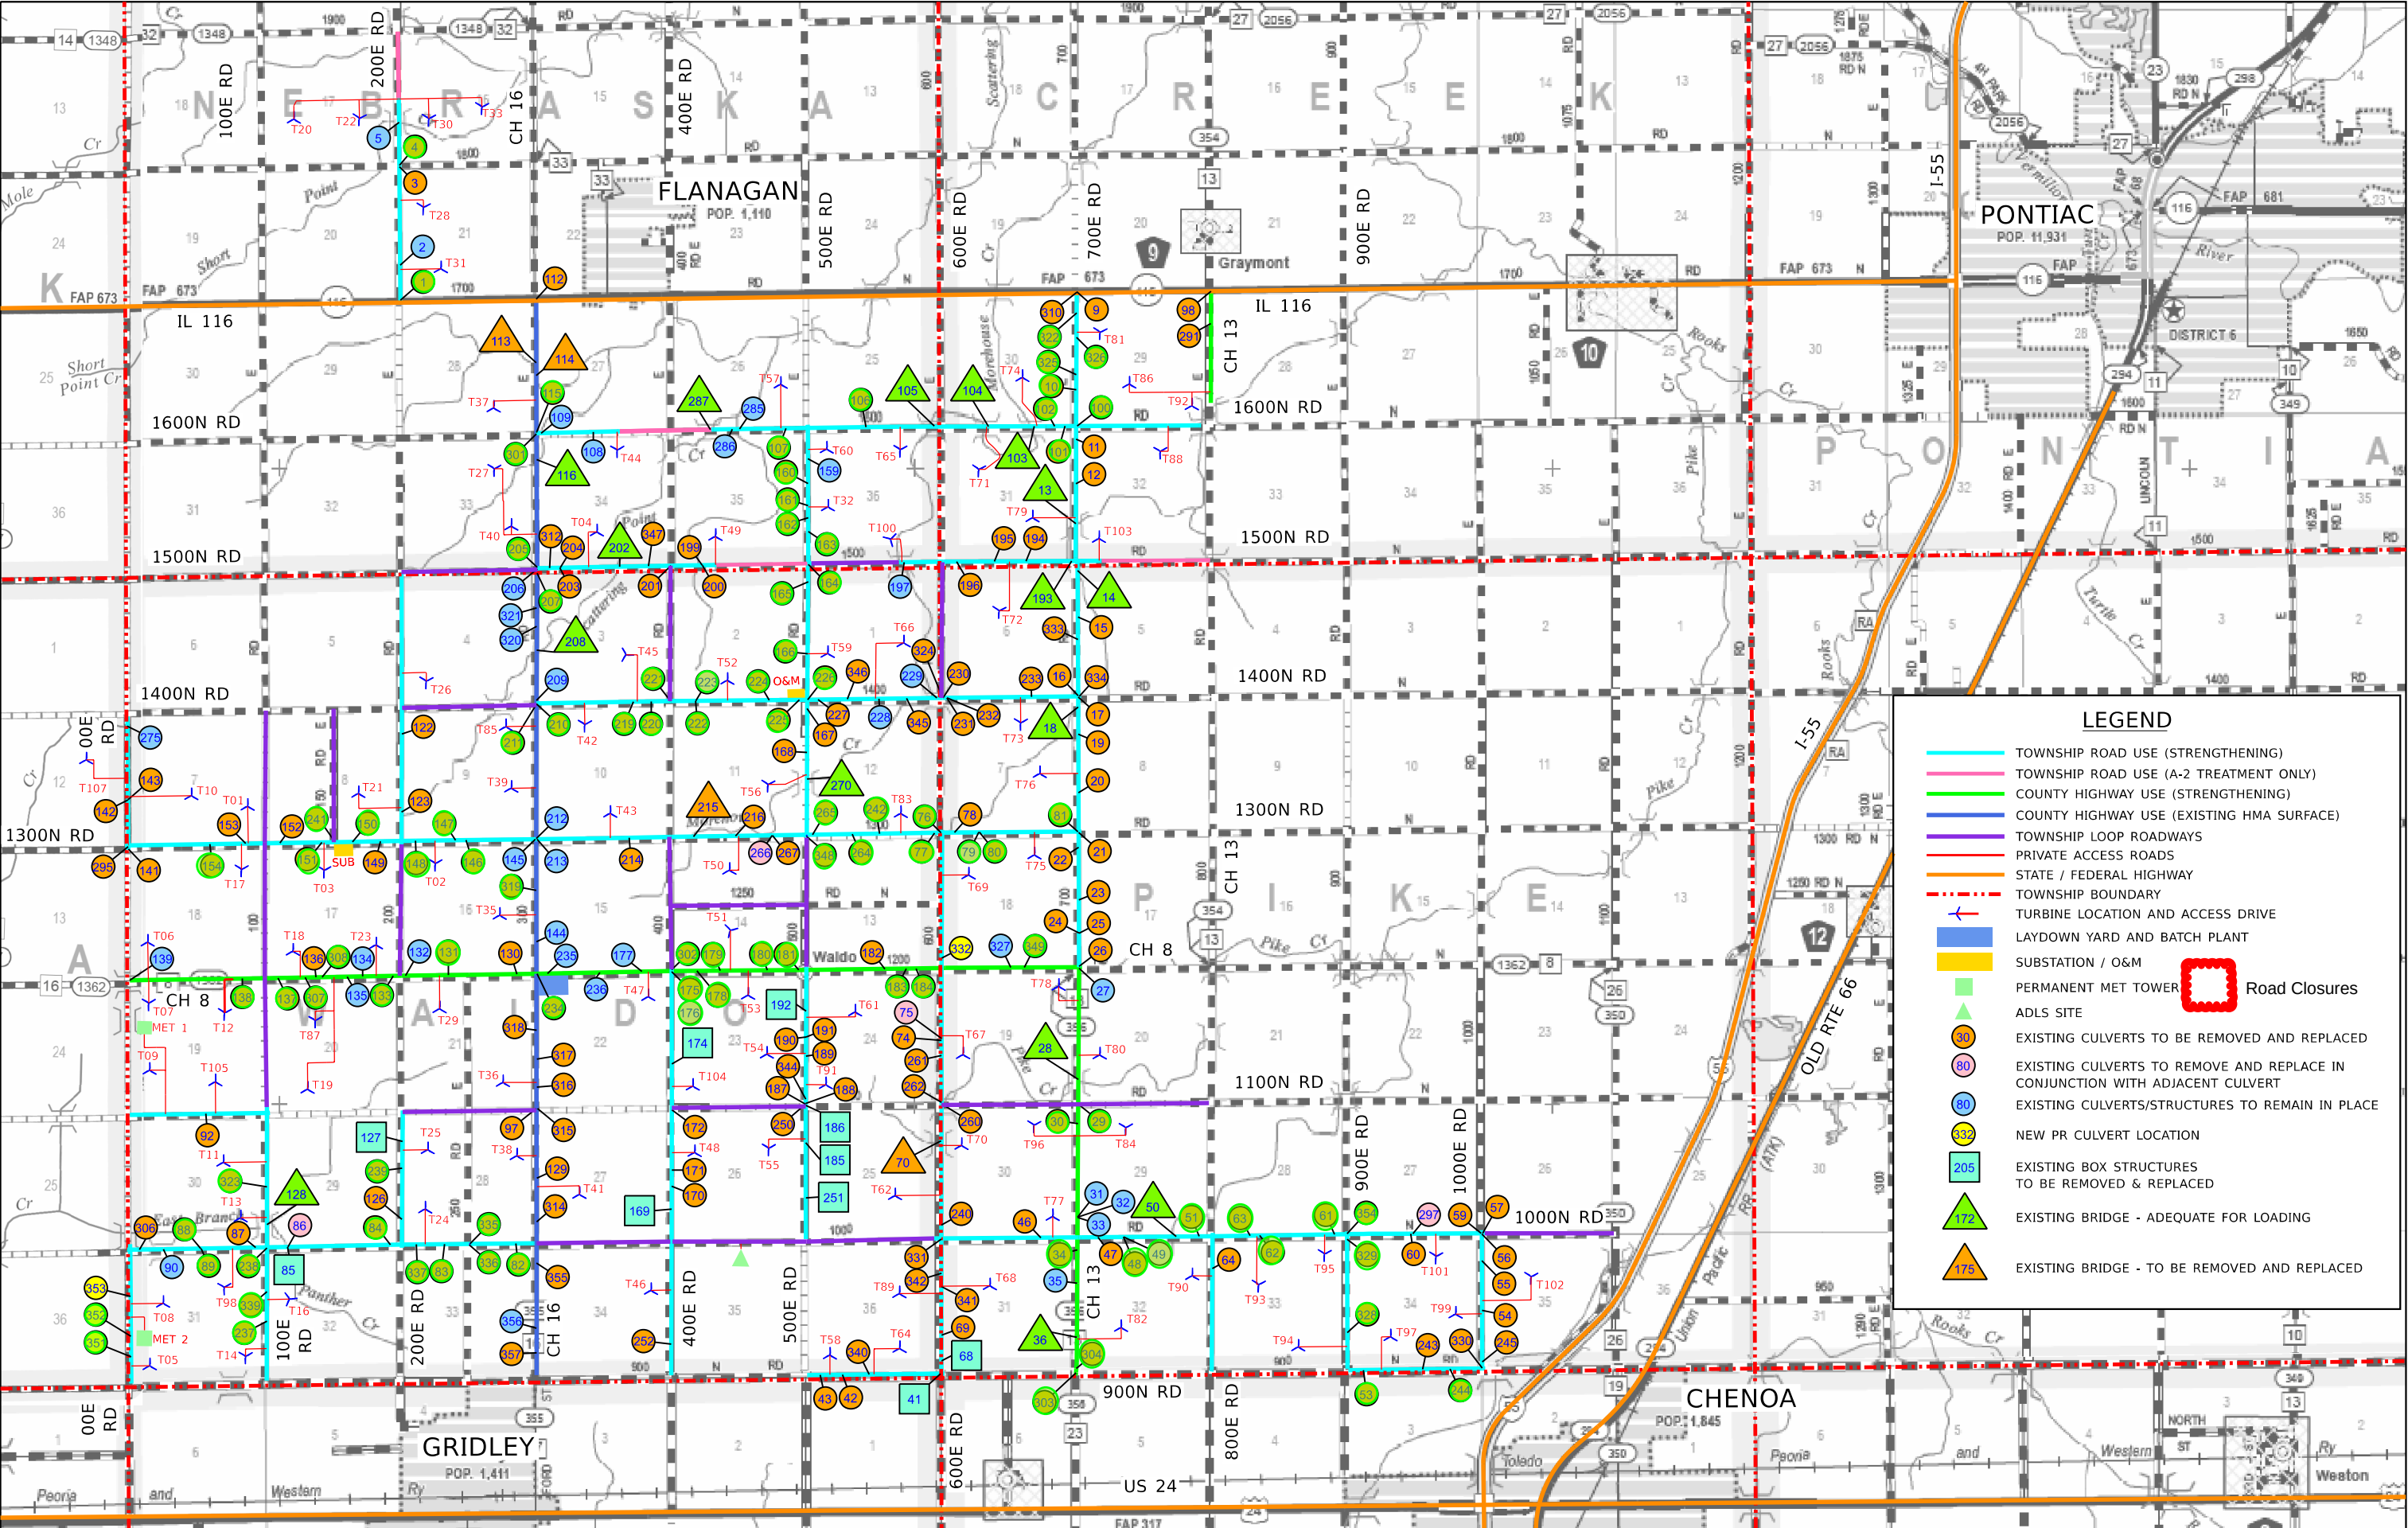

LEGEND

TOWNSHIP ROAD USE (STRENGTHENING)

TOWNSHIP ROAD USE (A-2 TREATMENT ONLY)

COUNTY HIGHWAY USE (STRENGTHENING)

COUNTY HIGHWAY USE (EXISTING HMA SURFACE)

TOWNSHIP LOOP ROADWAYS

PRIVATE ACCESS ROADS

STATE / FEDERAL HIGHWAY

TOWNSHIP BOUNDARY

TURBINE LOCATION AND ACCESS DRIVE

LAYDOWN YARD AND BATCH PLANT

SUBSTATION / O&M

PERMANENT MET TOWER

ADLS SITE

EXISTING CULVERTS TO BE REMOVED AND REPLACED

EXISTING CULVERTS TO REMOVE AND REPLACE IN CONJUNCTION WITH ADJACENT CULVERT

EXISTING CULVERTS/STRUCTURES TO REMAIN IN PLACE

NEW PR CULVERT LOCATION

EXISTING BOX STRUCTURES TO BE REMOVED & REPLACED

EXISTING BRIDGE - ADEQUATE FOR LOADING

EXISTING BRIDGE - TO BE REMOVED AND REPLACED

Road Closures

1	4/10/2026	REV 1	DESIGNED - JDA
00	2/20/2026	IFC SUBMITTAL	DRAWN - DRR/LNS
REV	DATE	DESCRIPTION	CHECKED - ML
			DATE - 04/14/2026

PANTHER GROVE 2 WIND PROJECT
LIVINGSTON COUNTY, ILLINOIS

EXHIBIT A - PROJECT LAYOUT MAP (REVISION 1)

SCALE: N.T.S. SHEET 1 OF 1 SHEETS STA. TO STA.

Farnsworth GROUP

100 WALNUT ST #200
PEORIA, ILLINOIS 61602
(309) 689-9888 / info@f-w.com

TOTAL SHEETS	SHEET NO.	REVISION NO.
