



Panther Grove 2			Daily Safety Topics				DUNN COMPANY Monday, August 10, 2026						
Manpower			Please adhere to traffic control devices.										
10	Dunn Company		Site Notes										
4	Tobey's Construction & Cartage												
7	KVCC												
2	Millennia Professional Services												
0	Material Service Testing												
0	Beniach Construction Company												
4	Dirtworks												
1	HLR												
1	LPM Management Services												
29	Totals												
Key (S) = Start (C) = Continue (F) = Finish			LAST WORKING DAY Sunday, August 9, 2026		TODAY Monday, August 10, 2026		NEXT WORKING DAY Tuesday, August 11, 2026		Quantity Tracking				
ACTIVITY			LOCATION(S)		LOCATION(S)		LOCATION(S)		QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
Road Closures Unfinished Work Zones			200E:1800N-1900N Protecting Work 1800N:100E-200E Protecting Work 1800N:200E-300 Protecting Work 200E:1800N-IL116 Protecting Work 1600N:CH16-400E Protecting Work 1600N:500E-600E Protect work 1600N:600E-700E Protect work 1600N:700E-800 Protect work 600E:1500N-1600N Protect work 600E:IL116-1600N Protect work 1300N:100E-150E Protect work 1300N:500E-600E Protect work 1300N:600E-700E Protect work 600E:1250N-1300N Protect work 600E:1300N-1400N Protect work										
Road Closures Active Work Zones			200E:1800N-1900N Punch List 1800N:100E-200E Punch List 1800N:200E-300 Punch List 200E:1800N-IL116 Punch List 1600N:CH16-400E Punch List 1600N:400E-500E Punch List 1600N:500E-600E Punch List 1600N:600E-700E Punch List 1600N:700E-800E Punch List 600E:1500N-1600N Punch List 600E:IL116-1600N Punch List 1300N:100E-150E 151 700E:1600N-IL116 10		200E:1800N-1900N Oil and Chip 1800N:100E-200E Oil and Chip 1800N:200E-300 Oil and Chip 200E:1800N-IL116 Oil and Chip 1600N:CH16-400E Oil and Chip 1600N:400E-500E Widening 500E:1500N-1600N Widening 1600N:500E-600E Oil and Chip 1600N:600E-700E Oil and Chip 1600N:700E-800E Oil and Chip 600E:1500N-1600N Oil and Chip 600E:IL116-1600N Oil and Chip 1300N:100E-150E 151								
Box Culvert Install									0.0	0.0	EA	15.0	0.0%
Pipe Culvert Install			S 151 C 10		S 303				2.0	56.0	EA	222.0	25.2%
Agg. Widening					C 1600N:400E-500E S 500E: 1600N-1500N				0.0	0.6	Mi	75.0	0.8%
Agg. Profile Adj. & Add Rock									0.0	0.0	MI	75.0	0.0%
Road Pulverization									0.0	21,595.8	SY	781,532.0	2.8%
Cement Stabilization									0.0	21,595.8	SY	781,532.0	2.8%
Agg Surface Install			C 1600N:500E-600E 4" Agg Cap		C 1600N:500E-600E 4" Agg Cap				2,640.0	19,240.0	LF	804,095.0	2.4%
Agg. Shoulder									0.0	1.5	MI	75.0	2.0%
Earthwork									0.0	2.0	MI	75.0	2.7%
Oil and Chip					C 200E:1800N-1900N Oil and Chip C 1800N:100E-200E Oil and Chip C 1800N:200E-300 Oil and Chip C 200E:1800N-IL116 Oil and Chip C 1600N:CH16-400E Oil and Chip S 1600N:500E-600E Oil and Chip S 1600N:600E-700E Oil and Chip S 1600N:700E-800 Oil and Chip S 600E:1500N-1600N Oil and Chip S 600E:IL116-1600N Oil and Chip				0.0	0.0	LF	374,014.0	0.0%
Seeding									0.0	0.0	SY	1,412,544.0	0.0%
Punchlist			C 200E:1800N-1900N Punch List C 1800N:100E-200E Punch List C 1800N:200E-300 Punch List C 200E:1800N-IL116 Punch List C 1600N:CH16-400E Punch List S 1600N:500E-600E Punch List S 1600N:600E-700E Punch List S 1600N:700E-800 Punch List S 600E:1500N-1600N Punch List S 600E:IL116-1600N Punch List						0.0	0.5	MI	75.0	0.7%
HMA									0.0	0.5	TON	75.0	0.7%
Crane Pad Stabilization									0.0	0.0	EA	109.0	0.0%
Access Road Stabilization			S 7.12.19.87		S 19.18.23.29				0.0	9.0	EA	109.0	8.3%

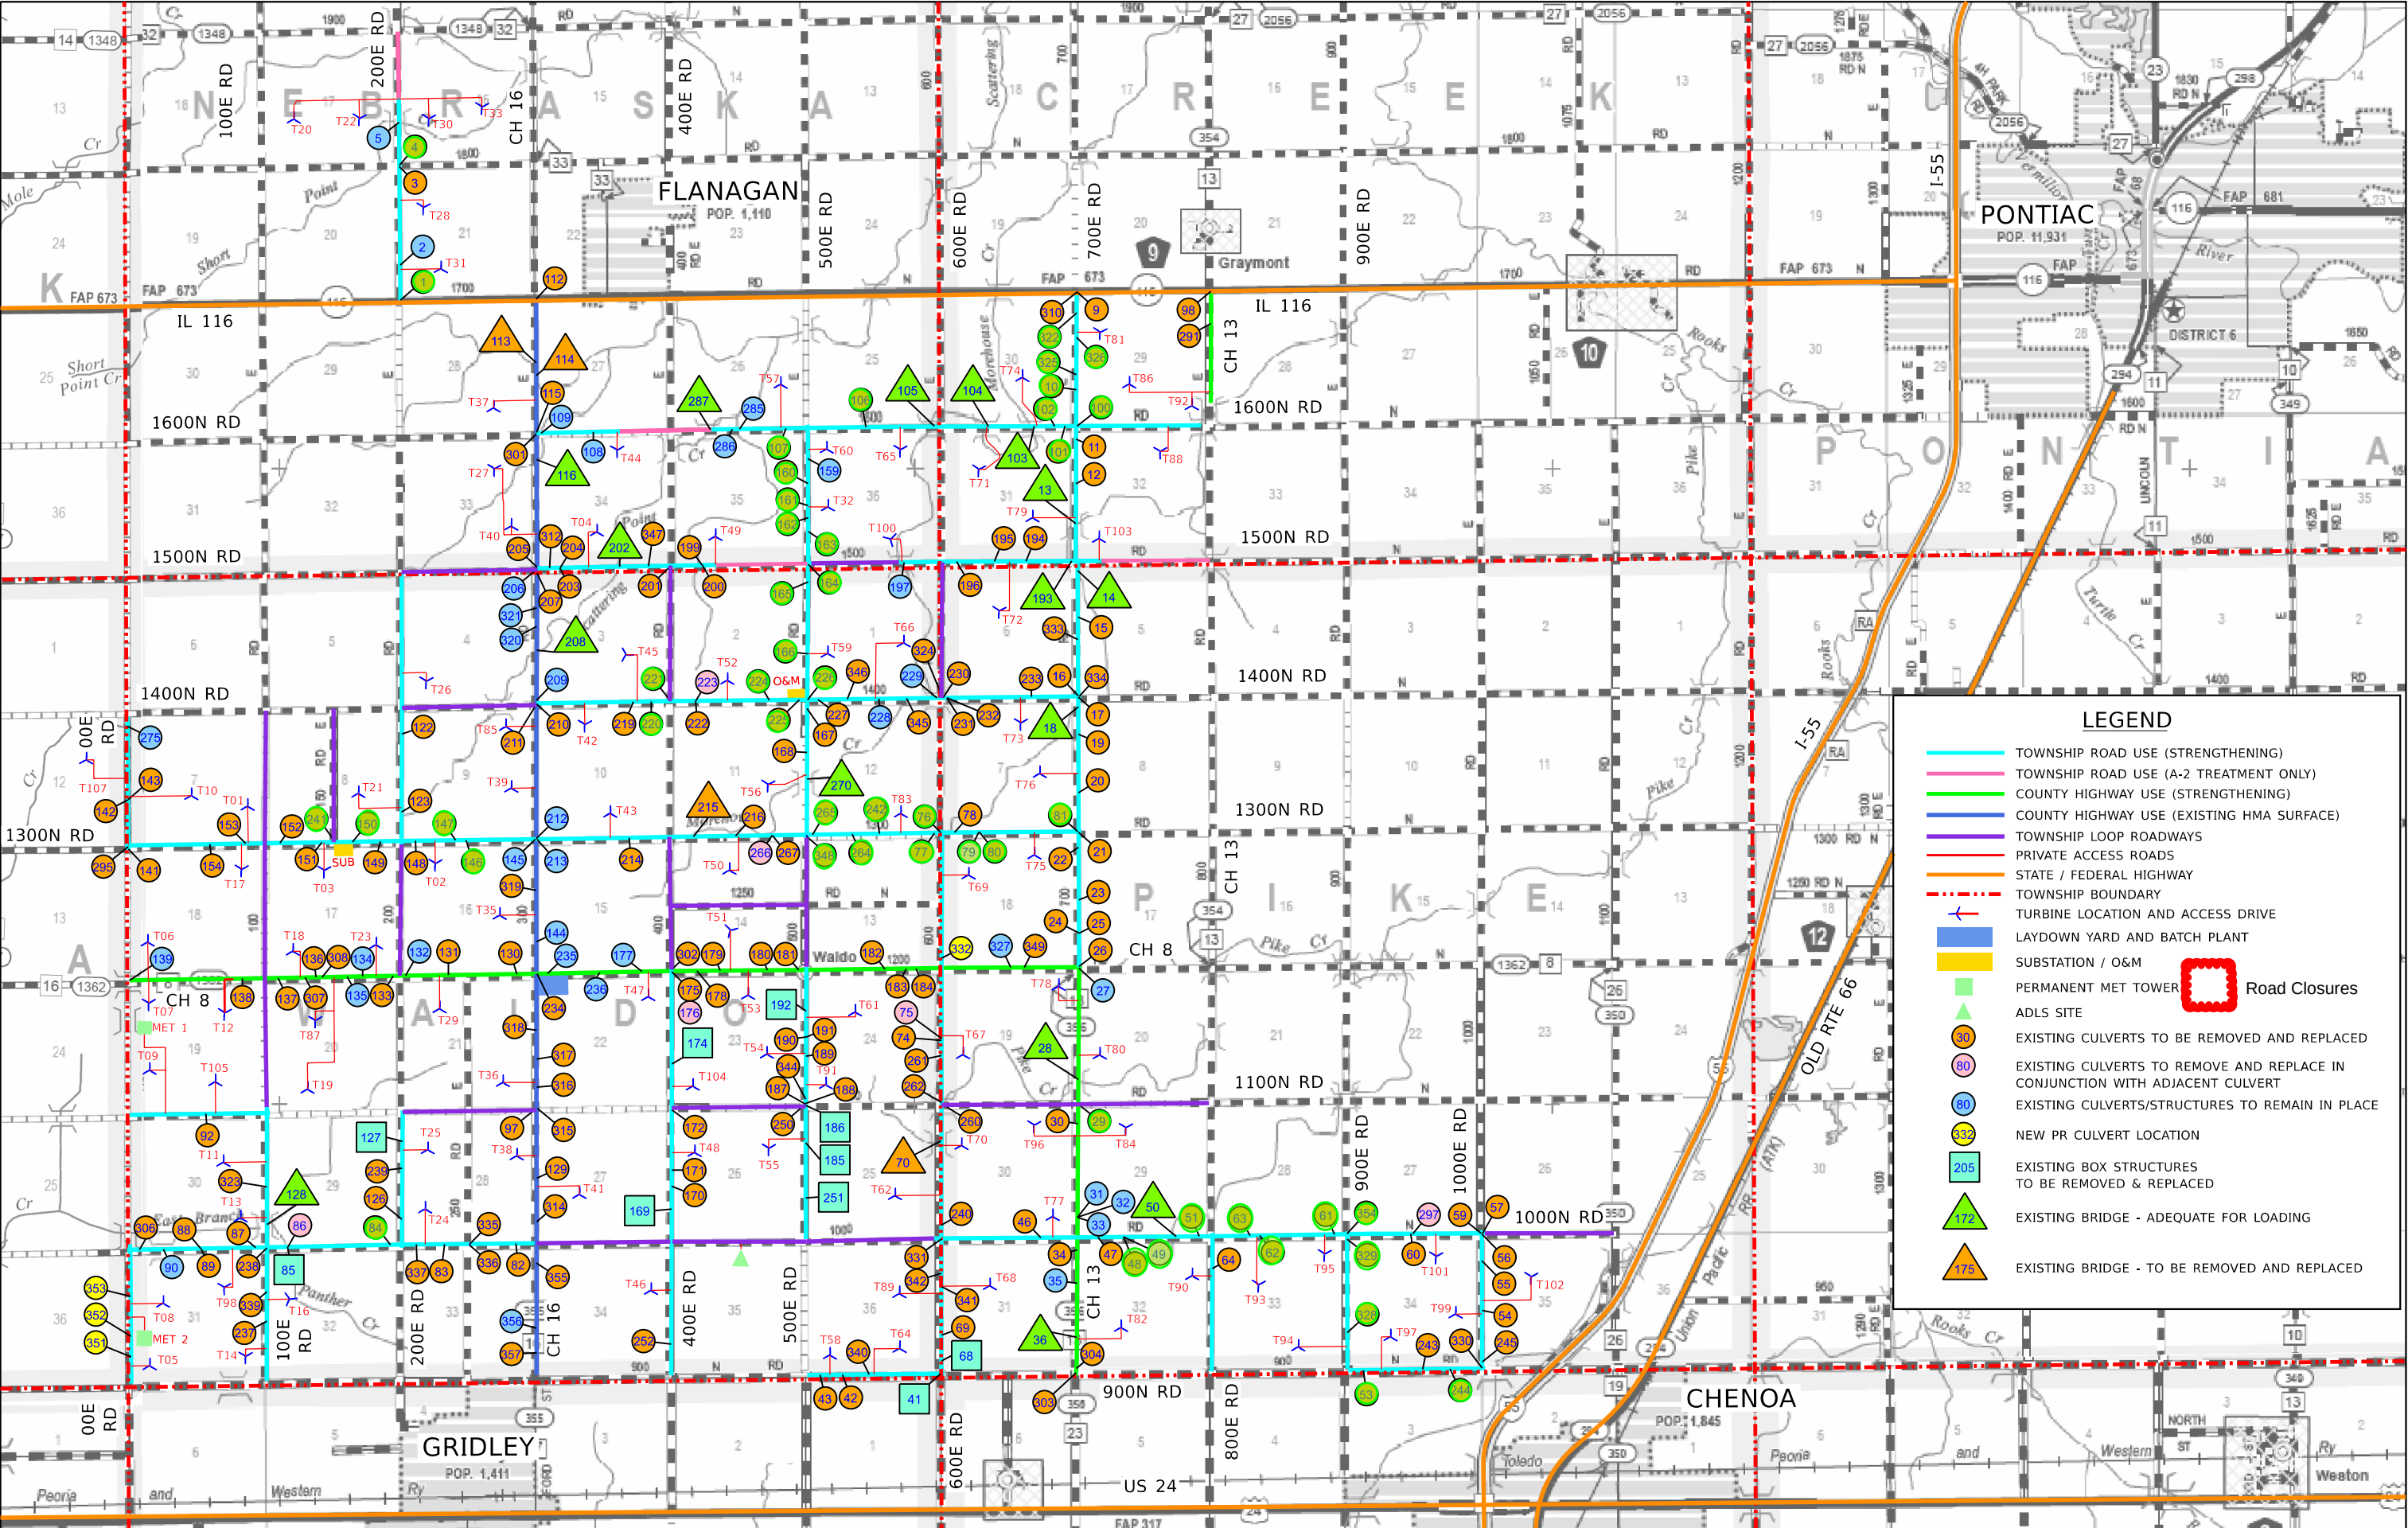

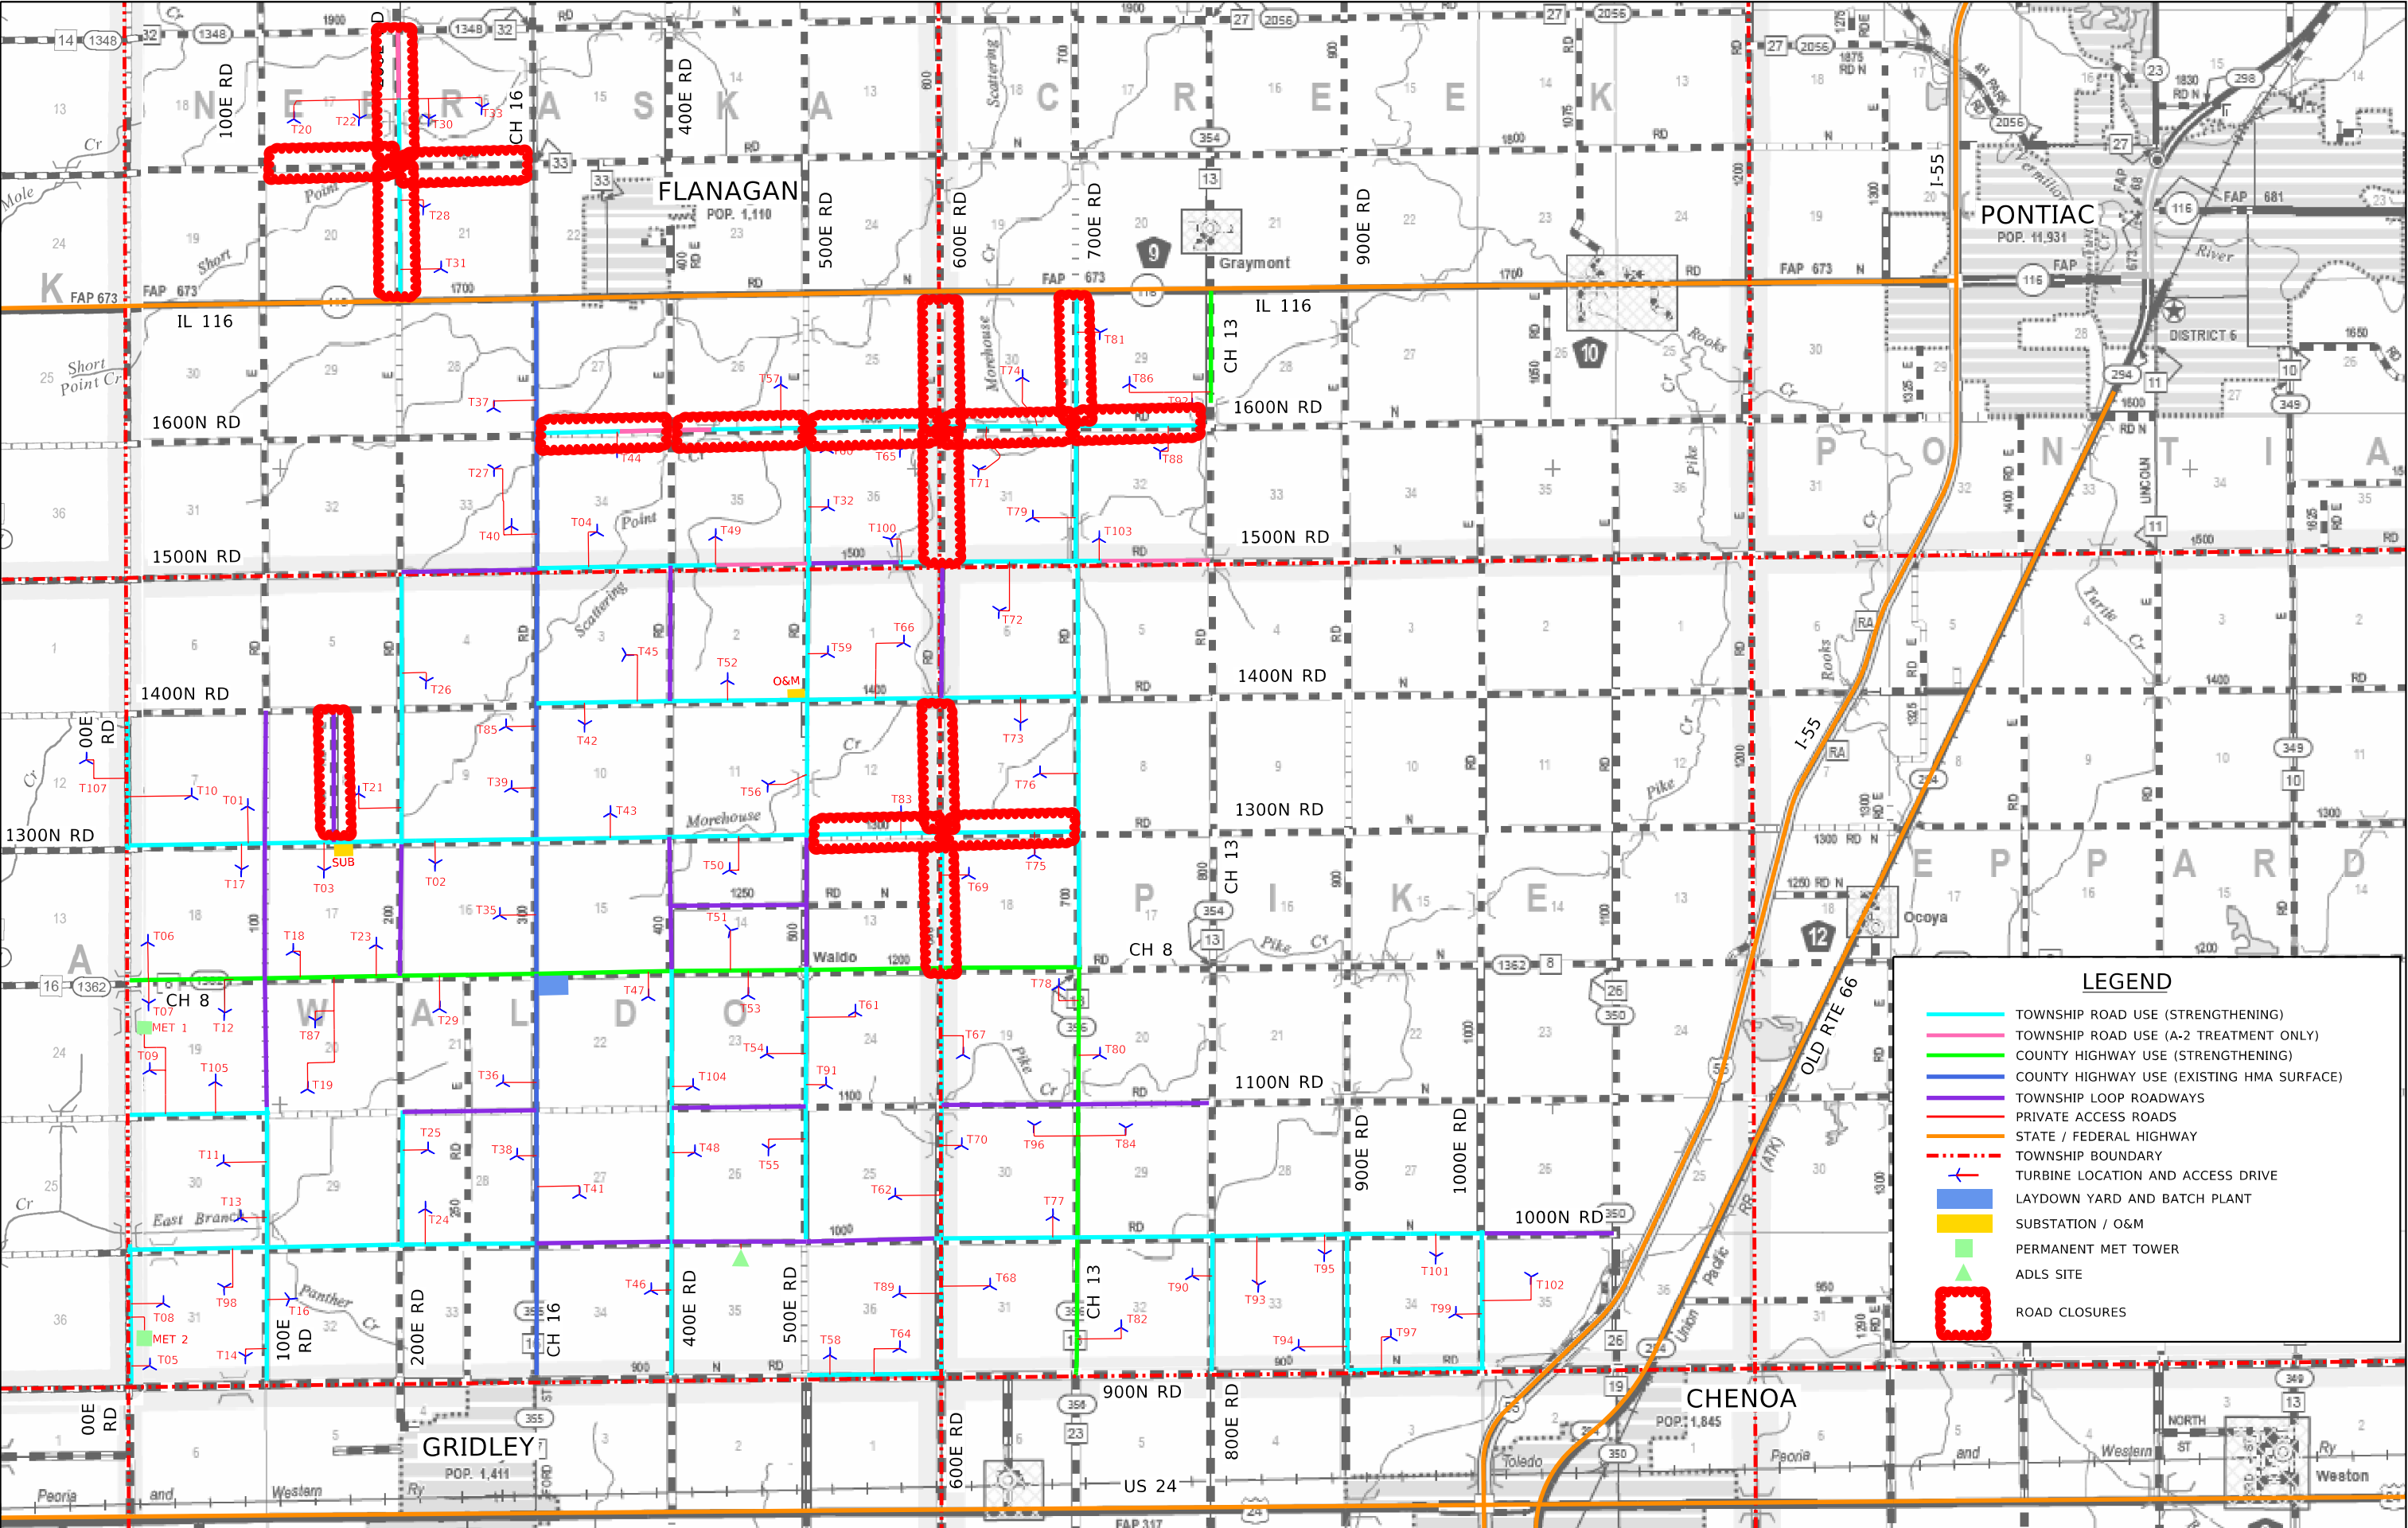

LEGEND

TOWNSHIP ROAD USE (STRENGTHENING)

TOWNSHIP ROAD USE (A-2 TREATMENT ONLY)

COUNTY HIGHWAY USE (STRENGTHENING)

COUNTY HIGHWAY USE (EXISTING HMA SURFACE)

TOWNSHIP LOOP ROADWAYS

PRIVATE ACCESS ROADS

STATE / FEDERAL HIGHWAY

TOWNSHIP BOUNDARY

TURBINE LOCATION AND ACCESS DRIVE

LAYDOWN YARD AND BATCH PLANT

SUBSTATION / O&M

PERMANENT MET TOWER

ADLS SITE

ROAD CLOSURES
