Panther Grove 2

	10-Nov-26	Today
Daily Weather as of 7:00am	Cloudy	Sunny
Low Temperature (F)	40	37
High Temperature (F)	67	60
Ground Wind Speed (MPH):	7 mph	4 mph
Precipitation (in)	0.00	24%
November Precip Total (In)	0.50	

Daily Safety Topics

Leading edges and Elevated work- Just because we are not working up tower or an elevated work platform doesn't mean we aren't at risk for falls. When we are exposed to a fall whether it's on an elevated surface or drop to lower level we need to make sure in our hazard recognition we speak on whether we can eliminate the risk or if we need to acquire and utilize fall protection.

Congested areas - With many vehicles and people within the same work area, there are sure to congested areas. Let's ensure

Site Notes

Friday, November 13, 2026

	ACTIVITY	LAST WORKING DAY Tuesday, November 10, 2026 LOCATION(S)	TODAY Wednesday, November 11, 2026 LOCATION(S)	NEXT WORKING DAY Thursday, November 12, 2026 LOCATION(S)
Public Roads	Strip Public Road Radii	P12 (1400N RD / 500E RD)	P12 (1400N RD / 500E RD)	
	Mowing Public Road Radii			
	Stone Public Road Radii	P21 (CH 8 / 500E RD), P22 (CH 8 / 600E RD)	P12 (1400N RD / 500E RD), P22 (CH 8 / 600E RD)	
Access Roads	Strip Access Road			
	Cement Stabilization			
	Stone Access Road	T002, T78	T80	
	Strip Access Road Radii			
	Stone Access Road Radii			

Quantity Tracking

QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
	11	EA	35	31.4%
	11	EA	35	31.4%
	78138	LF	161120	48.5%
	77221.5	LF	161120	47.9%
	59548.5	LF	161120	37.0%
	64	EA	TBD	#VALUE!
	61	EA	TBD	#VALUE!

Site Information

Manpower	
19	White Construction Management
47	White Construction Operators
27	White Construction Laborers
16	White Construction Ironworkers
0	White Construction Millwright
3	White Construction Electrician
15	Dunn Company
8	West Wind
0	Tobey's Construction & Cartage
0	KVCC
6	Prairie Materials
19	JF Edwards
5	Keeley
165	**Total**

Equipment	
48	Pickup Trucks
3	Dozers
0	Rollers
1	Graders
1	Cargo Trailer
0	Cranes
3	Excavators
0	Forklift
13	Trailers
0	Sand Truck
1	Sheepfoot Roller
0	Reclaimer Stabilizer
1	Smooth Drum Roller
2	Water Trucks
5	Skid Steer
78	**Total**

Additional Comments

Plan of the Day (POD) Report

11-Nov-2026

PANTHER GROVE WIND ENERGY FACILITY

Weather Notes: Rain out on 10-15	LAST WORKING DAY	TODAY	NEXT WORKING DAY	2-Day Lookahead
	64° / 47° Temp Range	59° / 43° Temp Range	47° / 33° Temp Range	42° / 30° Temp Range
	None Precipitation	25% | 0.00 in | None Precipitation	18% | 0.00 in | None Precipitation	None Precipitation
	None | None Lighting Risk	None | None Lighting Risk	None | None Lighting Risk	None | None Lighting Risk
	None | 0% | None Severe Forcast	None | 0% | None Severe Forcast	None | 0% | None Severe Forcast	None | 0% | None Severe Forcast
	10.6 Max Wind	11.4 Max Wind	20.3 Max Wind	13.4 Max Wind
	28 Max Gust	24.2 Max Gust	31.3 Max Gust	28 Max Gust
(S) Start (C) Continue (F) Finish	Tuesday, November 10, 2026	Wednesday, November 11, 2026	Thursday, November 12, 2026	Friday, November 13, 2026
	LOCATION(S) Road / Repening	LOCATION(S) Road / Repening	LOCATION(S) Road / Repening	LOCATION(S) Road / Repening

Today's Notes

Active Cure	Date	Day	Cure		
CH8:CH16-400E	10/23	19	10/30		
N/A					
N/A					
N/A					
N/A					

Manpower	Scope	QTY
Dunn Company	Agg Surface, Earthwork	15
Tobey's Constr.	Pipe Culvert	0
KVCC	Agg Surface	0
Millennia	QC	0
Material Serv. Test.	QC	0
Beniach	Oil and Chip	0

Notes:
Box Culvert: In procurement

Pipe Culvert: Ongoing

Agg Widening: On hold

Profile Adj./Add Rock: On hold

Pulverization: on hold

Stabilization: on hold

Agg Surface: on hold

Oil and Chip: on hold

Earthwork: on hold

Seeding: on hold

HMA: On hold until IDOT permits are in place.


Punchlist: On going


Long Duration Road Closures

Short Duration Road Closures

	LAST WORKING DAY	TODAY	NEXT WORKING DAY	2-Day Lookahead
Short Duration Road Closures	☑ CH16:1400N-1500N 11/9/2026 ☑ CH16:1400N-1300N 11/9/2026 ☑ 1400N:CH16-200E 11/9/2026 ☑ 1400N:CH16-400E 11/9/2026	☑ 1300N:00E-100E 11/11/2026 ☑ 700E:CH8-1300N 11/11/2026 ☑ CH8:600E-CH13 11/11/2026 ☑ CH8:CH13-800E 11/11/2026 ☑ CH13:1100N-CH8 11/11/2026		

		QTY Last Work Day	QTY Complete	Unit	Total QTY	% Complete	TODAY	NEXT WORKING DAY	2-Day Lookahead
Public Road Improvements	Box Culvert	0.0	1.0	EA	15.0	6.7%			
	Pipe Culvert S 26	1.0	110.0	EA	222.0	49.5%	C 26 S 153 S 154		
	Spraying MC-30 on roads that were Aggregate Widened only on widened areas MC-30 C 1000N:CH13-800E C 1000N:800E-900E C 1000N:900E-1000E C 800E:900N-1000N C 900E:900N-1000N C 1000E:900N-1000N C 900N:900E-1000E	0.0	23.0	Mi	75.0	30.7%	MC-30		
	Prof. Adj.	0.0	12.0	EA					
	Pulverization	0.0	23.5	Mi	75.0	31.3%			
	Stabilization	0.0	23.5	Mi	75.0	31.3%			
	Agg Surface	0.0	23.5	Mi	75.0	31.3%			
	Oil and Chip	0.0	23.5	Mi	75.0	31.3%			
	Earthwork	0.0	23.5	Mi	75.0	31.3%			
	Seeding	0.0	23.5	Mi	75.0	31.3%			
	Punchlist	0.0	23.5	Mi	75.0	31.3%			
	HMA F CH 16 Patches 113.210/211	0.0	7.0	EA	17.0	41.2%			
Site	Crane Pad		12.0	EA	109.0	11.0%			
	Access Road	0.0	43.0	EA	109.0	39.4%			

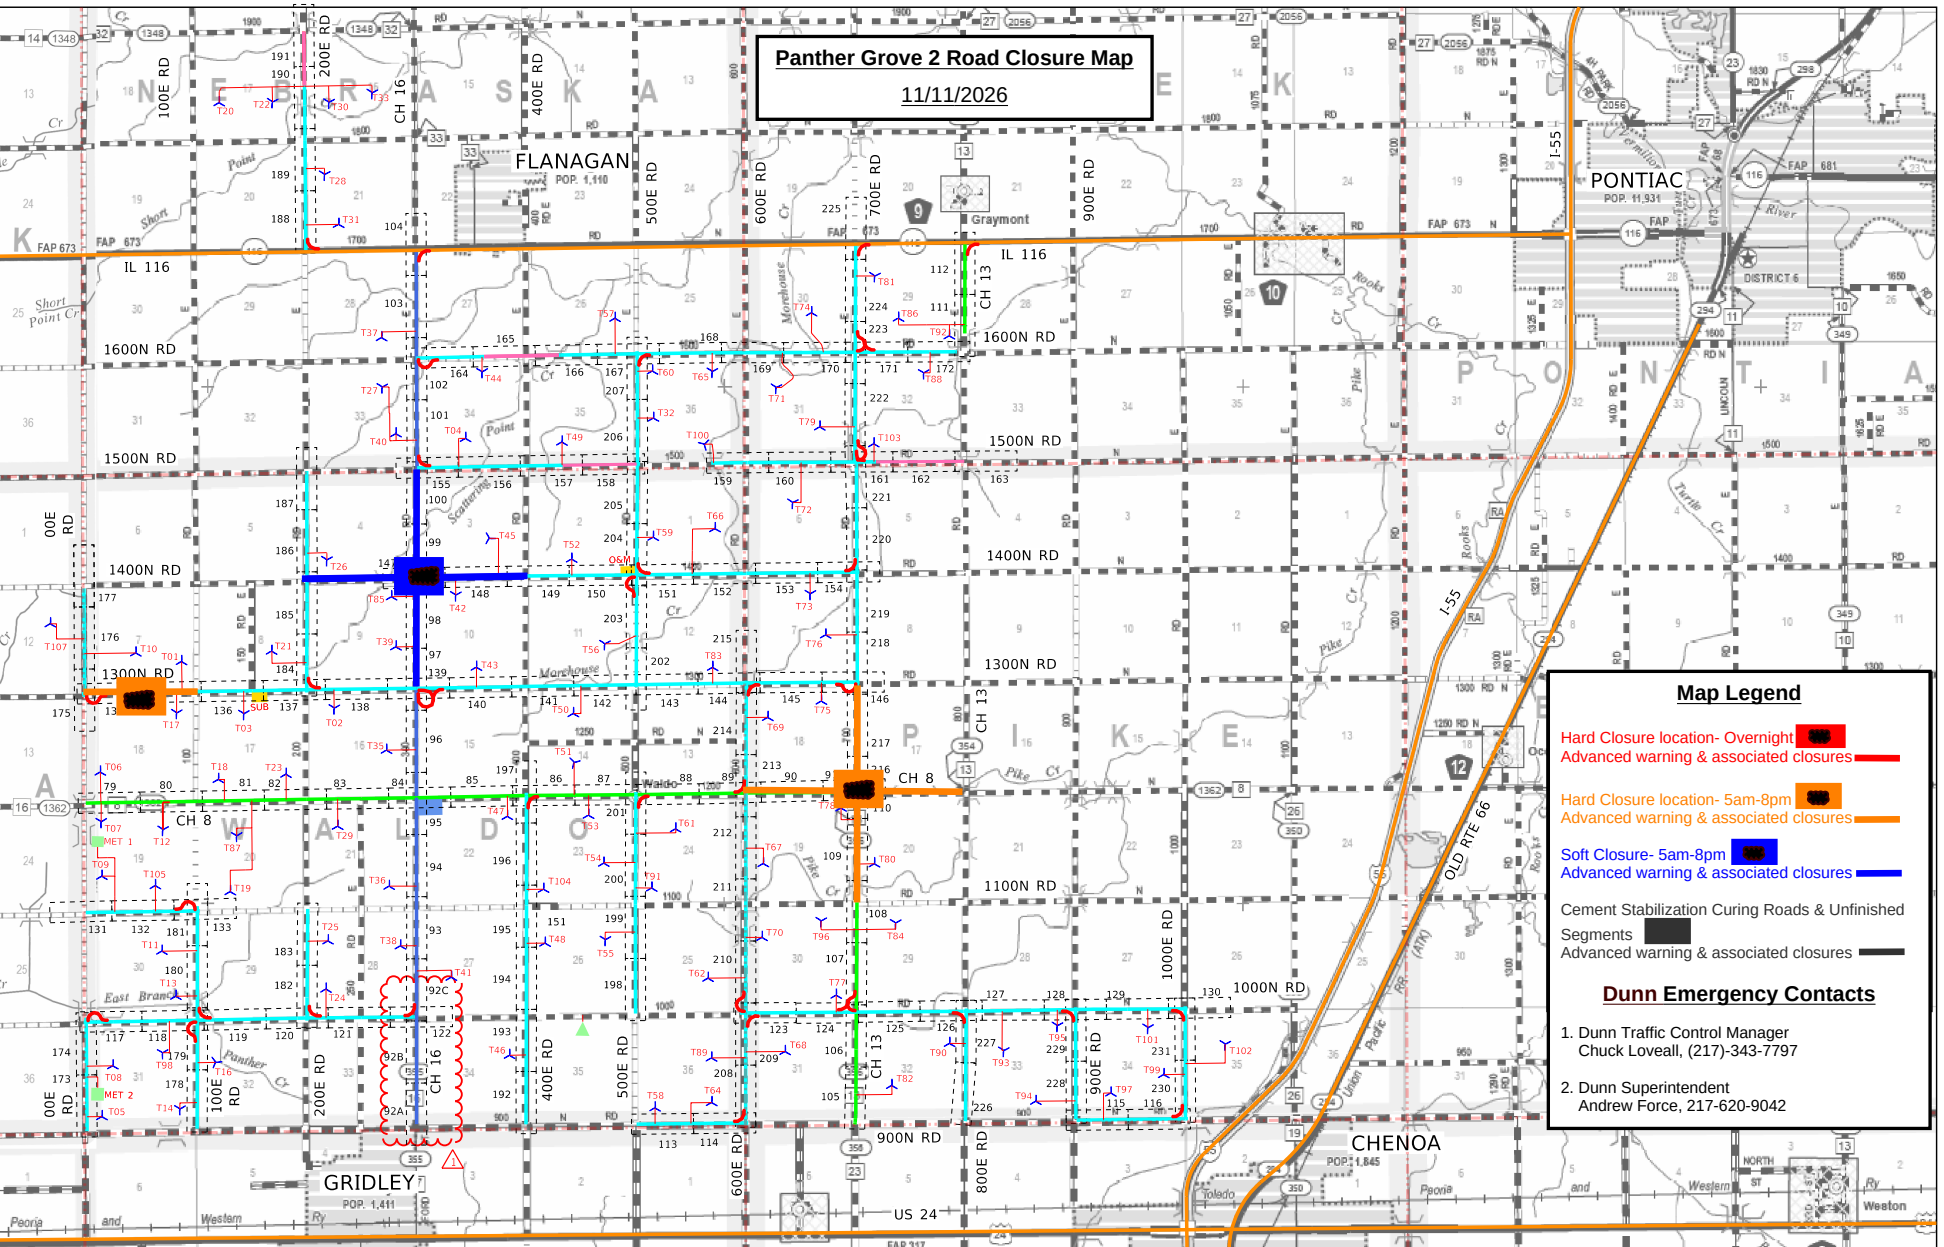
Panther Grove 2 Road Closure Map
11/11/2026
Map Legend
Hard Closure location- Overnight
Advanced warning & associated closures
Hard Closure location- 5am-8pm
Advanced warning & associated closures
Soft Closure- 5am-8pm
Advanced warning & associated closures
Cement Stabilization Curing Roads & Unfinished Segments
Advanced warning & associated closures
Dunn Emergency Contacts
1. Dunn Traffic Control Manager
Chuck Loveall, (217)-343-7797
2. Dunn Superintendent
Andrew Force, 217-620-9042
FLANAGAN
POP. 1,110
PONTIAC
POP. 11,931
GRIDLEY
POP. 1,411
CHENOA
POP. 1,845
Graymont
DISTRICT 6
IL 116
1600N RD
1500N RD
1400N RD
1300N RD
1100N RD
1000N RD
900N RD
100E RD
200E RD
400E RD
500E RD
600E RD
700E RD
800E RD
900E RD
CH 16
CH 13
CH 8
I-55
US 24
OLD RTE 66
FAP 673
FAP 116
FAP 681
Short Point Cr
Panther Cr
East Branch
Waldo
Pike Cr
Rooks Cr
Turtle Cr
Scattering Point
Morehouse
Peoria and Western Ry
Toledo Peoria and Western Ry
Union Pacific (ATK)

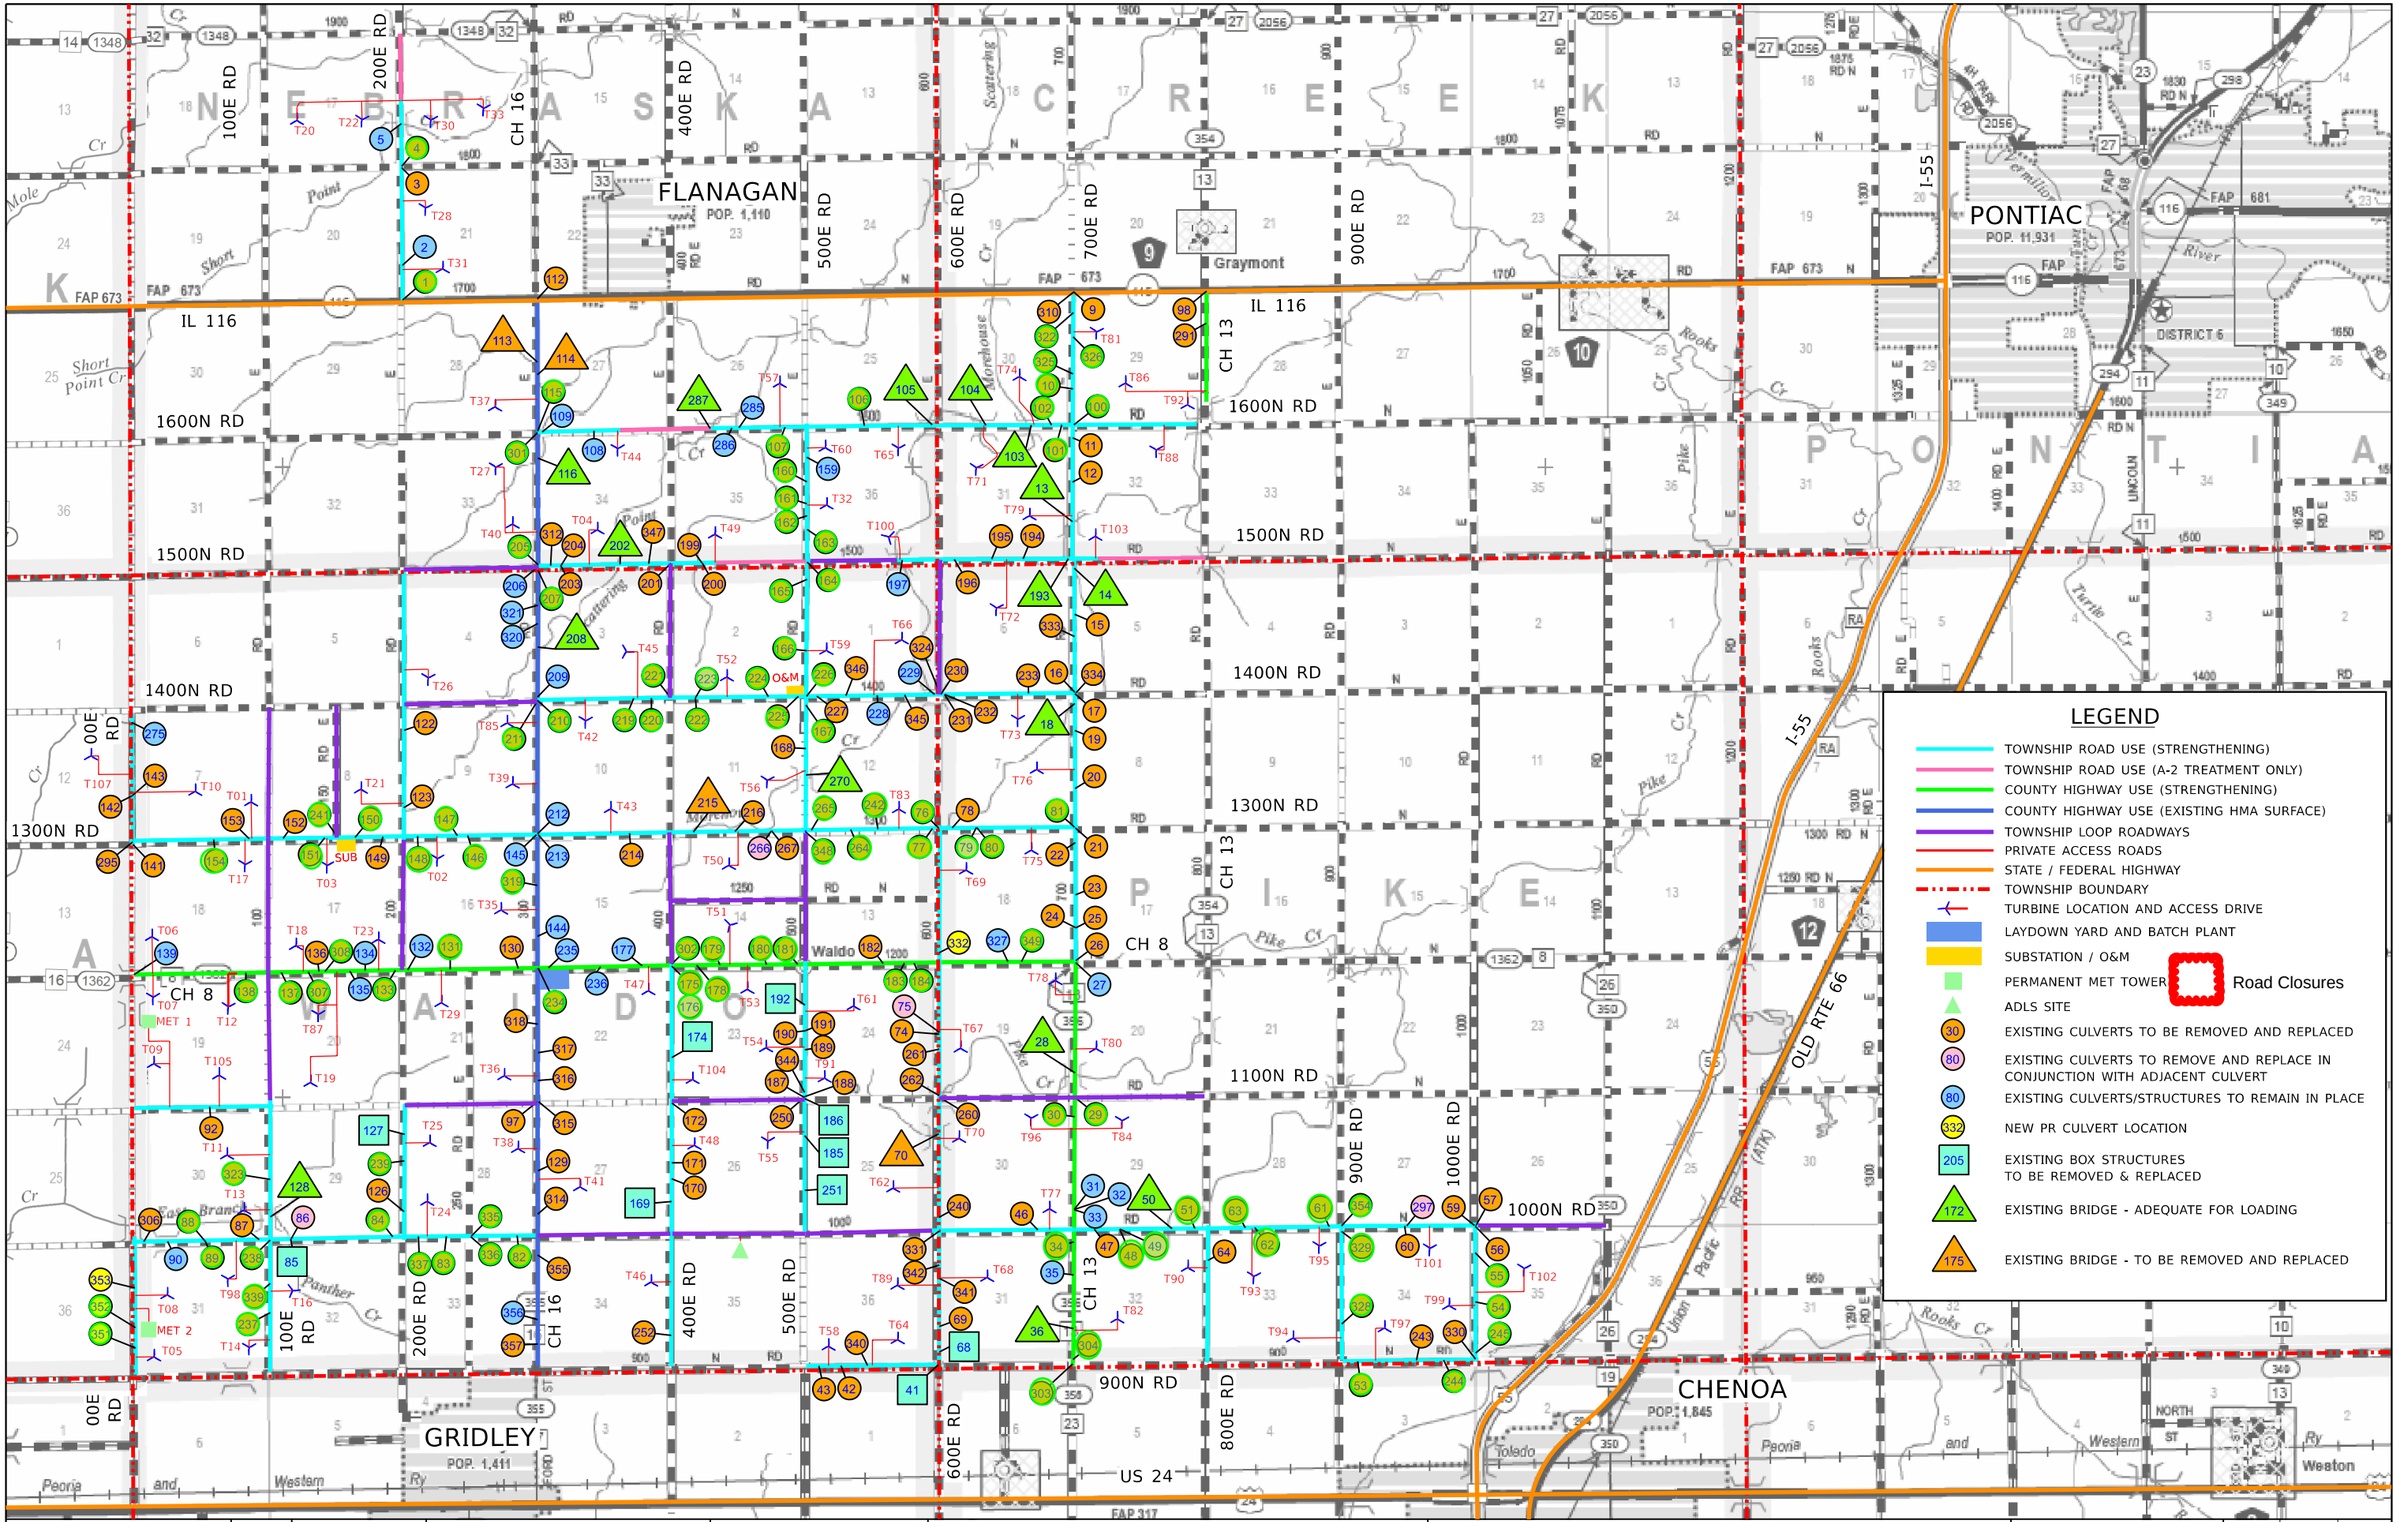

REV	DATE	DESCRIPTION
1	4/10/2026	REV 1
00	2/20/2026	IFC SUBMITTAL

DESIGNED - JDA
DRAWN - DRR/LNS
CHECKED - ML
DATE - 04/14/2026

PANTHER GROVE 2 WIND PROJECT
LIVINGSTON COUNTY, ILLINOIS

EXHIBIT A – PROJECT LAYOUT MAP (REVISION 1)

SCALE: N.T.S. | SHEET 1 OF 1 SHEETS | STA. TO STA.

Farnsworth GROUP
100 WALNUT ST #200
PEORIA, ILLINOIS 61602
(309) 689-9888 / Info@f-w.com

TOTAL SHEETS	SHEET NO.	REVISION NO.
