Panther Grove 2

	6-Nov-26	Today
Daily Weather as of 7:00am	Cloudy	Sunny
Low Temperature (F)	38	43
High Temperature (F)	52	63
Ground Wind Speed (MPH):	11 mph	9 mph
Precipitation (in)	0.00	6%
November Precip Total (In)	0.50	

Daily Safety Topics

Speed in and around site- Lets work together to make sure we are watching our speed around work areas, laydown yard, and access roads. Nothing is so important that we risk not going home safely or put someone else life in danger.

MUD/Site conditions- With the weather we have had lets make sure we avoid driving in the mud and when not possible if we do get mud into the road, we reach out to get the sweeper out. If we are hauling equipment or material around take some

Site Notes

Monday, November 9, 2026

	ACTIVITY	LAST WORKING DAY Friday, November 6, 2026 LOCATION(S)	TODAY Monday, November 9, 2026 LOCATION(S)	NEXT WORKING DAY Tuesday, November 10, 2026 LOCATION(S)
Public Roads	Strip Public Road Radii	P21 (CH 8 / 500E RD), P22 (CH 8 / 600E RD)	P22 (CH 8 / 600E RD)	P22 (CH 8 / 600E RD)
	Mowing Public Road Radii			
	Stone Public Road Radii	P21 (CH 8 / 500E RD), P22 (CH 8 / 600E RD)	P21 (CH 8 / 500E RD), P22 (CH 8 / 600E RD)	P21 (CH 8 / 500E RD), P22 (CH 8 / 600E RD)
Access Roads	Strip Access Road			
	Cement Stabilization	T78, T80, T96	T84,T82	T84,T82
	Stone Access Road			
	Strip Access Road Radii			
	Stone Access Road Radii			

Quantity Tracking

QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
	12	EA	35	34.3%
	10	EA	35	28.6%
	66695	LF	161120	41.4%
	67827.5	LF	161120	42.1%
	55073.5	LF	161120	34.2%
	63	EA	TBD	#VALUE!
	59	EA	TBD	#VALUE!

Site Information

Manpower

19	White Construction Management
47	White Construction Operators
27	White Construction Laborers
16	White Construction Ironworkers
0	White Construction Millwright
3	White Construction Electrician
15	Dunn Company
8	West Wind
0	Tobey's Construction & Cartage
0	KVCC
6	Prairie Materials
19	JF Edwards
5	Keeley
165	**Total**

Equipment

48	Pickup Trucks
3	Dozers
0	Rollers
1	Graders
1	Cargo Trailer
0	Cranes
3	Excavators
0	Forklift
13	Trailers
0	Sand Truck
1	Sheepfoot Roller
0	Reclaimer Stabilizer
1	Smooth Drum Roller
2	Water Trucks
5	Skid Steer
78	**Total**

Additional Comments

Plan of the Day (POD) Report

7-Nov-2026

PANTHER GROVE WIND ENERGY FACILITY

Weather Notes: Rain out on 10-15	LAST WORKING DAY		TODAY		NEXT WORKING DAY		2-Day Lookahead	
	48° / 38°	Temp Range	49° / 35°	Temp Range	53° / 37°	Temp Range	58° / 38°	Temp Range
	10% | 0.00 in | None	Precipitation	None	Precipitation	None	Precipitation	None	Precipitation
	None | None	Lighting Risk	None | None	Lighting Risk	None | None	Lighting Risk	None | None	Lighting Risk
	None | 0% | None	Severe Forcast	None | 0% | None	Severe Forcast	None | 0% | None	Severe Forcast	None | 0% | None	Severe Forcast
	16	Max Wind	8.4	Max Wind	4.6	Max Wind	7.6	Max Wind
	28.9	Max Gust	13.9	Max Gust	8.1	Max Gust	16.1	Max Gust
(S) Start (C) Continue (F) Finish	Friday, November 6, 2026		Saturday, November 7, 2026		Sunday, November 8, 2026		Monday, November 9, 2026	
	LOCATION(S)		LOCATION(S)		LOCATION(S)		LOCATION(S)	
	Road	Repening	Road	Repening	Road	Repening	Road	Repening

Today's Notes

Active Cure	Date	Day	Cure		
CH8:CH16-400E	10/23	15	10/30		
N/A					
N/A					
N/A					
N/A					

Manpower	Scope	QTY
Dunn Company	Agg Surface, Earthwork	15
Tobey's Constr.	Pipe Culvert	0
KVCC	Agg Surface	0
Millennia	QC	0
Material Serv. Test.	QC	0
Beniach	Oil and Chip	0

Notes:

Box Culvert: In procurement

Pipe Culvert: Ongoing

Agg Widening: On hold

Profile Adj./Add Rock: On hold

Pulverization: on hold

Stabilization: on hold

Agg Surface: on hold

Oil and Chip: on hold

Earthwork: on hold

Seeding: on hold

HMA: On hold until IDOT permits are in place.


Punchlist: On going

Long Duration Road Closures

LAST WORKING DAY	☑ 500E:1300N-1400N	11/6/2026	
TODAY	☑ CH16:1400N-1500N	11/7/2026	
	☑ CH16:1400N-1300N	11/7/2026	
	☑ 1400N:CH16-200E	11/7/2026	
	☑ 1400N:CH16-400E	11/7/2026	
NEXT WORKING DAY	☑ CH16:1400N-1500N	11/7/2026	
	☑ CH16:1400N-1300N	11/7/2026	
	☑ 1400N:CH16-200E	11/7/2026	
	☑ 1400N:CH16-400E	11/7/2026	
2-Day Lookahead	☑ CH16:1400N-1500N	11/7/2026	
	☑ CH16:1400N-1300N	11/7/2026	
	☑ 1400N:CH16-200E	11/7/2026	
	☑ 1400N:CH16-400E	11/7/2026	

Short Duration Road Closures

	LAST WORKING DAY	QTY Last Work Day	QTY Complete	Unit	Total QTY	% Complete	TODAY	NEXT WORKING DAY	2-Day Lookahead
Public Road Improvements — Box Culvert		0.0	1.0	EA	15.0	6.7%			
Pipe Culvert	S 167 Pipe Culv. S 167 field tile	1.0	109.0	EA	222.0	49.1%	S 210 S 211		C 210 C 211
Aggregate Widening	MC-30 1000N:CH13-800E 1000N:800E-900E 10000N:900E-1000E 800E:900N-1000N 900E:900N-1000N 1000E:900N-1000N 900N:900E-1000E	0.0	23.0	Mi	75.0	30.7%	MC-30 1000N:CH13-800E 1000N:800E-900E 10000N:900E-1000E 800E:900N-1000N 900E:900N-1000N 1000E:900N-1000N 900N:900E-1000E		
Prof. Adj.		0.0	12.0	EA					
Pulverization		0.0	23.5	Mi	75.0	31.3%			
Stabilization		0.0	23.5	Mi	75.0	31.3%			
Agg Surface		0.0	23.5	Mi	75.0	31.3%			
Oil and Chip		0.0	23.5	Mi	75.0	31.3%	S CH8:CH16-400E		
Earthwork		0.0	23.5	Mi	75.0	31.3%			
Seeding		0.0	23.5	Mi	75.0	31.3%			
Punchlist		0.0	23.5	Mi	75.0	31.3%			
HMA		0.0	7.0	EA	17.0	41.2%			C CH 8 Patches S CH 16 Patches 113.210/211
Site — Crane Pad			12.0	EA	109.0	11.0%			
Access Road		0.0	40.0	EA	109.0	36.7%	S 96.94.82		

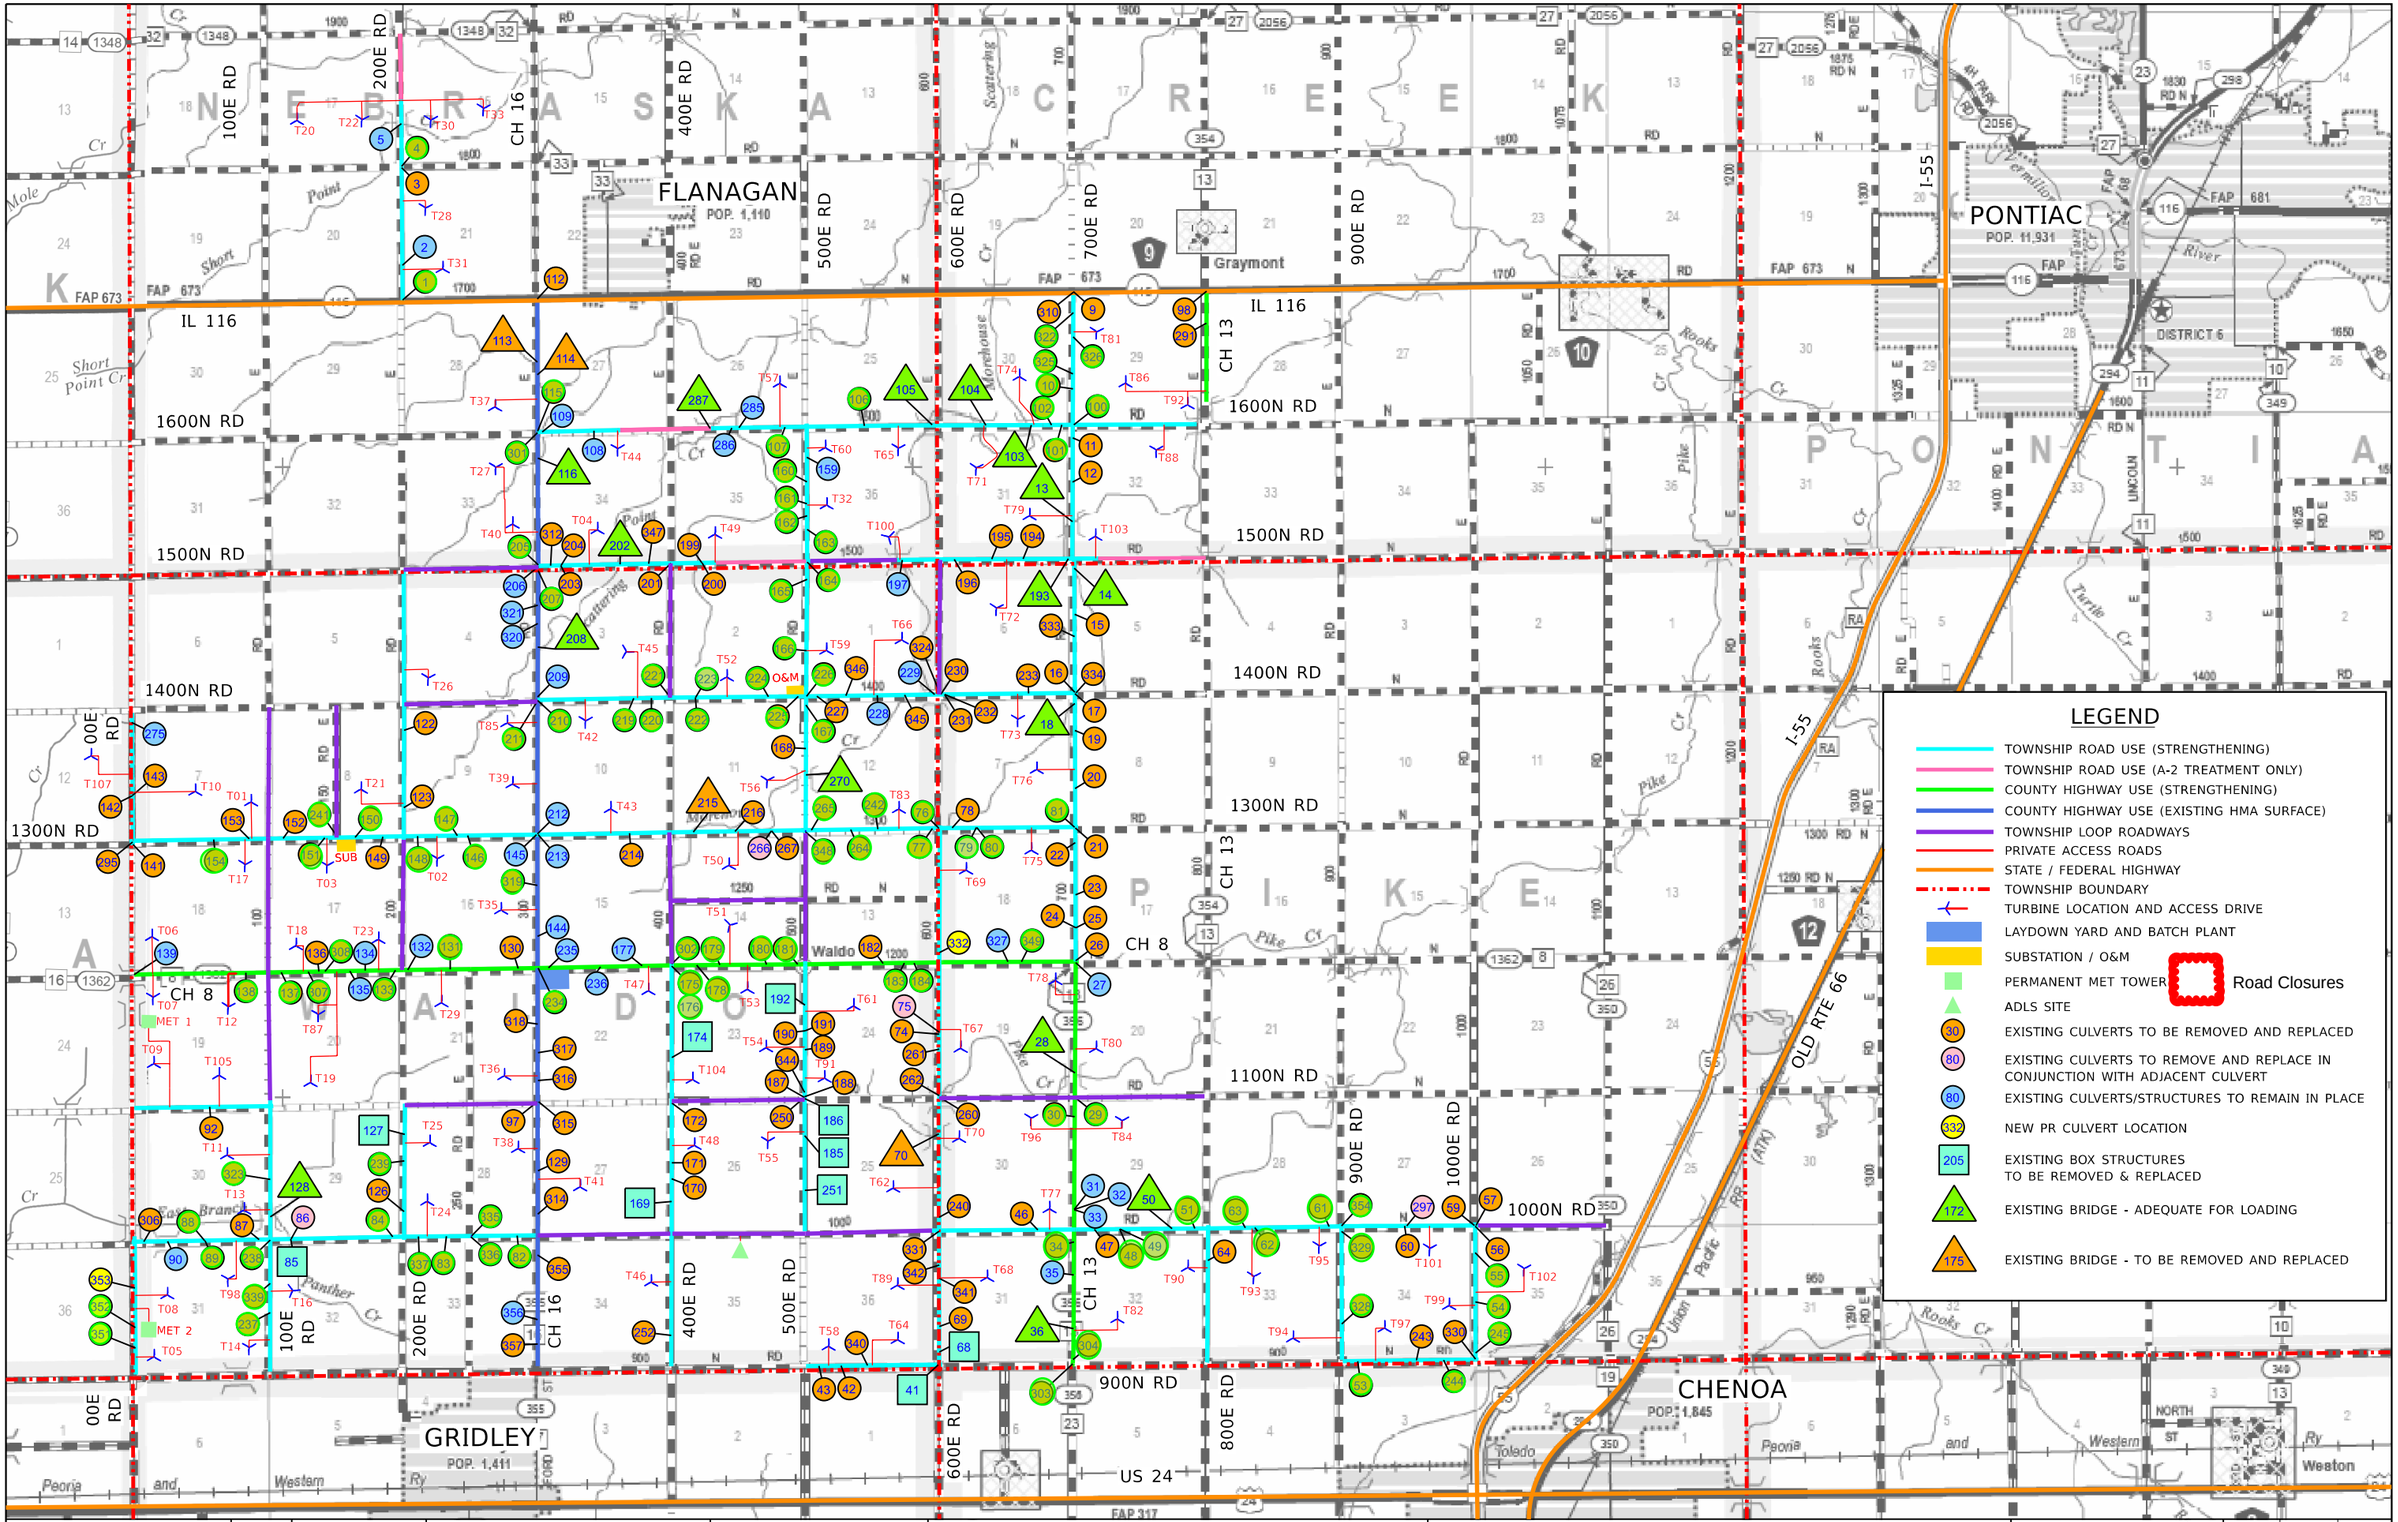

REV	DATE	DESCRIPTION
1	4/10/2026	REV 1
00	2/20/2026	IFC SUBMITTAL

DESIGNED - JDA
DRAWN - DRR/LNS
CHECKED - ML
DATE - 04/14/2026

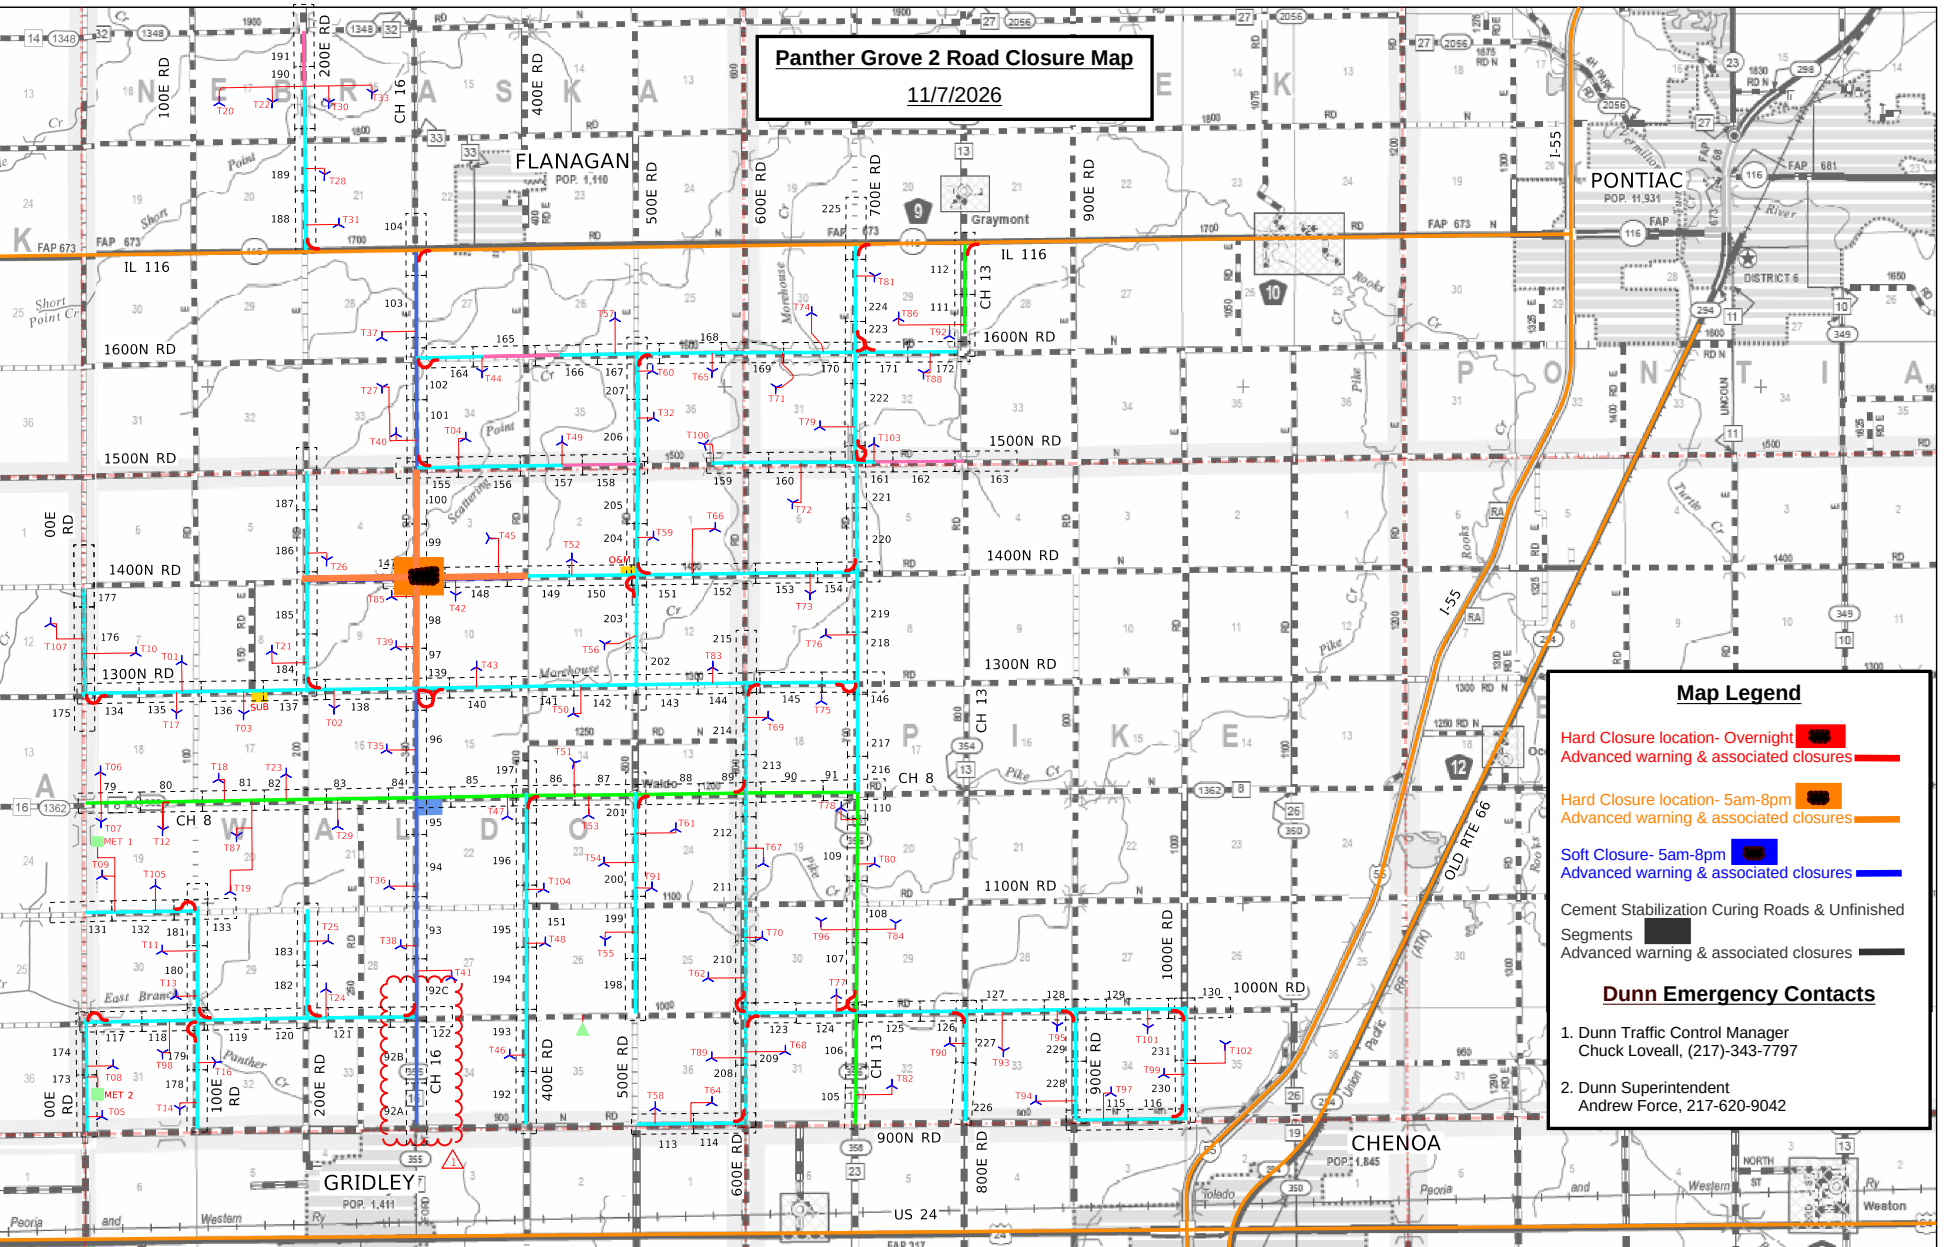
PANTHER GROVE 2 WIND PROJECT
LIVINGSTON COUNTY, ILLINOIS

EXHIBIT A – PROJECT LAYOUT MAP (REVISION 1)

SCALE: N.T.S. | SHEET 1 OF 1 SHEETS | STA. TO STA.

Farnsworth GROUP
100 WALNUT ST #200
PEORIA, ILLINOIS 61602
(309) 689-9888 / Info@f-w.com

TOTAL SHEETS	SHEET NO.	REVISION NO.


Panther Grove 2 Road Closure Map
11/7/2026
Map Legend
Hard Closure location- Overnight
Advanced warning & associated closures
Hard Closure location- 5am-8pm
Advanced warning & associated closures
Soft Closure- 5am-8pm
Advanced warning & associated closures
Cement Stabilization Curing Roads & Unfinished Segments
Advanced warning & associated closures
Dunn Emergency Contacts
1. Dunn Traffic Control Manager
Chuck Loveall, (217)-343-7797
2. Dunn Superintendent
Andrew Force, 217-620-9042
FLANAGAN
POP. 1,110
PONTIAC
POP. 11,931
GRIDLEY
POP. 1,411
CHENOA
POP. 1,845
IL 116
1600N RD
1500N RD
1400N RD
1300N RD
1100N RD
1000N RD
900N RD
100E RD
200E RD
400E RD
500E RD
600E RD
700E RD
800E RD
900E RD
CH 16
CH 13
CH 8
I-55
US 24
OLD RTE 66
Graymont
DISTRICT 6
